

Dehradun Branch Office:

39/3, 1st Floor, Subhash Road Dehradun, Uttarakhand (248001) Ph: 7017919244, 9958632707

Dated: 28/08/2022

File No.: VIS (2022-23) PL282-214-408

## PROJECT LENDERS INDPENDENT **ENGINEER (LIE) REPORT**

OF

### **GROUP HOUSING SOCIETY** "EDEN SENIOR LIVING & WELLNESS"

#### SITUATED AT

KHATA KAHTAUNI NO. 00025 (FASLI 1416 TO 1421), KHASRA NO. 39 & 40, MAUZA CHAK BHAGWANTPUR, PARGANA PACHWADOON, TEHSIL SADAR, DEHRADUN, UTTARAKHAND

### PROMOTER/S

### M/S. EDEN RETIREMENT LIVING PVT. LTD.

FORMERLY KNOWN AS ALPINE CONSTRUCTION PVT. LTD. THROUGH ITS Corporate Valuers DIRECTORS MR. SANJIV VOHRA, MR. DEEPAK GUPTA & MR. SAMIR GUPTA)

- Business/ Enterprise/ Equity Valuations
- REPORT PREPARED FOR
- Lender's Independent Engineers (LIL) AB NATIONAL BANK, CLPC BRANCH, DEHRADUN
- Techno Economic Viability Consultants (Tease of any givery/ issue or escalation you may please contact Incident Manager g. We will appreciate your feedback in order to improve our services.
- Agency for Specialized Account Monitoring (ASAS) provide your feedback on the report within 15 days of its submission after which rt will be considered to be correct.
- Project Techno-Financial Advisors
- Chartered Engineers
- Industry/Trade Rehabilitation Consultants
- NPA Management
- Panel Valuer & Techno Economic Consultants for PSU

CORPORATE OFFICE:

D-39, 2nd floor, Sector 2, Noida-201301 Ph - +91-0120-4110117, 4324647, +91 - 9958632707 E-mail - valuers@rkassociates.org | Website: www.rkassociates.org



	TABLE OF CONTENTS					
CD NO	DESCRIPTION	DACENO				
SR. NO.	DESCRIPTION	PAGE NO.				
PART A	Report Summary	3				
PART B	Introduction	5				
	1. The Project	5				
	2. About the Company	6				
	Location of the Project	6				
	4. Project Overview	8				
	5. Scope of the Report	10				
	6. Purpose of the Report					
	7. Methodology Adopted	10				
PART C	Plant Infrastructure Sections & Facility Details	11				
	1. Land Details	11				
	2. Project Infrastructure Details	12				
PART D	Project Consultants, Contractors & Suppliers	18				
	A. Confirmed Contractors	18				
PART E	Project Cost and Means of Finance	20				
	1. Total Project Cost	20				
	2. Current Status and Total Expenditure Incurred Till Date	22				
	3. Sources of Finance & Utilization of Funds	25				
PART F	Statutory & Regulatory Approvals, Clearances & NOC	26				
PART G	Project Schedule & Current Status	27				
	Project Schedule Chart	27				
PART H	Observations and Comments	29				
PARTI	Documents of the Project	30				
PART J	Photos	32				
PART K	Disclaimer	41				





### IMPORTANT NOTICE

COPYRIGHT FORMAT: This report is prepared on the copyright format of R.K Associates, to serve our clients with the best available information and analysis to facilitate them to take rational business decisions. Legally no one can copy or distribute this format without prior approval from R.K Associates. It is meant only for the advisory/ reference purpose for the organization/s as mentioned on the cover page of this report. Distribution or use of this format by any organization or individual other than R.K Associates will be seen as unlawful act and necessary legal action can be taken against the defaulters.

This report is intended for the sole use of the intended recipient/s and contain material that is STRICTLY CONFIDENTIAL AND PRIVATE.

**DEFECT LIABILITY PERIOD**: - In case of any query/ issue or escalation you may please contact Incident Manager: @ le@rkassociates.org. We try our level best to ensure correctness in the calculations done, rates adopted and various other data points & information mentioned in the report but still can't rule out typing, human errors or any other mistakes. In case you find any such mistake or inaccuracy in any data point of the report please help us by bringing all such points into our notice immediately or within 15 days of the report delivery in writing, to rectify these timely failing after which R.K Associates won't be held responsible for any such inaccuracy in any manner. We would highly appreciate your feedback in order to improve our services.





PART A	REPO	ORT SUMMARY
1. Name of the Project	:	Eden Senior Living & Wellness
2. Project Location	:	Khata Kahtauni No. 00025 (Fasli 1416 To 1421), Khasra No. 39 & 40, Mauza Chak Bhagwantpur, Pargana Pachwadoon, Tehsil Sadar, Dehradun, Uttarakhand.
3. Name of the Promoters	:	M/s. Eden Retirement Living Pvt. Ltd. (Formerly known as M/s. Alpine Construction Pvt. Ltd.)
4. Address and Phone Number	:	M/s. Eden Retirement Living Pvt. Ltd. D-29, Third Floor, Defence Colony, New Delhi
5. Prepared for Bank	:	Punjab National Bank, MCC Branch, Dehradun
6. Date of Survey	C.IN	22 <sup>nd</sup> August 2022
7. Date of Report		28th August 2022
8. Report type	:	Project LIE Report
9. Purpose of the Report	:	Review & evaluate Project Progress, capital expenditure & other execution details of the Project to facilitate creditors for taking business decision on the Project.
10. Scope of the Report	:	To assess, evaluate & comment on Reasonableness & sufficiency of:  (a) Project expenditures (b) Project physical progress (c) Project schedules (d) Statutory Approvals, Licenses & Registrations



11. Documents produced for perusal : PROJECT EXPENDITURE

**DETAILS:** 1.Invoices

2. Trial Balance Sheet

3.CA Certificate

**12. Annexure with the Report** : 1. Site Photographs

2. PO/ PI/ Invoices

3. Trial Balance Sheet

4. CA Certificate







**PART B** 

### INTRODUCTION

1. THE PROJECT: Eden Retirement Living Pvt. Ltd. has proposed to develop Group Housing Society named 'Eden Senior Living & Wellness' comprising of high rise apartments having total 2 towers. Company is developing both the towers together with each tower having Basement + Stilt Floor + 10 Floors on total 1.05 acres (4280 sq. mtr.) of land at Khata Kahtauni No. 00025 (Fasli 1416 To 1421), Khasra No. 39 & 40, Mauza Chak Bhagwantpur, Pargana Pachwadoon, Tehsil Sadar, Dehradun, Uttarakhand. The society is distributed with different types of units, viz. 2 BHK Type-I, 2 BHK Type-II, 1 BHK & Studio.





2. ABOUT THE DEVELOPER COMPANY: Eden Retirement Living Pvt. Ltd., a company incorporated under the name of M/s. Alpine Construction Pvt. Ltd. in the year 1987 and then changed the name to Eden Retirement Living Pvt. Ltd. w.e.f. 2<sup>nd</sup> March, 2017, with its Directors/ Shareholders Mr. Sanjiv Vohra, Mr. Deepak Gupta & Mr. Samir Gupta.

Eden Retirement Living Pvt. Ltd. is a Delhi based company. From public domain we couldn't gather much information about this company and its experience in real estate. However, from the information available to us, it appears that the company is mainly operated by seasoned professionals Shareholders Mr. Sanjiv Vohra, Mr. Deepak Gupta & Mr. Samir Gupta having wide Industry experience in different sectors. Out of all the Directors, Mr. Sanjiv Vohra appears to be having experience in real estate and have been engaged in the development of many real estate Projects in Dehradun like:

- 1. Doon Trafalgar with 132 apartments in Dhorankhas, Near IT Park, Dehradun
- 2. Princess Park 44 units along GMS Road, Opp. St. Jude School, Dehradun
- 3. Doon Trafalgar Extn. With 72 units in Dhorankhas, Near IT Park, Dehradun

As per the Project brochure and the company's websaite, Mr. Deepak Gupta is a qualified Chartered Accountant having over 35 years of global experience in management consulting, banking, executive search with working experience in the companies like Korn/Ferry International's India office, DHR International's India office & Citibank at senior positions. He began his career in management consulting with KPMG and then with PwC in Healthcare Consulting from 1983 to 1989 in USA.

Mr. Samir Gupta holds a postgraduate degree in Management and a Bachelor of Engineering degree in Electronics. He is having 27 years of business experience. As per his profile it appears that he is basically from Electronics & IT field is a Co-founder and Director of Samtech Infonet Ltd., Pyramid Cyber Security & Digital Forensic Pvt. Ltd., Olpoints InfoTech Pvt. Ltd. and Force Infosystems Pvt. Ltd.

**3. LOCATION:** Eden Senior Living and Wellness is located at Purkul Road, Mauza Bhagwantpur, Pargana Pachwadoon, Tehsil Sadar, Dehradun, Uttarakhand

**ROAD:** The said property lies within easy reach, linked by road, rail and air to Delhi and other major cities of the country. Below establishments are at the following distances from the project:

MAX Senior Living Apartments – Antara : 500 mtr.
 5 Star Hotel : 3 Km

3. MAX Super Speciality Hospital : 5 Km4. Rajpur Road Round-about : 7 Km

5. Ghanta Ghar : 12 Km

6. Mussoorie : 25 Km

7. Proposed Purkul Ropeway : 3 Km






8. Kasiga School

1 Km

RAIL: Eden Senior Living and Wellness is located closet to Dehradun Railway Station at a distance of approximately 15 km, connected through Main Mussoorie Road. Apart from this the property is also connected to Haridwar Railway Station through road which is approximately 65 km away from Eden Senior Living and Wellness.

**AIR:** The nearest International Airport is the Chandigarh International Airport, located at a distance of approximately 175 Km from Eden Senior Living and Wellness. The nearest Airport to the location is Jolly Grant Airport, Dehradun, which is approximately 35 km away from the location, which is currently being operated only for Domestic Flights.

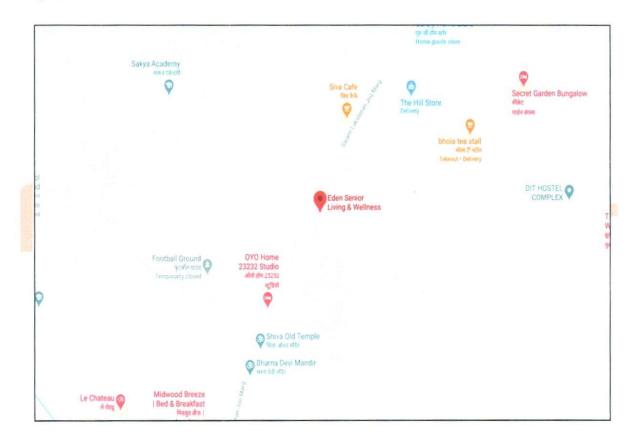



7





4. PROJECT OVERVIEW: Eden Retirement Living is developing a Group Housing Project named 'Eden Senior Living and Wellness' accommodating apartment space having approx. saleable area measuring 1,40,000 sq. ft. spread over a land area measuring 4280 sq. mtr. at Khata Kahtauni No. 00025 (Fasli 1416 To 1421), Khasra No. 39 & 40, Mauza Chak Bhagwantpur, Pargana Pachwadoon, Tehsil Sadar, Dehradun, Uttarakhand. However as on date the latest status of saleable area is that it has increased from 1,40,000 sq. ft. to 1,57,579 sq. ft.

As per the MDDA approved building Plan, this Project envisage to construct total 96 units in 2 towers in different categories viz., 2 BHK, 1 BHK and Studio apartment. As per the information provided by developer, the builder has upgraded the units of flats in which 11 apartments has been added. However, the built-up area of the project is same the saleable area has increased.

The specification of the project is revised and the developer is now providing the facilities like AC (Centralised in the lobby and Split/ Window in the units), Kitchen Appliances (Refrigerator, Over and other item), Washing Machines.

Total proposed project cost was estimated to be Rs.54.74 crore However as per latest CA certificate provided by the company it has now been revised to Rs.87.28 crore. The same is yet to be approved by the lender. As per official sanction letter, term Loan amounting to Rs.10 cr. is sanctioned by the bank with a debt-equity ratio of 241.



Company has obtained all the required preliminary, statutory approvals & clearances like NOC from Fire Safety Department, Excavation Permission, RERA Registration Certificate from Uttarakhand Real Estate Regulatory Authority, etc.

Eden Retirement Living Pvt. Ltd. has already acquired the land measuring 4280 sq. mtr. from Mr. Ashish Agarwal as per the Sale Deed dated: 15<sup>th</sup> January, 2015.

For the construction purpose, Eden Retirement Living Pvt. Ltd. has signed a Construction Agreement with M/s. Shraddha Nirman Pvt. Ltd. on 17<sup>th</sup> December, 2019, to construct proposed Group Housing Society having 2,27,000 sq. ft. of estimated construction area.

As per the site survey, we have observed the following observations:

#### Tower - 1

- 1. Slab Work completed of basement + stilt + 10th floor
- 2. Blockwork/brickwork completed from 1st to 9th floor.
- Electrical works: 1<sup>st</sup> to 5<sup>th</sup> Wall conducting done
   8 7<sup>th</sup> floor wall conduiting work in progress
   Electrical wiring 1<sup>st</sup> to 4<sup>th</sup> floor completed
- 4. False ceiling/POP Work: 1st to 4th floor completed
- 5. Stone work: 1st floor completed and 2nd WIP
- Flooring: 1st floor tiling works under progress.
- Water proofing: Bathroom (1st to 3rd floor completed), Balcony (1st and 2nd floor completed), Core pack (1st to 4th floor completed)
- 8. Plumbing work: up to 6th floor completed
- 9. Cast Iron railing: 1sty and 2nd floor completed
- 10. AC Work: 1st to 5th floor completed

### Tower – 2

- 11. Slab Work completed of basement + stilt + 9th floor
- 12. Blockwork/brickwork completed from 1st to 6th floor.
- 13. Electrical works: 1<sup>st</sup> floor completed Up to 4<sup>th</sup> floor wall conduiting work in progress
- 14. False ceiling/POP Work: 1st floor completed
- 15. Stone work: 1st floor completed and 2nd WIP
- 16. Flooring: No work started yet
- 17. Plumbing work: up to 4th floor completed
- 18. AC Work: up to 6th floor completed

Presently as per site survey, the project is delayed by a year. Clarification for delay in the project was sought from the borrower. Accordingly borrower has informed that they



were not able to efficiently progress the work to COVID-19 pandemic induced supply chain issues. However, considering the speed of work at the moment the project is estimated to achieve the Commercial operation date by 31st December 2022 which can also come down to October 2022 if same speed of work is maintained in the project.

#### 5. SCOPE OF THE REPORT:

- To review & scrutinize following below points:
- Review current status of the Project on site.
- Review capital expenditure incurred on site including preliminary & preparative expenses.
- Review position of various statutory, non-statutory clearances and regulatory clearances obtained by the company.
- Review the construction schedule of the project and advice on the scheduled COD
  of the project, whether same is achievable by the company or not.
- Advise Lender's on any other issue/ constraints in the project which may affect its progress.
- 6. PURPOSE OF THE REPORT: To provide fair detailed analysis report to the Bank based on the "in-scope points" mentioned above subject to the details/ data/information provided by the client for facilitating Bank to take appropriate decision on in regard to credit facility extended to the Project.

#### 7. METHADOLOGY ADOPTED:

- a. Site Survey
- b. Review & analysis of the Project initiation, planning, contract agreements, statutory regulatory approval documents and other data, information provided by officials of Eden Retirement Living Pvt. Ltd.
- c. Compilation & Preparation of the Report based on "in scope points".
- d. Report submission.





### PART C

### PLANT INFRASTRUCTURE SECTIONS & FACILITY DETAILS

### 1. LAND DETAILS:

Eden Retirement Living Pvt. Ltd. has already acquired the land measuring 4,280 sq. mtr. from Mr. Ashish Agarwal through Sale Deed no. 408, dated: 15<sup>th</sup> January, 2015.



{Table: 1}

PARTICULARS	DETAILS
Total Land Area	4280 m <sup>2</sup>
Location	Khata Kahtauni No. 00025 (Fasli 1416 To 1421), Khasra No. 39 & 40, Mauza Chak Bhagwantpur, Pargana Pachwadoon, Tehsil Sadar, Dehradun, Uttarakhand
Boundaries	North: Others Property South: Road East: Drain West: Purkul Road 40 ft. wide





#### 2. PROJECT INFRASTRUCTURE DETAILS:

Eden Retirement Living Pvt. Ltd. Is developing a Group Housing Society named 'Eden Senior Living & wellness' having approx. saleable area measuring 1,57,579 sq. ft. spread over a land area ad-measuring 4,280 sq. mtr. at Khata Kahtauni No. 00025 (Fasli 1416 To 1421), Khasra No. 39 & 40, Mauza Chak Bhagwantpur, Pargana Pachwadoon, Tehsil Sadar, Dehradun, Uttarakhand.

This project is comprising of 2 towers (Basement + Stilt + 10 Floors each) having total Area of Construction of Approx. 2,27,000 sq. ft.

For the purpose of the development of the Project, Eden Retirement Living has engaged a main Architect M/s. VYOM Architects & Interior Designer for the Design and Structural Services. Eden Retirement Living Pvt. Ltd. has engaged M/s. Shraddha Nirman Pvt. Ltd. for Building / Structural construction work as per below mentioned Terms & Conditions:

### {Table: 2}

Estimated Area of	2,27,000 sq. ft (Basement + Stilt + 10 Floors) excluding
Construction	elevation features & swimming pool which will be measured and priced separately.
Contract Value	Rs.690 per sq. ft + GST
Type of contract	With material, labour, all the labour, material, tools and Equipment except Steel which will be provided by the Project owner.
Mobilization Advance	- SACIATES
Performance Security	2% of payment of entire contract
Time of completion	18 months from the date of signing the agreement and structure in 15 months from the date of this agreement.
Mode of Payment	As per schedule mentioned in Table below.
Other conditions	Payment shall be made as per payment schedule attached herewith and only 75% Payment will be made on submission of the bill by the contractor against their running bill and balance of 23% of the balance payment within 10 days of submission after deducting statutory dues and adjustment of mobilization advance. 2% of payment of entire contract will be kept as performance guarantee & will be released after satisfactory completion of the contract and settlement of final bill.  Fixed price contract with no escalation clause.





### MODE OF PAYMENT (AREA-WISE)

pprox.	Area: 2,27,000 Sq. Ft.	
S. No.	Payment Level	Payment %
1	Basement Raft & up to basement roof	20.00
2	Slab Casting	
	Stilt Slab	4.00
	1st Floor Slab	4,00
	2nd Floor Slab	4.10
	3rd Floor Slab	4.10
	4th Floor Slab	4.20
	5th Floor Slab	4.20
	6th Floor Slab	4.30
	7th Floor Slab	4.30
	8th Floor Slab	4.40
1	9th Floor Slab	4.40
1	10th Floor Slab	4.50
		46.50
3	Brick Work	
	1st Floor	1.50
	2nd Floor	1.50
	3rd Floor	1.60
	4th Floor	1.60
	5th Floor	1.70
	6th Floor	1.70
	7th Floor	1.80
	8th Floor	1.80
	9th Floor	1.90
	10th Floor	1.90
		17.00
4	Internal Plaster ·	
	Stilt	1.00
	1st Floor	1.00
	2nd Floor	1.10
	3rd Floor	1.10
	4th Floor	1.20
	5th Floor	1.20
	6th Floor	1.30
	7th Floor	1.30
	8th Floor	1.40
	9th Floor	1.40
	10th Floor	1.40
		13.40
5	External Plaster	3.10
		en through

### {Table: 3}: Carpet Area Description

No. of		Carpet Area	Balco	Carpet Area With Balcony	Total Carpet Area with Balcony	Area Under Cupboard	Area Under Walls	Area under Cupboard s and walls	Area under Cupboar ds and walls	Covered Area Per Flat	Total Covered Area
18	2 BHK TYPE-A	1055	306	1361	24,498	20	127	147	2646	1508	27144
46	2 BHK TYPE-B	1035	283	1318	60,628	22	125	147	6762	1465	67390
8	2 BHK TYPE-C	1096	283	1379	11,032	22	125	147	1176	1526	12208
1	1 BHK TYPE-A	671	138	809	809	0	77	77	77	886	886
8	1 BHK TYPE-B	671	112	783	6,264	0	77	77	616	860	6880
8	1 BHK TYPE-C	662	112	774	6,192	0	77	77	616	851	6808
18	Studio	503	76	579	10,427	0	53	53	954	632	11381
107	Total:				119,850			0	Silvino	aluers .	132697



### {Table: 4}: Super Saleable Area

No. of Flats		Carpet Area	Balco ny	Cupboard	Area Under Walls	Loading of Common Areas	Total Super Area (Per Flat)	Total Super Area
18	2 BHK TYPE-A	1055	306	20	127	281	1789	32202
46	2 BHK TYPE-B	1035	283	22	125	278	1743	80178
8	2 BHK TYPE-C	1096	283	22	125	278	1804	14432
1	1 BHK TYPE-A	671	138	0	77	156	1042	1042
8	1 BHK TYPE-B	671	112	0	77	156	1016	8128
8	1 BHK TYPE-C	662	112	0	77	156	1007	8056
18	Studio	503	76	0	53	120	752	13541
107	Total:							157579

											EDEN SEN	OR LIVING REA STATES		IN .								
MIT	DESCRIPTION		CAR	PET AREA	And The	-	BUILTU	PAREA	The same	SUPER	AREA			TOTAL CARPET	TOTAL BUILTUP	NO. OF	TOTAL NO. OF	emas can	RPET AREA OF		Inner man	
VPE		APARTMENT (SQM)	CUPBOARD (SQM)	(SQM)	Al	CARPET NEA	APART CUPBO	+ TAIN		TAREA	TOTALSU		FLOOR	AREA PER FLOOR (SQM)	AREA PER FLOOR (SQM)	TLOORS	UNITS		FLOORS		TOTAL BUIL ALL F	10085
					SOM	SQFT	SQM	SQFT	SQM	sqit	SQM	SQFT						SQM	SQFT	SUPER AREA	SQM	SOFT
VI	NEU III	District Co.				CESTO S	200	EFTIREAT	INT HOM	E (157 FOR	TH FLOORS	1					-	1		PORTION		-
RA	2 BHK	96.16	2.02	26.28	124.46	1,339.69	136.29	1,457.03	25.63	-		1,742.89	6	746.76	W817.74	6 1	/ 49	5,974,08	64,325,00	1,230.15	6,541.92	10.44
198	28HK	/ 98.01	1.84	28.41	128.26	1,380,59		1,505.78	26.31		200112	1.788.93	2	256.52	279.78	- 8	16		72,089,45	420.88	The state of the s	70.43
OF.	-	/ 59.12		10.40	69.52	748.31	76.69	825.49	14.42	155.23	91.11	580.72	2	139.04	153.38	8	-	distance and the second	11.973.01	23075	-	18 20
50	STUCIO	45.79		7.09	53.88	579.96	58.81	633.03	11.06			752.07	. 2	107.76	117.62	. 8			9,279.43	175.94		16.17
			3		1000					1	DEAL AREA OF	FUNTSPERF	FOOK (FON)	1,250.08	1,868.52	TOTALANA	OF ALL UNITS ON	10,000.64	1,07,646.89	9.99	10,948.16	1,17,84
	-	50 E S	5000	THE REST	-		-114	RENTAL	HOME IS	TH TO 10TH	PROOPS		THE REAL PROPERTY.			251.10 %	THE CORE STORY					
SA	CHOUTZ	37.41	- 1	7.53	44.94	483.73	48.71	524.31					1	44.94	(48.71	3	2	29.28	957.47	-	97.42	104
150	STUDIO	/ 35.88	1.27	₩ 14.08	51.24	551.55	55.14	593.53			-	-	1	51.24	55.14	2	2	-	1103.09	-	110.28	15%
SC	AND REPORT OF TAXABLE PARTY.	32.83	1.93	8.72	43.48	468.02	47.00	505.91					1	43.48	47.00	2	1	16.56	936.04		94.00	-
SD	- incommon and	34.63	127	14.09	49.99	538.09	53.78	578.89			P		1	49.99	53.78	2	2	91 98	1,076.18		107.56	-
SE		33.53		7.58	41.06	441.97	44.56	479.64					1	41.06	44.56	- 2	2	82.12	383.94		89.12	
SF	STUDIO	31.40	-	10.34	41.74	449.29	45.49	488.69	-	150			1	41.74	45,40	- 1	1	41.74	449.29	N. The	45.40	
-											DEAL ANEA OF	LIMITS PERF	(MDS) RDD.	272.45	Description of the second		CEAULUNITS ON	503.16	5,416.01	Record of	543.78	5,85
_			100	7/75	-	-										91H & 23	WELDOWS   SOME					
	TOTAL CARPS	TAREA OF ALL	UNITS	10,503.80	MDS	-	PE V	Sunda-	State	1900	Parago I	TOTAL BUIL	TUP AREA	OF ALL PLOORS	18,916.70	SQM			Belleville State Co.	-		-
_	Sec. 1	of the later		1.13,062.90	SQFT	1									- 2,03.619.36					45		
_	TOTAL BLACT	PAREADFALL	UNITS	11,491.94	SOM		20 P. S			91998	FVSSIA	TOTAL BAI	CONTARE	OF ALL LINES	2,110.10	SQM						
4	-	-		1,23,699.24			-								22,713.12	SOFT						
4	CRULATION	AREA (15T TO	TH A	1,714.08				A 6414	Marie S	No. let		OTAL CUPE	DARD ARE	A OF ALL UNITS	135.34	SQM1						
4	ORD VARIOUS	462 4 1816 A		18,450.36											1,455.80	1300						
-	CROULATION	ANSA (2 IH)	1	201.23		_																
-	CIRCULATION	AREA CIOTHS		246.579																		
-	- Commentary	the law (g)	1	646.37		-																
				2.654.08	SOFT																	
	CIRCULATION	AREA ITERRACI	0 1	2,654.08 38.19	-																	
	CIRCULATION	AREA (TERRAC	1	The second second	SQM					1	Total	Common A	treas for Su	per Area	2.058.72							
		AREA (TERRACI		38.19	SQM SQFT						Total	Common A	leeas for Su	per Area	2.058.72							
	COMMON AR	EAS (common i	booner)	38.19 411.08 364.64 3,709.76	SQM SQFT SQM SQFT						Total	Common A	leeas for Su	per Area	2.058.72							
	COMMON AR		booner)	38.19 411.08 344.64 3,709.70 900.95	SQM SQFT SQM SQFT SQM						Total	Common A	leeas for Su	per Area	2,058.72							
	COMMON AR	EAS (common E	tsoner)	38.19 411.08 364.64 3,709.70 900.95 5,697.83	SQM SQFT SQM SQFT SQM SQFT						Total	Common A	teras for Su	ger Area	2.058.72							
	COMMON AR	EAS (common i	tsoner)	38.19 411.08 364.64 3,709.70 900.95 5,697.63 937.76	SQM SQFT SQM SQFT SQM SQFT SQM						Total	Common J	leeus for Su	iper Area	2.058.72							
	COMMON AS COMMON AS	EAS (common E EAS 9TH FLOOR EAS 20TH FLOO	tsoner)	38.19 411.09 844.64 8,709.76 900.95 5,697.83 937.76 10,094.05	SQM SQFT SQM SQFT SQM SQFT SQM SQFT						Total	Common A	leeus for Su	per Area	2.058.72							
	COMMON AS COMMON AS	EAS (common E	tsoner)	38.19 411.08 864.64 8,709.76 900.95 9,692.83 987.76 10,094.05 361.41	SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM						Total	Common A	treas for Su	per Area	2.058.72							
	COMMON AR COMMON AR COMMON AR SERVICE AREA	EAS (common 8 EAS 9TH FLOOR EAS 20TH FLOOR IS BASEMENT	tsorer)	38.19 411.08 364.64 8,709.76- 900.95 9,692.83 937.76 10,994.05 361.41 3,890.22	SQM SQFT SQFT SQM SQFT SQFT SQM SQM SQFT SQM SQFT SQM SQM SQFT SQM SQM SQM SQFT SQM SQM SQM SQFT SQM SQM SQM SQFT SQM						Total	Common A	treas for Su	iger Area	2.058.72							
	COMMON AR COMMON AR COMMON AR SERVICE AREA	EAS (common E EAS 9TH FLOOR EAS 20TH FLOO	tsorer)	38.19 411.08 864.64 8,709.76 900.95 9,692.83 987.76 10,094.05 361.41	SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM						Total	Common A	Areas for Su	iger Area	2.058.72							
	COMMON AR COMMON AR COMMON AR SERVICE AREA TOTAL BUILTR	EAS (common 8 EAS 9TH FLOOR EAS 20TH FLOOR IS BASEMENT	tsoner)	38.19 411.08 344.64 3,709.70 900.95 5,692.83 937.76 10,094.05 361.41 3,890.22 1,439.95	SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT						Total	Common A	ineas for Su	iper Arab	2.058.72							
	COMMON AR COMMON AR COMMON AR SERVICE AREA TOTAL BUILTR	EAS (common 8 EAS 9TH FLOOR EAS 20TH FLOOR IS BASEMENT UP AREA (STLT)	tsoner)	38.19 411.08 844.64 8,709.70 900.95 9,692.83 937.70 10,094.05 861.41 3,890.12 1,439.95	SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM						Total	Common A	ineas for Su	iper Arab	2.058.72							
	COMMON AR COMMON AR COMMON AR SERVICE AREA TOTAL BUILTE	EAS (common 8 EAS 9TH FLOOR EAS 20TH FLOOR IS BASEMENT UP AREA (STLT)	tsoner)	38.19 411.08 364.64 8,709.70 900.95 5,692.83 937.76 10,094.05 369.022 1,439.95 15,499.62 13,230.00	SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM						Total	Common A	izeas for Su	sper Arab	2.058.72							
	COMMON AR COMMON AR COMMON AR COMMON AR TOTAL BUILTE TOTAL BUILTE TOTAL BUILTE	EAS (COMPTION ) EAS 9TH FLOOR EAS 10TH FLOOR US BASEMENT UP AREA (STAT) UP AREA (STAT) UP AREA (15TTO)	Roomer)  A  R  A  DETM()	38.19 411.00 864.64 5,709.70 900.95 5,697.83 937.76 10,094.05 951.41 3,899.22 1,419.5 15,499.62 11,270.00	SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM						Total	Common A	ireas for Su	pper Area	2.058.72							
	COMMON AR COMMON AR COMMON AR COMMON AR TOTAL BUILTE TOTAL BUILTE TOTAL BUILTE	BAS (common II EAS 9TH FLOOR BAS 20TH FLOOR IS BASEMENT IP AREA (STUT) IP AREA (STUT)	Roomer)  A  R  A  DETM()	38.19 611.08 344.64 3.709.70 900.95 5,092.83 947.76 361.41 3,899.22 13,230.60 142,409.72 1,145.95 1,145.95 1,145.95 1,145.95 1,145.95 1,145.95 1,145.95	SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM SQFT SQM						Total	Common A	liveas for Su	ger Area	2.058.72							
	COMMON AR COMMON AR COMMON AR SERVICE AREA TOTAL BUILTE TOTAL BUILTE TOTAL BUILTE	BAS (common is BAS 9TH FLOOR BAS EXTEN FLOOR UP AREA (STET) UP AREA (STET) UP AREA (STET) UP AREA (STET)	Roomer)  A R A DETH()	38.19 611.08 344.64 5.709.70 90035 5.692.83 937.76 10.284.41 3.890.22 1,433.95 13.499.62 13.230.60 1.42,407.72 1.148.52 22,822.67 1,139.53 12,334.65	SQM SQFT SQM SQM SQM SQM SQM SQM SQM SQM SQM SQM						Total	Common A	liveas for Su	per Area	2.058.72							
	COMMON AR COMMON AR COMMON AR SERVICE AREA TOTAL BUILTE TOTAL BUILTE TOTAL BUILTE	EAS (COMPTION ) EAS 9TH FLOOR EAS 10TH FLOOR US BASEMENT UP AREA (STAT) UP AREA (STAT) UP AREA (15TTO)	Roomer)  A R A DETH()	38.19 611.08 611.08 364.64 3,703.70 900.95 5,609.83 987.76 10,094.06 951.41 3,890.22 13,439.62 11,439.62 11,439.62 11,439.62 11,439.62 11,145.62 11,145.62 12,344.63 12,344.63	SQM SQFT SQM SQM SQFT SQM SQM SQFT SQM SQM SQM SQFT SQM SQM SQM SQFT SQM SQM SQM SQM SQM SQM SQM SQM SQM SQM						Total	Common A	treas for Su	per Area	2.858.72							
	COMMON AR COMMON AR COMMON AR SERVICE AREA TOTAL BUILTE TOTAL BUILTE TOTAL BUILTE TOTAL BUILTE TOTAL BUILTE TOTAL BUILTE	BAS (common is BAS 9TH FLOOR BAS EXTEN FLOOR UP AREA (STET) UP AREA (STET) UP AREA (STET) UP AREA (STET)	ksorer)  A  R  A  DETH)	38.19 611.08 344.64 5.709.70 90035 5.692.83 937.76 10.284.41 3.890.22 1,433.95 13.499.62 13.230.60 1.42,407.72 1.148.52 22,822.67 1,139.53 12,334.65	SQM SQFT SQM SQM SQM SQM SQM SQM SQM SQM SQM SQM						Total	Common A	treas for Se	iger Aros	2.058.72							























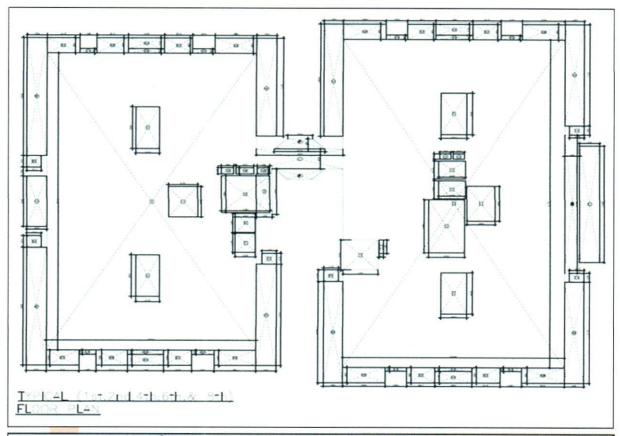

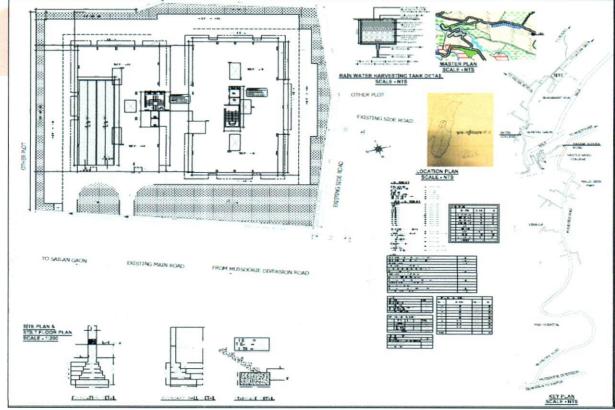





### PART D

### PROJECT CONSULTANTS, CONTRACTORS & SUPPLIERS

#### 1. CONFIRMED CONTRACTORS:

Following below consultants, contractors & suppliers have been engaged/ confirmed for different activities of the Project initiation and implementation activities:

{Table: 5}

S. No.	Name of the Company	Type of Contract	Scope of Work of Contract	Date of Agreement	Rates Agreed as per Contract
1	M/s. Shraddha Nirman Pvt. Ltd.	Per Square Feet	Civil & Structure Work for Group Housing Society	17/12/2019	Rs.690/- per sq. ft. + GST
2	M/s. Kaura & Co.	Per Square Feet	Water Proofing Treatment	23/10/2020	Refer to the work order attached below
3	M/s. Lakhinder Singh	Per Square Feet	Electrical Work	25/06/2020	Rs.20/- per sq. ft.
4	M/s. Air Wizz HVAC & Energy	Per Running	Installation, Testing & Commissioning of AC	22/00/2020	0-6
4	Solutions	Meter &	Equipments	22/09/2020	Refer to the work order attached below

S. No.	* Item Description	Rate (INR)	Area/Qty.
1	Waterproofing Treatment to sunken portion	48/Sq. Ft.	As per actual
2	Waterproofing Treatment to core cutting in sunken portion with dia of 6" to 8"	550/No.	As per actual
3	Treatment to tanks in two options by Injection Grouting/Food grade Epoxy coatings	80/Sq. Ft.	As per actual
4	Treatment to Crevices/Honeycombs & Joints	200/packer	As per actual
5	Epoxy Injection	850/packer	As per actual
6	Waterproofing Treatment to Balcony area by 2 Ply system app membrane (Plain/Mineral finish)	90/Sq. Ft.	As per actual
	Detailed work specifications are as per attached quotation		





File No.: VIS (2022-23) PL282-214-408

18



S. No.	Description	Qty.	Unit	Rate	Amount
1	Installation, testing & Commissioning of Variable refrigerant volume modular type	Q. J.		11010	711100111
	air- conditioning system suitable for Cooling				
	& Heating by inverter driven capacity control compressor complete with indoor and				
	outdoor units with individual controllers				
	with additional charging of Refrigerant gas.				
1.1	OUTDOOR UNITS				
a	6 HP	1	No.	12000	12000
1.2	Indoor units inclusive of Ref. piping , Drain piping etc as per drawings				
а	Cassette IDU	4	Nos.	2500	10000
2	Installation of 'Y' Joint Required for	3	Nos.	. 450	1350
	distribution of refrigerant in copper piping etc complete as per specifications				
3	Supply, Installation, Testing of				
	Interconnecting refrigerant pipe work with (19mm/13 mm thick) closed cell elastomeric				
	nitrile rubber tubular insulation between				
	each set of indoor & outdoor units as per				
	specifications, all piping inside the building				
	shall be properly supported with MS hanger.				
	Make Used: MANDEV / RAJCO/ MEXFLOW				
а	6.35 mm dia (13 mm thick)	14	Rmt.	330	4620
b	9.5 mm día (13 mm thick)	16	Rmt.	390	6240
С	12.7 mm dia (13 mm thick)	14	Rmt.	480	6720
d	15.9 mm dia (19 mm thick)	6	Rmt.	585	3510
e	19.1 mm dia (19 mm thick)	10	Rmt.	760	7600
f	22.2 mm dia (19 mm thick)		Rmt.	900	
4	Communication Cable interconnecting ODU & JDU Duly conduted				
a	1.5 sq.mm 2 core	38	Rmt.	150	5700
5	Power Cable for Indoor units with 3 pin top, with flexible condute	12	Rmt.	150	1800
6	Drain Piping				THE RESIDENCE OF THE PARTY OF T
	Rigid PVC piping complete with fittings,				
	supports as per specifications and duly				
4	insulated with 6 mm thick closed cell nitrile rubber insulation				
9	25 mm	40	Rmt.	150	6000
7 %	MS Stand for ODUs	1	No.	3500	3500
	TOTAL	Annual or security said			69040
	Discount 15%				10356
A STATE OF THE OWNER,	Total after Discoun				58684



#### PARTE

### PROJECT COST & MEANS OF FINANCE

1. TOTAL PROJECT COST: As per the Bank Loan Sanctioned Letter, the bank has sanctioned the Fresh Term Loan in favour of M/s. Eden Retirement Living Pvt. Ltd. of Rs.10 cr. with a Debt Equity Ratio of 2:1. Out of which 10.37 Crore has been disbursed till 31st July 2022 which is including GECL amount of Rs.1.89 Crore. Thus net term loan disbursed amounts to Rs.8.48 Crore.

The company has revised the project cost from 57.74 crore to 87.28 Crore. However revision in project cost is yet to be approved by the lender. Breakup of revised project cost is as below:

{Table: 6}

Sr. No.	Particulars	Amount (In Rs. Cr.)	Amount (In Rs. Cr.)
1.	Land & Land Development	8.34	8.34
2.	Construction	38.47	68.09
3.	Legal consultation and other charges	0.82	
4.	Cost of approvals	2.90	
5.	Marketing expense and others	1.19	11.54
6.	Pre-operative and Preliminary Expenses	0.86	
7.	Bank Interest	2.15	
	Total Project Cost	54.74	87.97

Source: Company

### **Observations & Comments:**

- 1. The basis of the above estimated cost is as per the estimates provided by the Eden Retirement Living and is already approved by the lender.
- 2. This is a Group Housing Society and hard cost includes complete interiors, finishing, fittings & fixtures of both the towers admeasuring total construction area ad-measuring 2,27,000 sq. ft. as per contract agreement and total constructed area from Basement to 10th Floor = 15,665.94 sq. mtr (1,68,631.31 sq. ft,.) as per MDDA approved map
- 3. Total covered area from Basement to 10<sup>th</sup> Floor = 1,56,65.94 sq. mtr. (1,68,631.31 sq.ft.) as per approved map and as per the total construction area including balconies measuring 2,27,000 sq.ft as per construction contract agreement works out to be ~Rs.1,700 sq.ft, appears to be reasonable as per the specification shown in the developers brochure for the Group Housing Society.
- 4. As per Details of Proposed revised project cost available with us, the envisaged expenses in the project amounts to Rs. 87.97 Crore. However as per means of finance is only available for Rs.87.29 Crore. As per our discussion with the borrower, they will be increasing the Means of finance amounting to Rs.0.68 Crore from advances from customers/unsecured loan from Directors. Lender to take note of it.

20 Salvers Valuers 20



{Table: 7}

	(Table.	. ,						
Name of the Project	Eden Senior Living & Wellness							
Constitution	Private Limited Company	Private Limited Company						
Name of the Company	Eden Retirement Living Private Limited							
Registered office address	D-29, TF Defence Colony, New Delhi - 11	10024						
Location of the Site	Purukul, Dehradun							
Name of the Promoters Directors	Deepak Gupta							
	Sanjiv Vohra							
	Samir Gupta							
Nature of Industry	Real Estate Developers							
Total Area of land	4280 Sq. Mtr.							
No. of Units and storeys	107 units and 10 Storeys							
Saleable Area	157579 Sq. Ft approx							
Constructed Area	226215 Sq. Ft approx							
	Particulars	Original Estimated Project Cost	Proposed Revision in Project Cost					
	Land and Land development	8.34	8.34					
	Construction Cost	38.47	68.09					
Total Cost of Project	Pre-operative xpenses	0.86						
Total Cost of Project	Legal consultation and other charges	0.82						
	Cost of approvals	2.9	11.54					
	Marketing expenses and other charges	1.2						
	Bank interest	2.15						
	Grand Total	54.74	87.97					
	Share Capital	2.50	10.00					
Moons of Einance	Unsecured Loan from Directors	13.25	14.46					
Means of Finance	Advances from Customers	28.99	40.93					
	Bank Loan	10.00	21.90					
	Total	54.74	87.29					

**Note:** As per Details of Proposed revised project cost avaliable with us, envisaged expenses in the project amounts to Rs. 87.97 Croe. However as per means of finance is only available for Rs. 87.29 Crore. As per our discussion with the borrower, they will be increasing the Means of finance amounting to Rs. 0.68 Crore from advances from cutomers/unsecured loan from Directors. Lender to take note of it.

Source: Company





2. CURRENT STATUS & TOTAL EXPENDITURE INCURRED TILL DATE: Details of the expenditure in the Table below is recorded for the expenditure incurred up to 31<sup>st</sup> July 2022 only as provided by the company:

{Table: 8}

	{Table: 0}								
SR. NO.	PARTICULARS	EXPENDITURE DESCRIPTION	INCURRED TILL 31st JULY 2022	CURRENT STATUS OF WORK AND REMARKS					
		(All figures	s in cr.)						
		Allocated Amount at the time of Sanction	8.34	As per CA certificate dated 27/08/2022 the company has					
1.	Land & Land Development	Expenses incurred till 30 <sup>th</sup> December 2022	8.34	incurred Rs. 8.34 Crores on land.					
		Expenses incurred up to 31st July 2022	8.34						
		Allocated Amount at the time of Sanction	38.47	As per our analysis based on physical progress observed during site visit and invoices/Ledger provided by the borrower, the company has incurred					
2.	2. Construction expenses	Expenses incurred till 30 <sup>th</sup> December 2022	approximately towards Cons However As per la	approximately Rs.25.50 Crore					
		Expenses incurred up to 31st July 2022	27.89	Crore towards construction works.					
		MAND		As per CA certificate the company					
3.	Preliminary and Preoperative	Allocated Amount at the time of Sanction	11.54	has incurred Rs.1.97 Crore towards Preliminary and pre operative expenses. However, in Previous report the same was 4.29 Crore. Thus, there is a reduction of approximately Rs. 2.32 Crore. Reason for the same as per CA certificate is that balance amount					
	expenses	Expenses incurred up to 31st July 2022		has been transferred to construction of building which contains various preliminary expenses which were previously included in preliminary expenditure since the structure is now almost completed. The same was also observed during site visit.					
4.		Revised Allocated Amount at the time of Sanction		Expenses incurred on the project has been considered based on physical progress observed during site visit, detail of invoices provide by					
4.	Total	Expenses incurred till 30 <sup>th</sup> December 2022 as per CA certificate	32.03	the borrower and information of other small and miscellaneous expenditure provided by the					



Expenses approved till 30th December 2022	35.03	borrower. However, for Soft cost we have relied on CA certificate dated 30 <sup>th</sup> December 2021 with
Expenses incurred up to 31st July 2022 as per CA certificate	38.20	and other information provided by the borrower.
Expenses approved up to 31st July 2022	40.20	

#### **OBSERVATIONS:**

i. As per CA certificate dated 27<sup>th</sup> august 2022 with UDIN. 22506366AQBQXO5808, the borrower has incurred Rs.38.20 Crore in the project which includes and as per CA certificate dated 30<sup>th</sup> December 2022 with UDIN. 21506366AAAACF3943 the company had incurred Rs. 32.03 Crore. Breakup of both the expenditures is as below:

Particulars	Cost of	Expenditure up	Expenditure up	Incremental
	Project	to 30 <sup>th</sup>	to 31st July	expenditure
		December 2022	2022	
HARD COST				
Land and land development	8.34	8.34	8.34	0.00
Construction	38.47	18.28	23.82	5.54
SOFT COST			-	
Legal Consultation and other	0.82	0.12	0.14	0.02
charges	0.02	0.12	A T	0.02
Cost of approvals	2.90	2.90	2.90	0.00
Marketing expenses and	1.20	0.54	0.56	0.02
others	1.20	0.01	0,00	0.02
Pre-operative and other expenses	0.86	0.86	0.86	0.00
Bank interest	2.15	0.99	1.58	0.59
Total (SC+HC)	54.74	32.03	38.20	6.17
Expenditure of Progress				
observed but invoices	-	3.00	1.50	-
pending				
Expenditure Approved		35.03	40.20	

**Note:** The structure of the Project is almost completed and finishing works are under progress in the project. The total built up area of the project is 2,27,000 sq. ft (Basement + Stilt + 10 Floors). According to Structure construction rate including brickworks applicable in Dehradun the company has incurred approximately Rs.25.50 Crore@Rs.1,100/- per Sq. ft. which is in line with the physical progress of structure observed during site visit.

In previous report we have considered the construction rate of approximately Rs.970/ft² which was only for structure construction. However, during latest site visit it was observed that the brickworks completion is also on the advance stages of completion. Thus, the construction rate has been considered as Rs.1,100/- per sq. ft. in this report.





24

- ii. As per CA certificate and other information provided by the Borrower, the company has incurred Rs.8.34 Crore towards land and land development which includes Rs.6.35 Crore towards purchase of land as per sale deed and Approx. Rs.2.00 Crore towards land development as per information provided by the borrower and physical progress observed during site visit.
- iii. As per our analysis based on actual physical progress observed during site visit, invoices/Ledger provided by the borrower, the company has incurred approximately Rs.25.50 Crore towards Construction works. However, we have only received invoices amounting to approx. Rs.24 crore. Clarification was sought from the borrower who informed that invoices are generated for complete work assigned at that point. Therefore, those invoices will be shared with us as soon as the contractor issues the same after 100% work completion and will be covered in subsequent report.
- iv. We have only analysed the Hard cost i.e., cost incurred towards land and Construction cost which is in line with the physical progress observed during site visit. However, for soft cost like Legal Consultation and Other charges, Cost of Approvals, Marketing expenses, bank interest and other Pre-operative and other expenses we have relied on CA certificate and other information provided by the borrower since we have not verified the books of accounts.





#### 3. SOURCES OF FINANCE & UTILIZATION OF FUNDS:

Means of Finance of Rs.38.20 Crore is as below:

{Table: 9}

PARTICULARS	PLANNED CURRENT STATE OF AMOUNT INVESTMENT UP TO 31.07.2022		BALANCE
Shared Capital	2.50	2.50	0.00 -2.52
Unsecured Loans from Directors	13.25	15.77	
Bank Term Loan	10.00	8.48	1.52
GECL	1.89	1.89	0.00
Advance from customers	28.99	9.56	19.43
	56.63	38.20	18.43

Source: As per the CA certificate dated 27th August 2022 with UDIN. 22506366AQBQXO5808.

#### Comments:

- 1. Means of finance have been considered for Rs.38.20 Crore only since the extra expenditure is based on visual observations on site.
- 2. The Term loan limit of the Borrower was Rs.10.00 Crore. However, the infusion as on date stands at Rs.10.37 Crore. Clarification was sought from the borrower regarding the excess term loan disbursal. Accordingly, the company has informed that GECL amounting to Rs.1.89 Crore was disbursed to the company during COVID period which has been considered in disbursal of loan only.



### PART F

### STATUTORY & REGULATORY APPROVALS, CLEARANCES & NOC

{Table: 10}

SR.	NAME OF LICENSE/ REGISTRATION	PURPOSE	DATE OF ISSUE	Current	
No.	ISSUING AUTHORITY		LICENCE NO.	Status	
	Building Plan Approval		25.04.2018		
1.	Mussoorie Dehradun Development Authority	Building Plan	MDDA/SL/LTR/2218/17-18	Obtained	
	Sanction of Power Load		02.04.2019		
2.	Uttarakhand Power Corporation Limited	Electricity	Connection No. 7069999001310	Obtained	
3.	Fire Safety Clearance	Firefiabting	01.01.2018	Obtained	
3.	Fire Department, Dehradun	Firefighting	3/CFO(GHP)/141/17		
4.	Excavation clearance	Excavation	15.01.2019	Obtained	
	DC, Dehradun	Clearance	03/khanij/2019		
	RERA Permission	Construction	25.06.2018		
5.	Real Estate Regulatory and Authority, Dehradun	Approval	UKREP06180000273	Obtained	
6.	Wat <mark>er C</mark> on <mark>nect</mark> ion	Water	CIAIL	Not	
0.	Uttarakhand Jal Pay Sansthan	v valei	Requirement to be fulfilled by Tube-Well	Obtained	

### **Observations & Comments:**

 Eden Retirement Living has obtained all the required Preliminary & Statutory Approvals from different Government Agencies but no formal document is available for Water Connection through concerned authority.





### PART G

### PROJECT SCHEDULE & CURRENT STATUS

1. PROJECT SCHEDULE CHART: Project schedule is summarized in the below chart mentioning the important activities and milestones as provided by the developer. This has been revised post COVID pandemic disruption from the original schedule. The revised COD of the project is 31.12.2022 and the same is also accepted by the lender vide Amendment in drawdown, COD letter issued by PNB dated 30.12.2021.

				REV	ISED	RE-RE	VISED		
S.No.	Activity	Start	Finish	Finishing & Interiors		Finishing	& Interiors	Remarks	
				Start	Finish	Start	Finish	Tower 1	Tower 2
1	Engineering setup and moblization of Contractor at site	01.03.2019			-			Completed	Completed
2	Land Excavation	01.04.2019		•			-	Land Excavation work completed at site.	Land Excavation work completed at site.
3	Foundation & Casting of Basement	07.06.2019			E	-		this electrical work and	Foundation and Basement construction work is completed at site. Along with this electrical work and plumbing work is completed.
4	Casting of Stilt roof	01.10.2019					01.0	Completed	Completed
5	Casting of First Floor Roof	01.12.2019	31.01.2020	01-03-2022	28.02.2020	01-03-2022	15-09-2022	Structure Works, Brick works, Electrical works,     False ceilin gworks, water proofing works, plumbing works completed.     Flooring works under progress.	Structure works, Brickworks, electrical works, False ceiling works and plumbing works completed.     Water proofing works under progress
6	Casting of Second Floor Roof	01.02.2020	30.06.2020	01.04.2020	31.05.2020	01-05-2022	15-10-2022	Structure Works, Brick works, Electrical works, False ceilin gworks, water proofing works, plumbing works completed.     Flooring works Not yet started	Structure works, Brickworks, and plumbing works completed.     Electrical works, False ceiling worjs and Water proofing works under progress     Flooring works not yet started
7	Casting of Third Floor Roof	15.07.2020	30.09.2020	01.06.2020	31.07.2020	01-06-2022	15-11-2022	Structure Works, Brick works, Electrical works, False ceilin gworks, water proofing works, plumbing works completed.     Flooring works Not yet started	1. Structure works, Brickworks, and plumbing works completed. 2. Water proofing works under progress 3. Electrical works, False ceiling works and Flooring works not yet started



	COD	30.09.2022			15.07	.2023		oject completion will be delayed rks are slow on progress.	
15	Casting of Tenth Floor Roof  Commencement of external development work	01.09.2022	30.09.2022	-	30.09.2021	01-06-2023		Completion of finshing works in Tower 1 are slow on progress.	Completion of Finsihing works in Tower 2 are slow progress
13	Casting of Nineth Floor Roof	01.10.2021	30.11.2021	01.06.2021	31.07.2021	01-04-2023		Structure works and Brickworks completed.     Electrical works, false ceiling works, Flooring works, Water proofing works and plumbing works not yet started.  Under Progress.	Structure works completed.     Brickworks, Electrical works, Flooring works, Waterproofing works and plumbing works not yet started.  Under progress
12	Casting of Eighth Floor Roof	01.07.2021	15.09.2021	01.04.2021	31.05.2021	01-03-2023	15-04-2023	Structure works and Brickworks completed.     Electrical works, false ceiling works, Flooring works, Water proofing works and plumbing works not yet started.	Structure works completed.     Brickworks, Electrical works, Flooring works, Waterproofing works and plumbing works not yet started.
11	Casting of Seventh Floor Roof	05.03.2021	20.04.2021	01.02.2021	31.03.2021	01-02-2023	15-03-2023	Structure works,     Brickworks, Plumbing works     completed.     Electrical works under     progress.     False ceiling works,     Flooring works, and water     proofing works not yet     started	Structure works completed     Brickworks under progress.     Electrical works, False ceiling works, Flooring works,     Waterproofing works and plumbing works not yet started.
10	Casting of Sixth Floor Roof	20.01.2021	28.02.2021	01.12.2020	31.01.2021	01-12-2022	15-02-2023	completed. 2. Electrical works under progress. 3. False ceiling works, Flooring works, and water proofing works not yet started	Structure works, Brickworks completed.     Plumbing works under progress.     Electrical works, False ceiling works , water proofing works and Flooring works not yet started
9	Casting of Fifth Floor Roof	05.12.2020	15.01.2021	01.10.2020	31.11.2020	01-10-2022	15-01-2023	Structure Works, Brick works, Electrical works and plumbing works completed.     False Ceiling works, Flooring works and water proofing works Not yet started	Structure works, Brickworks completed.     Plumbing works under progress.     Electrical works, False ceiling works, water proofing works and Flooring works not yet started.
8	Casting of Fourth Floor Roof	20.10.2020	30.11.2020	01.08.2020	30.09.2020	01-08-2022	15-12-2022	Structure Works, Brick works, Electrical works, False ceiling works and plumbing works completed.     Flooring works and water proofing works Not yet started	Structure works, Brickworks, and plumbing works completed.     Water proofing works under progress     Electrical works, False ceiling works and Flooring works not yet started

#### Observation:

- 1. During site visit it was observed that the project is slow on progress and the project is anticipated to delay by about 6 months. Clarification was sought from the company regarding slow progress in the project. Accordingly the company verbally informed that there is labour shortage in the project since the COVID time Other than that no specific reason is provided to us for this shortage. Also, the company has provided us the revised implementation schedule of finishing works in the project which is attached above. The same is yet to be approved by the bank.
- 2. As per RERA extension document provided by the borrower, the registration of this project is extended by 18 months from initial date of 01.05.2021 to 30.10.2022. However since the project is anticipated to delay by about 6 month the company shall apply for extension in project completion date to RERA.

File No.: VIS (2022-23) PL282-214-408

28



### PART H

### **OBSERVATIONS & COMMENTS**

- During site visit it was observed that the project is slow on progress and the project is anticipated to delay by about 6 months. The company shall apply for extension in COD with RERA. Bank to take note of this.
- 2. As per our analysis based on actual physical progress observed during site visit, invoices/Ledger provided by the borrower, the company has incurred approximately Rs.25.50 Crore towards Construction works. However, we have only received invoices amounting to approx. Rs.24 crore. Clarification was sought from the borrower who informed that invoices are generated for complete work assigned at that point. Therefore, those invoices will be shared with us as soon as the contractor issues the same after 100% work completion and will be covered in subsequent report.
- 3. The structure of the Project is almost completed and finishing works are under progress in the project. The total built up area of the project is 2,27,000 sq. ft (Basement + Stilt + 10 Floors). According to Structure construction rate including brickworks applicable in Dehradun the company has incurred approximately Rs.25.50 Crore@Rs.1,100/- per Sq. ft. which is in line with the physical progress of structure observed during site visit.

In previous report we have considered the construction rate of approximately Rs.970/ft<sup>2</sup> which was only for structure construction. However, during latest site visit it was observed that the brickworks completion is also on the advance stages of completion. Thus, the construction rate has been considered as Rs.1,100/- per sq. ft. in this report.

- 4. Based on our analysis the project will suffer cost overrun on account of increase in material prices, labour charges, Rental charges of machineries and other allied factors. The issue was discussed with the borrower who agreed that the project cost will increase owing to these factors. Also, initially they were providing semi furnished flats. However, as on date they have decided to provide flats in fully furnished conditions only, which will also contribute to increase in the project cost.
- 5. As per the observation during the site survey conducted by our surveyor, we are of the view that the overall progress of the project is about 50% which is reasonable in our view. However financial progress as per CA certificate is about 70% considering cost of Project as Rs.54.74 Crore. The difference is due to Cost overrun that is anticipated in the project and will contribute to increase in Project cost which will factor in for low physical progress percentage Vs. Financial progress percentage
- 6. The company has revised the total project cost, however the built up area of the project is same as earlier. The company has proposed to construct 11 studio apartments on 9<sup>th</sup> floor. Also the company has upgraded the material to be used for the interior work of the units. As per the discussion with the officials we came to know that the amount shown in the head of construction includes the electronic appliances and other fittings which the developer is providing to their customers in fully furnished units.



### PARTI

#### DISCLAIMER

- 1. No employee or member of R.K Associates has any direct/ indirect interest in the Project.
- 2. This report is prepared based on the copies of the documents/ information which interested organization or customer could provide to us out of the standard checklist of documents sought from them and further based on our assumptions and limiting conditions. All such information provided to us has been relied upon and we have assumed that it is true and correct. Verification or cross checking of the documents provided to us has not been done at our end from the originals. If at any time in future, it's found or came to our knowledge that misrepresentation of facts or incomplete or distorted information has been provided to us then this report shall automatically become null & void.
- 3. This report is a general analysis of the project and not an audit report. All the information gathered is based on the facts seen on the site during survey, verbal discussion & documentary evidence provided by the client and is believed that information given by the company is true best of their knowledge.
- 4. All observations mentioned in the report is only based on the visual observation and the documents/ data/ information provided by the client. No mechanical/ technical tests, measurements or any design review have been performed or carried out from our side during Project assessment.
- Bank/FII should ONLY take this report as an Advisory document from the Financial/ Chartered Engineering firm and it's specifically advised to the creditor to cross verify the original documents for the facts mentioned in the report which can be availed from the borrowing company directly.
- 6. In case of any default in loans or the credit facility extended to the borrowing company, R.K. Associates shall not be held responsible for whatsoever reason may be and any request for seeking any explanation from the employee/s of R.K. Associates will not be entertained at any instance or situation.
- 7. This Report is prepared by our competent technical team which includes Engineers and financial experts & analysts.
- 8. This is just an opinion report and doesn't hold any binding on anyone. It is requested from the concerned Financial Institution which is using this report for taking financial decision on the project that they should consider all the different associated relevant & related factors also before taking any business decision based on the content of this report.
- All Pages of the report including annexures are signed and stamped from our office. In case any paper in the report is without stamp & signature then this should not be considered a valid paper issued from this office.
- 10. Defect Liability Period is <u>30 DAYS</u>. We request the concerned authorized reader of this report to check the contents, data and calculations in the report within this period and intimate us in writing if any corrections are required or in case of any other concern with the contents or opinion mentioned in the report. Corrections only related to typographical, calculation, spelling mistakes will be entertained within the defect liability period. No request for any illegitimate value revision, date change or any other facts & figures changes will be entertained other than the one mentioned above.
- 11. R.K Associates encourages its customers to give feedback or inform concerns over its services through proper channel at <a href="mailto:le@rkassociates.org">le@rkassociates.org</a> in writing within 30 days of report



- delivery. After this period no concern/ complaint/ proceedings in connection with the Valuation Services can be entertained due to possible change in situation and condition of the property.
- 12. Our Data retention policy is of <u>ONE YEAR</u>. After this period we remove all the concerned records related to the assignment from our repository. No clarification or query can be answered after this period due to unavailability of the data.
- 13. This Valuation report is governed by our (1) Internal Policies, Processes & Standard Operating Procedures, (2) R.K Associates Quality Policy, (3) Valuation & Survey Best Practices Guidelines formulated by management of R.K Associates, (4) Information input given to us by the customer and (4) Information/ Data/ Facts given to us by our field/ office technical team. Management of R.K Associates never gives acceptance to any unethical or unprofessional practice which may affect fair, correct & impartial assessment and which is against any prevailing law. In case of any indication of any negligence, default, incorrect, misleading, misrepresentation or distortion of facts in the report then it is the responsibility of the user of this report to immediately or atleast within the defect liability period bring all such act into notice of R.K Associates management so that corrective measures can be taken instantly.
- 14. R.K Associates never releases any report doing alterations or modifications from pen. In case any information/ figure of this report is found altered with pen then this report will automatically become null & void.

SURVEYED BY

Mr. Deepak Joshi

Date: 22<sup>nd</sup> August 2022

PREPARED BY

Er. Tejas Bharadwaj

Date: 28th August 2022



File No.: VIS (2022-23) PL282-214-408

31



DEFECT LIABILITY PERIOD - In case of any query/ issue or escalation you may please contact Incident Manager by writing at valuers@rkassociates.org. We ensure 100% accuracy in the Calculations done, Rates adopted and various other data points & information mentioned in the report but still can't rule out typing, human errors or any other mistakes. In case you find any mistake, variation, discrepancy or inaccuracy in any data point of the report, please help us by bringing all such points into our notice in writing at <a href="mailto:valuers@rkassociates.org">valuers@rkassociates.org</a>within 30 days of the report delivery, to get these rectified timely, failing which R.K Associates Valuers Techno Engineering Consultants (P) Ltd. won't be held responsible for any inaccuracy in any manner. Also if we will not hear back anything from you within 30 days, we will assume that report is correct in all respect and no further claim of any sort will be entertained thereafter. We would welcome and appreciate your feedback & suggestions in order to improve our services.

COPYRIGHT FORMAT - This report is prepared on the copyright format of R.K Associates Valuers Techno Engineering Consultants (P) Ltd. to serve our clients in the best possible way. Legally no one can copy or distribute this format without prior approval from R.K Associates. It is meant only for the organization as mentioned on the cover page of this report. Distribution or use of this format other than R.K Associates will be seen as unlawful act and necessary legal action can be taken against the defaulter







#### PART J

### DOCUMENTS OF THE PROJECT



### Amit P C Gupta & Associates (Chartered Accountants)

#### TO WHOM SOEVER IT MAY CONCERN

This is to certify that "M/S EDEN RETIREMENT LIVING PRIVATE LIMITED", a Company having Registered office At D-29, IIIRD FLOOR, DEFENCE COLONY, DELHI-110024 has incurred the following expenditure on the project as per the data maintained in their Financial Software.

#### Cost of Project and Means of Finance

(Rs. In lac)

Particulars	Original	Present Position as on a latest date 31.07.2022	Revised Cost of project	Escalation in cost of project	
	Α	В	С	D=C-A	
COST OF PROJECT					
Cost of land	834.36	834.36	834.36	0.00	
Construction of Building	4458.50	2789.25	7334.00	2875.50	
Pre-operative and preliminary expenses & other misc.	181.18	196.57	559.65	378.47	
Total	5474.04	3820.18	8728.01	3253.97	
Capital	250.00	250.00	250.00	0.00	
Unsecured loans	1325.00	1577.21	1446.00	121.00	
Advance from customers	2899.04	955.62	5032.01	2132.97	
Term Loan & GECL	1000.00	1037.35	2000.00	1000.00	
Total	5474.04	3820.18	8728.01	3253.97	

Note: We have transferred Rs. (429.36-196.57=232.79) to construction of building being various expenses which are now transferred on completion of civil construction which is almost done.

Thanking you

Yours truly

CA AMIT GUPTA

(Proprietor)

Shop No.6, First Floor, Kumar Shopping Complex,

Bhangel, Noida-201301

Membership No.506366

FRN: 022524N

UDIN NO:- 22506366AQBQXO5808

Dated 27/08/2022 Place: Noida

> Shop No. 6, Kumar Shopping Complex, Near Police Chowki Bhangel, Noida-201304 E-mail: amitpcguptaandassociates@gmail.com

Visit us : Http://amitca.in Mobile: 9818571188







The institute of Chartered Accountants of India

Unique Document Identification Number(UDIN) for Practicing Chartered Accountants

🎎 Generate UDIN 🎎 Bulk UDIN for Certificates 🔯 List UDIN Q. Search 🔑 Change Password 🔞 Revoke/Cancel UDIN

@ FAQs & Logout

You have logged in as: CA AMIT GUPTA (506366)

Last login: 27/08/2022 | 15:17:40

#### **Generate UDIN**

Membership Registration Number or MRN

506366

Member Name

AMIT GUPTA

E-mail ID.

amitpcguptaandassociates@gmail.com

Your Firm Registration No. or FRN

022524N - AMIT P.C. GUPTA & ASSOCIATES

Document Type

Certificates GST and Tax Audit Audit & Assurance

Type of Certificate

Others

\* Date of signing of Document (dd/min/y yyy):

7-08-2022

#### (eywords/Values: (Do not disclose client details)

S.no.	Particulars	Figures
1.	Cost of land	834.36
2.	Construction of Building	2789.25
3.	Pre-operative and preliminary expenses & other misc.	196 57
4	Total	3620 18
5	Term Loan & GECL	1037.35
. 6.	Total	1820.18
7.	Capital	250.00
ê.	Unsecured loans	1577.24
9.	Advance from customers	955.62
* Docum	ment Deschot-on	The Company has incurred the following expenditure on the pr

Remarks (Internal Reference Protes) Remarks - Hiese will not be shown to Authority (

#### DISCLAIMER

residitely as a run been the chapter by it as a second conservation of the decomposition of t




File No.: VIS (2022-23) PL282-214-408

34




**PART K** 

### SITE PHOTOGRAPHS

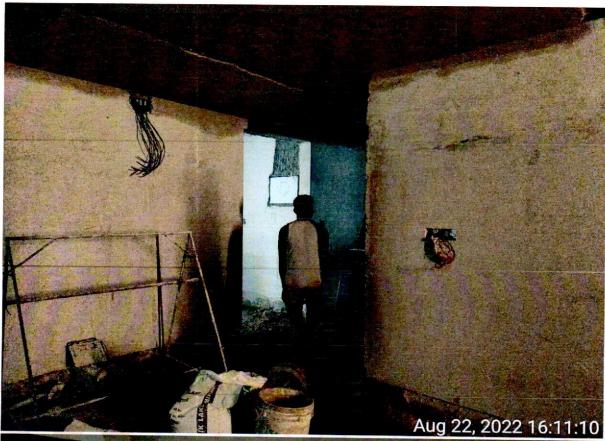






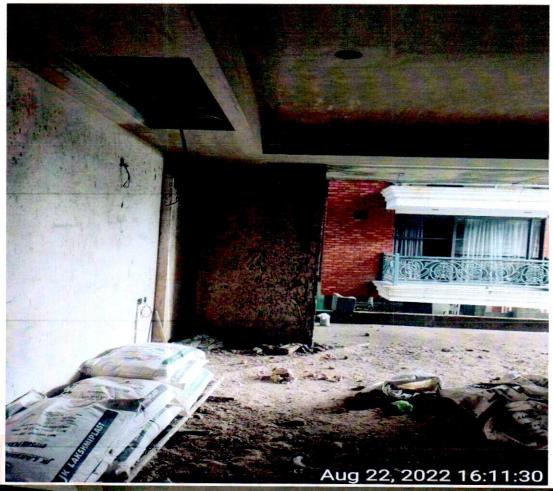







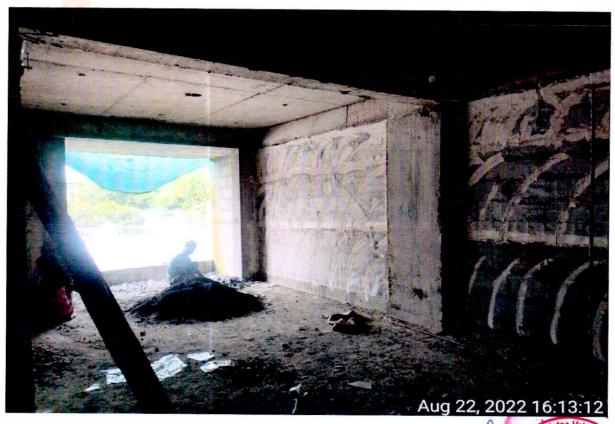

A SUBMINIST STATE OF STATE OF

File No.: VIS (2022-23) PL282-214-408

37









