

Dated: 17.09.2021

File No.: VIS (2021-22)-PL451-403-516

CAPITAL EXPENDITURE REPORT

OF

HOTEL GRAND ARC

SITUATED AT

VILLAGE - NAWADA INDERPUR, SHAHJAHANPUR, UTTAR PRADESH

PROMOTER

M/S. SHRI BALA JI HOSPITALITY

Corporate Valuers

- REPORT PREPARED FOR
- Business/ Enterprise/ Equity Value TERECTORATE OF TOURISM, UTTAR PRADESH
- Lender's Independent Engineers (LIE)
- Techno Economic Violatity Consultants (TEV) any query/ issue or escalation you may please contact Incident Manager
- Agency for Specialized Account Social Principles (ACC) We will appreciate your feedback in order to improve our services.
- Project Techno Valdad de 100/3003 de sour feedback on the report within 15 days of its submission after which report will be considered to be correct
- Chartered Engineers
- Industry/Trade Rehabilitation Consultants
- NPA Monogement
- Panel Valuer & Techno Economic Consultants for PSU Banks

CORPORATE OFFICE:

D-39, 2nd floor, Sector 2, Noida-201301 Ph - +91-0120-4110117, 4324647, +91 - 9958632707 E-mail - valuers@rkassociates.org | Website: www.rkassociates.org

HOTEL GRAND ARC, SHAHJAHANPUR



IMPORTANT NOTICE

COPYRIGHT FORMAT: This report is prepared on the copyright format of R.K Associates to serve our clients with the best possible information and analysis to facilitate them to take rational business decisions. Legally no one can copy or distribute this format without prior approval from R.K Associates. It is meant only for the advisory/ reference purpose for the organization/s as mentioned on the cover page of this report. Distribution or use of this format by any organization or individual other than R.K Associates will be seen as an unlawful act and necessary legal action can be taken against the defaulters.

This report is intended for the sole use of the intended recipient/s and contains material that is STRICTLY CONFIDENTIAL AND PRIVATE.

DEFECT LIABILITY PERIOD: - In case of any query/ issue or escalation you may please contact Incident Manager at le@rkassociates.org. We try to ensure maximum accuracy in the calculations done, rates adopted, assumptions taken and various other data points & information mentioned in the report but even still can't rule out typing, human errors or any other bonafide mistakes. In case you find any such mistake or inaccuracy in any data point of the report, please help us by bringing all such points into our notice immediately or within 15 days of the report delivery in writing, to rectify these timely failing after which R.K Associates won't be held responsible for any such inaccuracy in any manner. We would highly appreciate your feedback in order to improve our services.

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 1 of 51



HOTEL GRAND ARC, SHAHJAHANPUR

SECTIONS	PARTICULARS	PAGE NO.
Part A	REPORT SUMMARY	03
Part B	INTRODUCTION	05
	Name of the Project	05
	2. Project Overview	05
	Project Location	11
	Scope of the Report	13
	5. Purpose of the Report	13
	6. Survey Details	13
	7. Methodology Adopted	14
Part C	PLANT INFRASTRUCTURE SECTIONS & FACILITY DETAILS	15
	Building & Structural Details	15
	2. Plant & Equipment Details	16
	3. Main Machinery & Summary of Bills	17
Part D	PROJECT COST	18
	Project Capital Expenditure Evaluation	18-32
Part E	PHOTOGRAPHS FROM THE SURVEY	33-41
Part F	QUOTATIONS	43-48
Part G	DISCLAIMER	49-51







	PART A	REPORT SUMMARY				
1.	Name of the Project	:	Hotel Grand Arc			
2.	Project Location	:	Village - Nawada Inderpur, Shahjahanpur, U.P			
3.	Name of the Promoter	:	M/s. Shri Balaji Hospitality			
4.	Prepared for Organization	:	Directorate of Tourism, Uttar Pradesh			
5.	Chartered Engineer Firm	1	M/s. R. K. Associates Valuers & Techno Engineering Consultants (P) Ltd.			
6.	Date of Survey	:	10.09.2021			
7.	Date of Report	:	17.09.2021.			
8.	Report Type	:	Capital Expenditure Report			
9.	Purpose of the Report	:	To verify and examine capital expenditure status of the Project in regard to the special facilities & incentives given to Hotel projects as per Uttar Pradesh Tourism Policy-2018.			
10.	Scope of the Report	;	To verify and examine capital expenditure status of the Project.			
11.	Documents produced for Perusal	:	a) Detailed Project Report b) Break-up of the cost heads c) List of Invoices with Description of the Items			
			d) Copy of Invoices of Items e) Copy of CA Certificate f) Copies of various NOCs & Approvals g) Information received on e-mail			

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 3 of 51





12. Annexure with the Report

a) Photographs

:

 b) Other annexures (e.g. Invoices, NOCs & Approvals, CA Certificate etc.)



FILE NO.: VIS (2021-22)-PL-451-403-516

Page 4 of 51

HOTEL GRAND ARC, SHAHJAHANPUR



PART B

INTRODUCTION

 NAME OF THE PROJECT: Hotel Grand Arc situated at Village Nawada-Inderpur, Near Mumukshu Ashram, Shahjahanpur, Uttar Pradesh developed by M/s. Shri Balaji Hospitality.



2. PROJECT OVERVIEW: This star rated hotel is established by M/s. Shri Balaji hospitality located in District Shahjahanpur, Uttar Pradesh near Mumkshu Ashram, Sahjahanpur. As per Project Report, M/s. Shri Balaji Hospitality is incorporated on 27.12.2017 is a partnership firm having registered office at Gandhiganj, Sahjahanpur.

This Hotel project is built on total Land area about 6949.65 sq. mtr. (as per map) and 14678 sq. mtr. actual as per site or google measurement. Hotel comprises of Basement + Ground + 5 floor RCC roofed structure with total built up area of 6287.59 sq.mtr. The construction of the hotel began in year 2018 and achieved COD on 07.11.2020. This is a 61 key hotel, comprising of 49 Executive Rooms, 07 Executive Room (twin bed rooms), 4 suite rooms including 1 which is

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 5 of 51





designed for differently abled people and 1 apartment, 2 multi cuisine restaurants, 1 banquet hall, 1 conference room, swimming pool and other amenities and utility rooms as per the floor wise description given below:

Table: 1

S. No	Floor	Type of Room	Total Rooms
4	Second Floor	Executive Rooms	12
,	Second Floor	Suite Rooms	02
2	Third Floor	Executive Rooms	22
2	Third Floor	Suite Rooms	02
	Fourth Floor	Executive Rooms	15
3		Twin Bed Rooms	07
		Apartment	01
	Tota	ıl	61

To promote Tourism & Hospitality Industry in the state, UP State Government has offered capital subsidy and financial assistance as per Uttar Pradesh Tourism Policy-2018 on the capital investment on hotels, resorts, heritage hotels, motels, theme parks etc. in the state of U.P. As the subject project has been successfully completed and is commercially operational since 07.11.2020, therefore the promoter of the Project has applied for the subsidy under Uttar Pradesh Tourism Policy-2018.

For the purpose of verifying capital investment done by the M/s Shri Balaji Hospitality in the construction of Hotel Grand Arc, Department of Tourism, UP Government has appointed us as a consultant to provide an opinion on the capital investment incurred by the promoter under the eligible heads.





HOTEL GRAND ARC, SHAHJAHANPUR

As per the Uttar Pradesh Tourism Policy 2018, below listed capital investment subsidy to eligible tourism units:

Table: 2

- Eligible Capital Investment: The term Eligible Capital Investment shall include A. expenditure components as per the guidelines of Ministry of Tourism, Government of India, for the relevant Tourism Unit. However, the following heads of investments with respect of the unit shall not be eligible for incentives:
 - Working Capital;
 - íi. Pre-operative expenses and preliminary expenses;
 - 111. Second-hand plant and machinery purchased or shifted from within or outside country:
 - Interest capitalized; iv.
 - Consumable stores, inventories for maintenance or repairs; V.
 - Investment on land required for setting up the Unit, inclusive of the cost of the vi.
 - vii. Vehicles, furniture and fixtures, cutlery, crockery and utensils; and
 - Any construction which is in the nature of real estate transactions, e.g., shops, viii. flats, offices, etc. meant for sale/lease/rent.

Promoter informed to the Govt. of U.P that they have made capital investment of amount Rs.23.7757 Cr in the Project in the various heads like Buildings, Plant & Machinery & other miscellaneous items etc. Out of which the project includes eligible investment of Rs.18.0818 Cr for availing capital subsidy and Rs.5.6939 Cr as in-eligible expenditure on which capital subsidy is not allowed which is described in table below as per copy of Chartered Accountant certificate dated 18/06/2021:

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 7 of 51





Table: 3

S. No	Details		Amount	Bldg	P&M
3. 140	Details		(in lakh)	(in lakh)	(in lakh
	BOUNDARY WALL/S				
1.2	2815 Sq. Mtrs. @ 1500 per sq.		0.000000000		
	mtr.		42.23	42.23	
	INTERNAL ROADS, DRAINAGE &				
	ENTRANCE GATE/S				
	Internal Road (2243 sq. mtr. @				
1.3	1600 per sq. mtr.)	35.89		35.89	
	Drainage (401 run. Mtr. @ 600			1000000000	
	per run. Mtr.)	2.41		2.41	
	Entrance Gate	1.10			1.10
	Ditek 7EH Barrier	0.86	40.26		0.86
	SWIMMING POOL		-		
1.4	Structure 165 sq. mtr. @ 7000				
	per sq. mtr.	11.55		11.55	
	Swimming Pool machinery	6.19	17.74		6.19
	STORE/S		-		
1.5	391.42 sq. mtr. @ 13000 per sq. mtr.		50.90	50.90	
	KITCHEN/S				
1.6	328.72 sq. mtr. @ 13000 per sq. mtr.	42.73		42.73	
	Kitchen Items & Equipments	53.40	96.13		53.40
	WATER SUPPLY SYSTEM (Pipeline, tanks, pump house		A		
	water treatment plant etc.)				
	Tank 192 cu. Mtr. @ 15000 per	2222			
1.7	cu. Mtr.	28.80	-	28.80	
	Pipes	1.52	-	1.52	
	Pump House	1.04	-		1.04
	Water treatment plant	1.41	24.46		1.41
	Water Softening Plant	1.69	34.46		1.69
1.9	SEWERAGE TREATMENT PLANT				
1.9	& WASTE MGT. SYSTEM ETP Water Treatment Plant		2.84		2.84
	CENTRALIZED		2.04		2.04
1.10	AIRCONDITIONING SYSTEM				
1.10	Air Conditioners		108.30		108.30
	POWER SUPPLY SYSTEM		100.30		100.30
	INCLUDING SUB STATION,				
	TRANSFORMER, DISTRIBUTION		1		
	SYSTEM & ELECTRIFICATION				
1.11	Transformer	1.41	1		1.41
	Elect. Installation	103.72			103.72
	Voltage Stabilizer	0.54		Faction 8	0.54
	Inverter & Battery	3.84		18/	3.84
	Vidyut Suraksha Vibhag	0.48	109.99	[3]	0.48

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 8 of 51



HOTEL GRAND ARC, SHAHJAHANPUR

1.12	D.G. POWER BACK UP (FOR SELF USE)				
	Genset		42.09		42.09
	HOT & COLD WATER SUPPLY		72.03		42.0.
	SYSTEM, GAS/ STEAM SUPPLY				
1.14	LINE		9.59		9.59
	h Tith La College		9.59	_	9.59
	Heat Pump		_		
	ESTABLISHMENT OF SOUND,				1
	LIGHT, PUBLIC ADDRESS,				1
1.15	INTERNET SYSTEM AND		1		1
	NETWORK OF FIXED NATURE				
	Speaker, Woofer & Amplifiers	23.97			23.9
	Projecter Screen	0.64	24.61		0.64
	INSTALLATION OF FIRE				
1.16	DETECTION AND FIRE FIGHTING				1
4.40	SYSTEM				
	Fire fighting Equipments		29.16		29.10
	INSTALLATION OF NON				
	SHIFTABLE PLANT & MACH, FOR				
	THE INFRASTRUCTURE SUCH AS				
1.17	KITCHEN, LAUNDRY, HEALTH				
	CLUB, SPA, CONVENTION HALL,				1
	EXHIBITION HALL ETC.				1
					-
	Lump sum		1.50	1.50	
	OTHER FIXED STRUCTURES &				1
	PLANT & MACHINERY THAT ARE				1
	ESSENTIAL FOR THE				1
	COMMERCIAL OPERATION OF				1
	THE TOURISM UNIT				
	Statue & Mural Painting	8.96		8.96	
	3D Wall	2.62		2.62	100
1.19	PVC, Plant Flower & Trees	3.97		3.97	
and the second	Computers	9.74			9.74
	Geyser	0.20			0.20
	Security Items	1.07			1.07
	Fire Door	0.96			0.96
	Machine Scale	0.11			0.11
	Mobile Phone	0.56			0.56
	Washing Machine	5.42			5.42
	Round Off	0.02	33.63		0.02
	FREE PAID FOR OBTAINING	0.02	33.03		0.02
1.20	TECHNICAL KNOW-HOW				1
	Software		5.22		F 22
	INSTALLATION CHARGES OF		3.22		5.22
1.21	MACHINERY/ EQUIPMENT/				
	SERVICES				
	Lump sum		2.50	2.50	
	APPROACH ROAD,				
	EXPENDITURE & SEWERAGE				
1.22	(ON LAND TOURISM				
	UNIT)				
	Approach Road (265 sq. mtr. @			11.00	
	1600 per sq. mtr.)		4.24	4.24	
	RAIN WATER HARVESTING				
	SYSTEM				
1.25	Pipes	1.25		1.25	
	Water Boring	0.50		0.50	3
	Material	0.20	1.95	0.20	10
	Total	The St. B. Comp. Co. C.	657.34	241.77	415.5





Table: 4

S. No.	Heads of Capital Expenditure	Amount (Rs. In lakhs)
1	Eligible Capital Expenditure. (Break-up given from line item 1.1 to 1.25)	1808.18
1.1	Permanent structure for the project under the ownership and for use of the tourism unit, erected on land owned by the tourism unit and which is essential for its commercial operation.	1150.84
12	Boundary Wall/s	42.23
1.3	Internal roads, drainage & entrance gate/s.	40.26
1.4	Swimming pool/s.	17.74
1.5	Store/s:	50.90
1.6	Kitchen/s.	96.13
1.7	Water supply system(pipeline, tanks, pump house, water treatment plant etc.).	34.46
1.8	Boiler room & chimney.	NIL
1.9	Sewerage treatment plant and waste management system.	2.84
1.10	Centralized air conditioning system.	108.30
1.11	Power supply system.	109.99
1.12	D.G. Power backup(for self use).	42.09
1.13	Telecommunication tower(self established for own use).	NIL (on rent)
1.14	Hot & cold water supply system, gas/steam supply line.	9.59
1.15	Establishment of sound, light, public address, internet system and network of fixed nature.	24.61
1.16	Installation of fire detection and fire fighting system.	29.16
1.17	Installation of non-shiftable plant & machinery for the infrastructure such as kitchen, laundry, health club, spa, convention hall, exhibition hall etc.	1.50
1.18	Establishment of stationary swing sets, climbing walls, amusement/playing structure, permanent tents, etc. in play areas and parks.	NIL
	Continued	on page 2




HOTEL GRAND ARC, SHAHJAHANPUR

S. No.	Heads of Capital Expenditure	Amount (Rs. In lakhs)
1.19	Other fixed structures and plant & machinery that are essential for the commercial operation of the tourism unit.	33.63
1.20	Fees paid for obtaining technical know-how.	5.22
1.21	Installation charges of machinery/equipment/services.	2.50
1.22	Approach road, expenditure incurred for power supply including construction of sub-station, pipeline laid, water supply, water tank, pipeline for discharge of waste water & sewerage(on land where ownership is with the tourism unit)	4.24
1.23	Fixed residential tents for tourists, meant for use round the year and not for temporary use like mela, events or seasonal camps etc.	NIL
1.24	Solar/Bio energy system	NIL
1.25	Rain water harvesting system	1.95
2	Ineligible Capital Expenditure- As per Uttar Pradesh Tourism Policy 2018-Ineligible Items(Break-up given from line item 2.1 to 2.8)	569.39
2.1	Working Capital	48.11
2.2	Pre-operative and preliminary expenses	51.82
2.3	Second- hand plant and machinery purchased or shifted from within or outside country.	NIL
2.4	Interest Capitalized	240.94
2.5	Consumable stores, inventories for maintenance or repairs.	16.68
2.6	Investment on land required for setting up the tourism unit, inclusive of the cost of land.	NIL (on lease)
2.7	Vehicles, furniture & fixtures, cutlery, crockery and utensils.	211.84
2.8	Any construction which in nature of real estate transactions e.g. shops, flats, offices etc. meant for sale /lease/rent.	NIL
3.	Other Expenditures(Expenses not covered under Eligible Capital Expenditure & Ineligible Capital Expenditure. Provide details.)	NIL
4.	Total Capital Expenditure(1+2+3)	2377.57
5.	Arrangement of Capital	
5.1	Loan Amount from Bank(P.N.B.)	1195.18
5.2	Self/Promoter's Contribution(Partners' Capital)	267.32
5.3	Contribution from other sources(Loans from friends/relatives)	915.07
	Total(5.1 + 5.2 + 5.3)	2377.57

3. PROJECT LOCATION: This Hotel is setup by M/s. Shri Balaji Hospitality is located at Part of Khasra No.176, Village- Nawada Inderpur, Opposite Swami Sukhdevanand Inter college, Near Mumukshu Ashram, Tehsil- Sadar, District- Shahjahanpur, Uttar Pradesh. Project site is well connected by rail, road and airport. The nearest airport from the site is Lucknow Airport located at the distance of 177 km. The Project site is also well connected through Road network via NH-9 which is only few mtrs. away from the hotel. Shahjahanpur Railway Station is the nearest railway station which is around only 05 km from the project.



HOTEL GRAND ARC, SHAHJAHANPUR

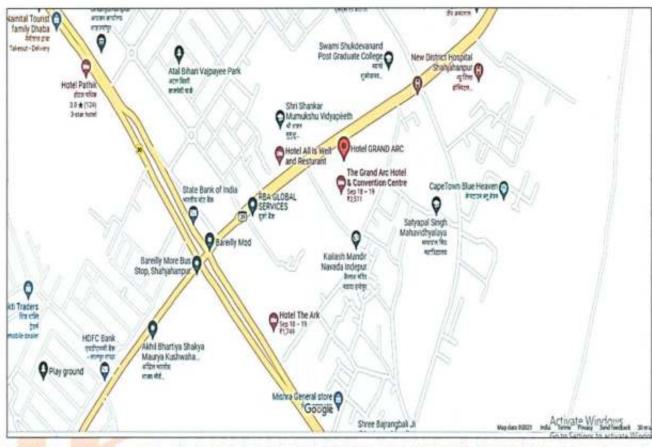



Page 12 of 51

FILE NO.: VIS (2021-22)-PL-451-403-516





4. SCOPE OF THE REPORT: To verify and examine the capital expenditure of the eligible investment of the project in regard to avail subsidy & incentives given to Hotel Projects development under Uttar Pradesh Tourism Policy-2018.

All the assessment carried out for the Project is done based on the documents provided to us and its correlation by the Engineering team through site inspection, various other discussions with the Project proponents and its resources and Industry standards and benchmark cost and thus forming an opinion out of it.

- 5. PURPOSE OF THE REPORT: To provide opinion on the Capital Expenditure incurred by the promoter in the development of the Hotel to help Directorate of Tourism, Government of Uttar Pradesh to take informed business decision on the project in relation to avail subsidy and incentives.
- 6. SURVEY DETAILS: This Hotel has been surveyed by our engineer Mr. Abhishek Solanki on September 10th, 2021. Site inspection was done in the presence of Hotel Grand Arc's representative. All the details pertaining to physical setup and progress of the hotel have been cross checked as per the documents provided to us.
 - a) During the site visit we have found that all the machinery & assets mentioned in the list provided to us by the client were present at the site and seems to be in good condition.
 - b) As per our visual observation, the main building of the hotel found to be built as per the copy of approved map provided to us. Swimming Pool, Lawn and some part of parking is not mentioned in the approved map. The total Plot area of the site is larger than the provided approved map area. Possession certificate is issued by the competent authority.
 - c) Extensive photographs have been taken of all different sections of the hotel to give a clear visual representation of the hotel establishment. At the time of site survey we have found the hotel is in operation.
 - d) Some of the photographs has been attached annexed with the report.





7. METHADOLOGY ADOPTED:

- a) Study of Detailed Project Report to know the Project proposed plan & estimates.
- b) Correlation of the capital expenditure of different section with Civil, P&M based industry benchmark with the provided copy of bills & invoices.
- c) Site visit by our engineer Mr. Abhishek Solanki to assess the project execution status on the ground at the site.
- d) Discussions with the Owner's representative on the site.
- e) Correlation of the provided information with the Industry standards, CPWD SOR, etc.
- f) Other information obtained regarding the project from the sources in the public domain.



FILE NO.: VIS (2021-22)-PL-451-403-516

HOTEL GRAND ARC, SHAHJAHANPUR



PARTC

PROJECT INFRASTRUCTURE SECTIONS & FACILITY DETAILS

 BUILDING & STRUCTURAL DETAILS: This Hotel project is a Basement + Ground + 5 floor RCC roofed structure with total built up area of 6287.59 sq.mtr. as per approved Map. The construction of the hotel had begun in year 2018 and is commercially operational since 07-11-2020. M/s. Shri Balaji hospitality has shown to have incurred Rs.12.60 Cr in Building & Civil works to construct the Hotel.

As per approved Map total land area is 6,949.65 sq.mtr. However the complete hotel is established on total land area approx. 14,678 sq. mtr. The portion of land area which is not shown in approved Map includes lawn, swimming pool & some part of parking as shown in Map below. As per verbal discussion with the promoters the land part which is not mentioned in the approved Map is also under ownership of promoters family and shareholders.



M/s. Shri Balaji Hospitality has engaged Local masons and laborers only for the Civil & building related works. The hotel construction is done by workers on daily wages which are monitored by the promoters.

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 15 of 51







Table: 5

BUILDING DETAILS					
1.	Approach Road & Guard Room	5.	Lawn 2		
2.	Parking	6.	Swimming Pool		
3	Entrance	7.	Main Structure		
4.	Lawn 1	8.	Lawn		

As per the approved map, lawn, swimming pool & some part of parking is not mentioned in approved map.

2. PLANT & EQUIPMENT DETAILS: In Machinery section Promoter has shown various equipments which have been installed that are needed for smooth operation of the hotel. Details of major heads with their cost is shown the table below. Breakup of expenses under each head is annexed in the annexure. Cost has been taken based on the item wise breakup and their bills/ invoices provided by the promoter and found installed on the site.

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 16 of 51





Table: 6

S. No.	Description of Assets	Items	Amounts	P&M
3. 140.	Description of Assets	Mellis	(in Lakhs)	(in Lakh
1	Internal Roads, Drainage &	Entrance Gate	1.10	1.10
	Entrance Gate/S	Ditek 7EH Barrier	0.86	0.86
2	Swimming Pool	Swimming Pool machinery	6.19	6.19
3	Kitchen/S	Kitchen Items & Equipments	53.40	53.40
	Water Supply System (Pipeline,	Pipes	1.52	0.00
4	Tanks, Pump House Water	Pump House	1.04	1.04
*	Treatment Plant Etc.)	Water treatment plant	1.41	1.41
	Treatment Flant Etc.)	Water Softening Plant	1.69	1.69
5	Sewerage Treatment Plant & Waste Mgt. System	ETP Water Treatment Plant	2.84	2.84
6	Centralized Airconditioning System	Air Conditioners	108.30	108.30
7	Power Supply System Including Sub Station,	Transformer	1.41	1.41
	Transformer, Distribution System & Electrification	Elect. Installation		103.72
0		Voltage Stabilizer	0.54	0.54
8		Inverter & Battery	3.84	3.84
		Vidyut Suraksha Vibhag	0.48	0.48
9	D.G. Power Back Up (For Self Use)	Genset	42.09	42.09
10	Hot & Cold Water Supply System, Gas/ Steam Supply Line	Heat Pump	9.59	9.59
11	Establishment Of Sound, Light,	Speaker, Woofer & Amplifiers	23.97	23.97
11	Public Address, Internet System	Projecter Screen	0.64	0.64
12	Installation Of Fire Detection And Fire Fighting System	Fire fighting Equipments	29.16	29.16
		Computers	9.74	9.74
	Other Fired Street, and 9 Blant 9	Geyser	0.20	0.20
	Other Fixed Structures & Plant &	Security Items	1.07	1.07
13	Machinery That Are Essential For	Fire Door	0.96	0.96
	The Commercial Operation Of The	Machine Scale	0.11	0.11
	Tourism Unit	Mobile Phone	0.56	0.56
		Washing Machine	5.42	5.42
14	Free Paid For Obtaining Technical Know-How	Software	5.22	5.22
	Total		417.07	415.55

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 17 of 51





PART D

PROJECT CAPITAL EXPENDITURE EVALUATION

Table: 7

	Table: 7							
S.No.	PARTICULARS	TOTAL INCURRED AMOUNT (As per CA certificate) (All Figure	TOTAL INCURRED AMOUNT (As Approved by IE) s in Lakhs)	CURRENT STATUS OF WORK AND REMARKS				
1.	Building (Except Stores, Kitchen)	1150.84	1150.84	 The Promoter has shown Rs.1150.84 Lakhs for the complete construction of the civil structure of building except store and Kitchen portion as per format of UP Tourism for applying subsidy. Total built-up area of the hotel is 6287.6 sq.mtr. Area of Kitchen and store is around 328.72 sq.mtr and 391.42 sq.mtr respectively. So net area to be taken under this head is 5567.46 sq.mtr. As per this net area cost of construction comes about Rs.20,670.82 per sq.mtr or Rs.1920.33 per sq.ft. This is a star rated facility not less than 4 star built up on RCC structure, modern design & architecture using high class material and specifications such as Italian/ 				





granite tiles/ marble in common areas inside the hotel and wooden flooring inside rooms.

- Based on the benchmarking cost as per construction industry standards and CPWD norms, the similar type of construction of same type of quality of construction having similar built-up area cost around Rs.2000 to Rs.2400 per sq.ft. As per UPPWD SOR 2020 Plinth area rate for non-residential is Rs.21,650 per sq.mtr. or Rs.2011.29 per sq.ft.
- Based on the above analysis the incurred cost appears to be within the benchmark norms.
- As per IE review it is found that cost incurred in the Buildings & Civil work is in the market range. Hence cost of Rs.1150.84 Lakhs in this head is approved.

However, Bills/ Invoices were not available, nor checked for the same due to engagement of local contractors/ laborers. Our vetting

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 19 of 51





				is done based on the Industry benchmark cost for the construction as found on site.
2.	Boundary wall	42.23	42.23	 The Promoter has shown Rs.42.23 Lakhs in the completion of boundary wall. Total length of boundary wall is ~654 ru.mtr having 12'-14' height. The incurred cost comes out to be Rs.6750/per ru.mtr. which is well within the market rate range for such construction. As per IE review it is found that cost incurred in the Boundary wall is in the range.
				Hence the cost of Rs.42.23 Lakhs. Is approved. Bills/ Invoices were not available, nor checked for the same due to engagement of local contractors/ laborers. Our vetting is done based on the Industry benchmark cost for the construction as found on site. (Please see the attached table).
3.	Internal Road, Drainage, Entrance gate	40.26	40.26	Internal roads is ~250 ru.mtr of approx. 8 mtr width or 2243 sq.mtr made up of cement chequered concrete tiles.

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 20 of 51





As per UPPWD norms, rate for constructing footpath with interlocking tiles with kerb stones is Rs.1670 per sq.mtr. In between the interlocking tiles they have used vitrified tiles as well. As per UPPWD norms the cost comes out to be Rs.37.45 Lacs.

- Drainage of 401 ru. mtr. made up of cement concrete.
 As per UPPWD norms rate for constructing internal drainage is Rs.4225/- per ru.
 Mtr. which is well within the market rate range for such construction. As per UPPWD norms cost comes out to be Rs.16.94 Lacs.
- Entrance Gate is of Rs.1.10
 Lacs as per the Bill which seems reasonable as per its size and weight and has been taken accordingly.
- Boom barrier is installed of Rs.86,000/- as per Bill which is taken as it is as we have got a quotation of Rs.1,00,00/- for such barrier.

Bills/ Invoices were not available, for the civil works due to engagement of local contractors/

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 21 of 51





				laborers. Our vetting is done based on the Industry benchmark cost for the construction as found on site. So, based on the above analysis, the cost incurred Rs.40.26 Lakhs appears to be reasonable and approved accordingly. (Please see the attached table).
4.	Swimming pool	17.74	17.74	 Grand Arc has shown to have incurred Rs.11.56 Lakhs in Civil works and Rs.6,18,559/-in P&M. No standard benchmarking cost is available for construction of swimming pool. So we have taken the market reference for construction of swimming pool having similar area and similar depth which comes to be approx Rs.800/- to Rs.900/- per sq. ft. on construction and civil works. Total built-up area of swimming pool is 165 sq. mtr. and the market rate for such type of construction having similar area and same depth is between Rs.11 lacs to Rs.13.0 Lacs. Bills/invoices are provided for the swimming pool machinery only which comes to be

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 22 of 51





			Rs.6,18,559/ Quotation sought for such type of setup has also come around Rs.9 Lacs to us. So accordingly as per IE review it is found that cost incurred in the swimming pool is within market range. Hence the cost of Rs.17.74 Lakhs is approved.
5. Store	50.90	50.90	Total built-up area of the store is 391.42 sq.mtr for this the cost of construction comes about Rs.13,003.93/- per sq.mtr or 1208.10 per sq. ft. as per standard benchmarking cost as per UPPWD. Based on the benchmarking cost as per construction industry standards and CPWD norms, the similar type of construction of same type of quality of construction having similar built-up area cost around Rs.2000 to Rs.2400 per sq.ft. as part of hotel. As per UPPWD SOR 2020 Plinth area rate for non-residential is Rs.21,650 per sq.mtr. or Rs.2011.29 per sq.ft.

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 23 of 51





HOTEL GRAND ARC, SHAHJAHANPUR

				So accordingly IE has approved the total amount Rs.50.90 Lakhs for this head.
6.	Kitchens	96.13	96.13	As per benchmarking cost the construction cost of Kitchen (area 328.72 sq.mtr) comes around Rs.71.16/- Lakh. as per UPPWD plinth area rate of Rs.21,650/- per sq. mtr. or Rs.2011.35 per sq. ft. for non-residential construction.
				 The Promoter has also provided invoices/bills for kitchen equipment which are essential for operation having total value equals Rs.53.39 Lakhs.
				So accordingly the cost appears to be reasonable and hence IE have approved the total value of Rs.96.13 Lakhs shown in this head.
7.	Water supply system (pipeline, tanks, pump house, water treatment plant etc.)	34.46	34.46	 Out of total bills provided for all things except RCC tanks. The total of bills comes to Rs.5,66,942/ As per UPPWD standard benchmarking cost the cost of construction of tank is Rs.17/-per liter. The RCC tank having area of 192 cu.mtr. or 1,92,000 litre which is

FILE NO.: VIS (2021-22)-PL-451-403-516

Rage 24 of 51





				constructed by the hotel, will cost to be approx. Rs.32.64 Lacs. So, based upon this the total cost incurred in this head in the market range. Hence, IE has approved total amount i.e. Rs.34.46 Lakhs in this head.
8.	Sewerage treatment plant and waste management system.	2.84	2.84	As per the invoices/bills have been provided the total amount spent on construction of STP is Rs.2.84 Lakh. Based upon invoices/bills, it is found that cost incurred in the STP and Waste management system is in the range. Hence IE has approved the value of Rs.2.84 Lakhs
9.	Centralized air conditioning system.	108.30	108.30	As per the invoices/bills, the total amount incurred in installation of centralized air conditioning system is Rs.108.30 Lakhs. Based upon invoices/bills, it is found that cost incurred in the centralized air conditioning system is in the market range. Hence we approved the value of Rs.108.30 Lakhs.
10.	Power supply system	109.99	109.99	 As per the invoices/bills, the total amount incurred in this head is Rs.109.99 Lakhs.

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 25 of 51





				As per our internal quotations also cost found to be reasonable. Based on invoices/bills, we found that cost incurred in the Power supply system is in the market range. Hence we approved the value of Rs.109.99 Lakhs.
11.	D.G. Power backup (for self use)	42.09	42.09	As per the invoices/bills have been provided, the total amount incurred in this head is Rs.42.09 Lakhs. Based on this, we found that cost incurred in the DG set is in the range. Hence we approved the value of Rs.42.09 Lakhs.
12.	Hot & cold water supply system, gas/ steam supply line.	9.59	9.59	As per the provided invoices/bills the total amount incurred in this head is Rs.9.59 Lakhs. As per provided invoices and bills it is found that cost incurred in this head is in the market range. Hence we approved the value of Rs.9.59 Lakhs.
13.	Establishment of sound, light, public address, internet system and network of fixed nature.	24.61	24.61	As per the invoices/bills have been provided, the total amount incurred in this head is Rs.24.61 Lakhs. The English English The Engl

FILE NO.: VIS (2021-22)-PL-451-403-516

Page **26** of **51**



HOTEL GRAND ARC, SHAHJAHANPUR

				As per IE review it is found that cost incurred in this head is in market range. Hence we approved the value of Rs.24.61 Lakhs.
14.	Installation of fire detection and fire-fighting system.	29.16	29.16	As per the provided invoices/bills the total amount incurred in this head is Rs.29.16 Lakhs. As per provided invoices/bills, it is found that cost incurred in this head is in the market range. Hence we approved the value of Rs.29.16 Lakhs.
15.	Installation of non- shiftable plant & machinery for the infrastructure such as laundry, health club, spa, convention hall, exhibition hall etc.	1.50	1.50	As per the cash ledger statement, the total amount incurred in this head is Rs.1.50 Lakhs. As per IE review it is found that cost incurred in this head is in the market range. Hence we approved the value of Rs.1.50 Lakhs.
16.	Other fixed structures and plant & machinery that are essential for the commercial operation of the tourism unit.	33.63	19.89	Out of total Rs.33.63 Lakhs the promoter has spent Rs.18.08 Lakhs on machinery and other items and Rs.15.55 Lakhs on statue & Mural Paintings, 3D wall and Plant & Flowers.

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 27 of 51





- From the machinery bills we have neglected amount Rs.80,521/- which was spent on Tablet, Cartridge, Ink for printer and mobiles which are used as consumable and others have been approved as per Invoices/ Bills.
- From the total amount spent on statue, Mural painting, 3D wall and PVC, Plant and Trees. We have only approved the cost of 3D wall which cost to be approx. Rs.2.62 Lakhs for 3D wall which is as per market range. Expenditure which spent on statue, Mural Paimnting and Plant & Trees is not approved since it is the part of furniture and fixture.
- Total Built-up area which was covered under 3D wall is approx. 2600 sq. ft. The incurred cost comes out to be Rs.100/- per sq.ft. which is well within the market rate range for such construction.

So, IE has approved only Rs.19.89 Lakhs in this head.

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 28 of 51



HOTEL GRAND ARC, SHAHJAHANPUR

16.	Fees paid for obtaining technical know-how.	5.22	5.22	This amount is spent in the ERP software license for Hotel, website designing and other e-promotions. As per the provide invoices/bills, the total amount incurred in this head is Rs.5.22 Lakhs. So, as per IE review it is found that cost incurred in this head is in the market range. Hence we approved the value of Rs.5.22 Lakhs.
17.	Installation charges of machinery/ equipment/ services.	2.50	2.50	These amount is spent on installation of Transformer, Generator and other machinery like Geyser, television etc. As per IE review it is found that cost incurred in this head is in the market range. Hence we approved the value of Rs.2.50 Lakhs.
18.	Approach road, expenditure incurred for power supply including construction of substation, pipeline laid, water supply, water tank, pipeline for discharge of waste water & sewerage (on land where	4.24	4.24	 Internal roads is ~265 sq.mtr of approx. 15 mtr width made up of cement chequered concrete tiles. As per UPPWD norms rate for constructing approach road with interlocking tiles with kerb stones is Rs.1670

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 29 of 51





	ownership is with the tourism unit)			per sq.mtr. As per UPPWD norms the cost comes out to be Rs.4.42 Lacs. • Bills/ Invoices were not available, nor checked for the same due to engagement of local contractors/ laborers. Our vetting is done based on the Industry benchmark cost for the construction as found on site.
		5 0		So, Based on this, the cost incurred in construction of approach road is in the range. Hence, IE has approved the entire amount, for construction of approach road, power supply and construction of Substation, which is Rs.4.24 Lacs.
18	Rain water Harvesting System	1.95	1.95	 As per the invoices/bills provided by the Promoters for Pipes which is equals to Rs.1.25 Lacs. No Bills and invoices are provided for water boring and materials for rain water harvesting. As per market research we found that the total cost incurred in water boring and material for rain water harvesting is Rs.75,000/- to Rs.80,000/

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 30 of 51





			Based on this IE has approved Rs.1.95 Lakhs in this part as Promoter has constructed underground storage tank for rain water harvesting pictures of the same has been attached with the report.
Total	1808.18	1794.44	All the expenditure shown above is cross checked with the work done on site and from the respective Invoices / Bills / PO / ledger statements. Only major amount has been cross checked from the Invoices / Bills / PO due to voluminous paper of record. Industry benchmark & standards is applied only to Civil works cost for its verification since no Bills/ Invoices have been provided for the same due to involvement of petty contractors. In case of Plant & Machinery no specific benchmark cost standard is available. Therefore for Plant & Machinery cost verification individual invoices, bills and quotations from different vendors, and items available on sale on public domain are only relied upon.

FILE NO.: VIS (2021-22)-PL-451-403-516





(Please see attached annexure for head wise breakup and its related Bills/ Invoices).

FILE NO.: VIS (2021-22)-PL-451-403-516

HOTEL GRAND ARC, SHAHJAHANPUR



PART F

PHOTOGRAPHS





FILE NO.: VIS (2021-22)-PL-451-403-516

Page 33 of 51

HOTEL GRAND ARC, SHAHJAHANPUR









FILE NO.: VIS (2021-22)-PL-451-403-516









FILE NO.: VIS (2021-22)-PL-451-403-516

HOTEL GRAND ARC, SHAHJAHANPUR







FILE NO.: VIS (2021-22)-PL-451-403-516

HOTEL GRAND ARC, SHAHJAHANPUR







FILE NO.: VIS (2021-22)-PL-451-403-516

Page 37 of 51

HOTEL GRAND ARC, SHAHJAHANPUR









FILE NO.: VIS (2021-22)-PL-451-403-516

Page 38 of 51









FILE NO.: VIS (2021-22)-PL-451-403-516









FILE NO.: VIS (2021-22)-PL-451-403-516

Page 40 of 51









FILE NO.: VIS (2021-22)-PL-451-403-516

Page 41 of 51





PART F

QUOTATIONS

Washing Machine



Hydro Extractor









Drying Tumbler



Vaccum Ironing Table









Automatic Steam Generator



Door Frame Metal Detector







Printer



WRM WHT H060







Hydrant Pump



Voltage Stabilizer










Boom Barrier Housys White And Grey Boom Barrier ₹ 85,000 Get Latest Price Color White and Grey Housys. Material Aluminium Size 2.5 m to 6 m. HOUSYS Automatic, Semi-Automatic Type Automation Grade Automatic View Complete Details. Fill the quantity to get latest price! Quantity Piece **Get Latest Price**

JBL Loudspeaker












Swimming Pool

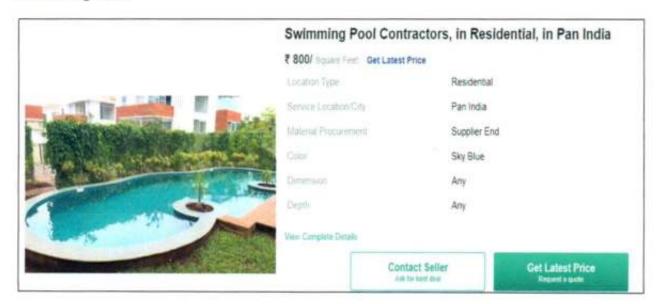









PART G

DISCLAIMER

- 1. No employee or member of R.K Associates has any direct/ indirect interest in the Project.
- 2. This report is prepared based on the copies of the documents/ information which interested organization or customer could provide to us out of the standard checklist of documents sought from them and further based on our assumptions and limiting conditions. All such information provided to us has been relied upon and we have assumed that it is true and correct. Verification or cross checking of the documents provided to us has not been done at our end from the originals. If at any time in future it's found or came to our knowledge that misrepresentation of facts or incomplete or distorted information has been provided to us then this report shall automatically become null & void.
- 3. This report is a general analysis of the project and not an audit report. All the information gathered is based on the facts seen on the site during survey, verbal discussion & documentary evidence provided by the client and is believed that information given by the Promoter is true best of their knowledge.
- 4. All observations mentioned in the report is only based on the visual observation and the documents/ data/ information provided by the client. No mechanical/ technical tests, measurements or any design review have been performed or carried out from our side during Project assessment.
- Interested organization should ONLY take this report as an Advisory document from the Financial/
 Chartered Engineering firm and it's specifically advised to the stakeholder to cross verify the
 original documents for the facts mentioned in the report which can be availed directly from the
 subject Promoter directly.
- In case of any default in loans or the credit facility extended to the borrowing Promoter, R.K.
 Associates shall not be held responsible for whatsoever reason may be and any request for
 seeking any explanation from the employee/s of R.K. Associates will not be entertained at any
 instance or situation.
- This Report is prepared by our competent technical team which includes Engineers and financial experts & analysts.
- 8. This is just an opinion report and doesn't hold any binding on anyone. It is requested from the concerned Financial Institution which is using this report for taking financial decision on the project that they should consider all the different associated relevant & related factors also before taking any business decision based on the content of this report.





- All Pages of the report including annexures are signed and stamped from our office. In case any
 paper in the report is without stamp & signature then this should not be considered a valid paper
 issued from this office.
- 10. Defect Liability Period is 30 DAYS. We request the concerned authorized reader of this report to check the contents, data and calculations in the report within this period and intimate us in writing if any corrections are required or in case of any other concern with the contents or opinion mentioned in the report. Corrections only related to typographical, calculation, spelling mistakes will be entertained within the defect liability period. No request for any illegitimate value revision, date change or any other facts & figures changes will be entertained other than the one mentioned above.
- 11. R.K Associates encourages its customers to give feedback or inform concerns over its services through proper channel at <u>valuer@rkassociates.org</u> in writing within 30 days of report delivery. After this period no concern/ complaint/ proceedings in connection with the Valuation Services can be entertained due to possible change in situation and condition of the property.
- 12. Our Data retention policy is of <u>ONE YEAR</u>. After this period we remove all the concerned records related to the assignment from our repository. No clarification or query can be answered after this period due to unavailability of the data.
- 13. This Valuation report is governed by our (1) Internal Policies, Processes & Standard Operating Procedures, (2) R.K Associates Quality Policy, (3) Valuation & Survey Best Practices Guidelines formulated by management of R.K Associates, (4) Information input given to us by the customer and (4) Information/ Data/ Facts given to us by our field/ office technical team. Management of R.K Associates never gives acceptance to any unethical or unprofessional practice which may affect fair, correct & impartial assessment and which is against any prevailing law. In case of any indication of any negligence, default, incorrect, misleading, misrepresentation or distortion of facts in the report then it is the responsibility of the user of this report to immediately or atleast within the defect liability period bring all such act into notice of R.K Associates management so that corrective measures can be taken instantly.
- 14. R.K Associates never releases any report doing alterations or modifications from pen. In case any information/ figure of this report is found altered with pen then this report will automatically become null & void.
- 15. If this report is prepared for the matter under litigation in any Indian court, no official or employee of R.K Associates will be under any obligation to give in person appearance in the court as a testimony. For any explanation or clarification, only written reply can be submitted on payment of charges by the plaintiff or respondent which will be 10% of the original fees charged where minimum charges will be Rs.15,000/-.

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 50 of 51





Place: New Delhi

Date : 28.09.2021

Note: This report contains 51 pages

FOR INTERNAL USE

SURVEYED BY: SE Abhishek Solanki

PREPARED BY: Engg. Team

REVIEWED BY: MA

For R.K Associates Valuers & Techno Engineering Consolitants Pvt. Ltd.

Project Engineering Team

R.K ASSOCIATES IMPORTANT NOTES:

- 1. <u>DEFECT LIABILITY PERIOD</u> In case of any query/ issue or escalation you may please contact incident Manager by writing at le@rkassociates.org. We ensure 100% accuracy in the Calculations done, Rates adopted and various other data points & information mentioned in the report but still can't rule out typing, human errors or any other mistakes. In case you find any mistake, variation, discrepancy or inaccuracy in any data point of the report, please help us by bringing all such points into our notice in writing at le@rkassociates.org within 30 days of the report delivery, to get these rectified timely, failing which R.K Associates Valuers Techno Engineering Consultants (P) Ltd. won't be held responsible for any inaccuracy in any manner. Also if we do not hear back anything from you within 30 days, we will assume that report is correct in all respect and no further claim of any sort will be entertained thereafter. We would welcome and appreciate your feedback & suggestions in order to improve our services.
- COPYRIGHT FORMAT This report is prepared on the copyright format of R.K Associates Valuers Techno Engineering
 Consultants (P) Ltd. to serve our clients in the best possible way. Legally no one can copy or distribute this format without
 prior approval from R.K Associates. It is meant only for the organization as mentioned on the cover page of this report.
 Distribution or use of this format other than R.K Associates will be seen as unlawful act and necessary legal action can be
 taken against the defaulter.

Julyed

FILE NO.: VIS (2021-22)-PL-451-403-516

Page 51 of 51
