
ASSOCIATES"

SURVEY FORM FOR GROUP HOUSING PROJECTS
Date: 29-11-21. Survey No. RKA/DNCR/
1. PROJECT NAME: Eureka. Park. (Phase 1).
2. PROJECT PROMOTER/S: (Company Name/ Director/s Name) M/J Land Kary Builder PH 240.
3. PROJECT BUILDER: M/S Land Kout & Beulch Put Us
4. PROJECT ARCHITECT: M/J ACPI Degin LAU 5. TOTAL ESTIMATED DE
5. TOTAL ESTIMATED PROJECT COST: AS Per cloc.
6. LAND COST: (PMR Value) Per doc.
7. ESTIMATED BUILDING CONSTRUCTION COST: OF Per doc
8. COMPLETED CONSTRUCTION COST: A por clor.
9. TOTAL NO. OF TOWERS/ BLOCKS: 10 tower.
10. TOTAL NO. OF FLOORS PER TOWER: Whatlen in Other page
11. TOTAL NO. OF FLATS: 1160 UN'TY
12. TYPE OF UNITS: 2BHK + 27, 3BHK + 27, 3BHK+ 4T.

13. SUPER AREA COVERED AREA OF UNITS: 1/100, 1285, 1575 SA W.
14. AMENETIES PRESENT IN THE PROJECT: (Club/ Gymnasium/ Swimming Pool/ Recreational centre/ Others)
15. TOTAL LAND AREA: 20.7+ Acres
16. TOTAL GROUND COVERAGE AREA: A per elec-
17. FAR/ TOTAL COVERED AREA: As per close.
18. PROPOSED GREEN AREA: De per elle.
18. PARKING AREA DETAILS (a) Basement Parking: (b) Stilt Parking: (c) Open Parking: (Total Area/ Parking for No. of Cars)
19. PROPOSED COMPLETION DATE OF THE PROJECT: Sep. 2023
20. PROGRESS OF THE PROJECT: (Total No. of Towers constructed/ Total FAR constructed) Worlden in other page
21. DEVELOPER/BUILDER PAST PROJECTS: First Project
22. LANDMARK: Self.
23. APPROACH ROAD WIDTH: 24 M.
24. PROJECT LAUNCH RATE:

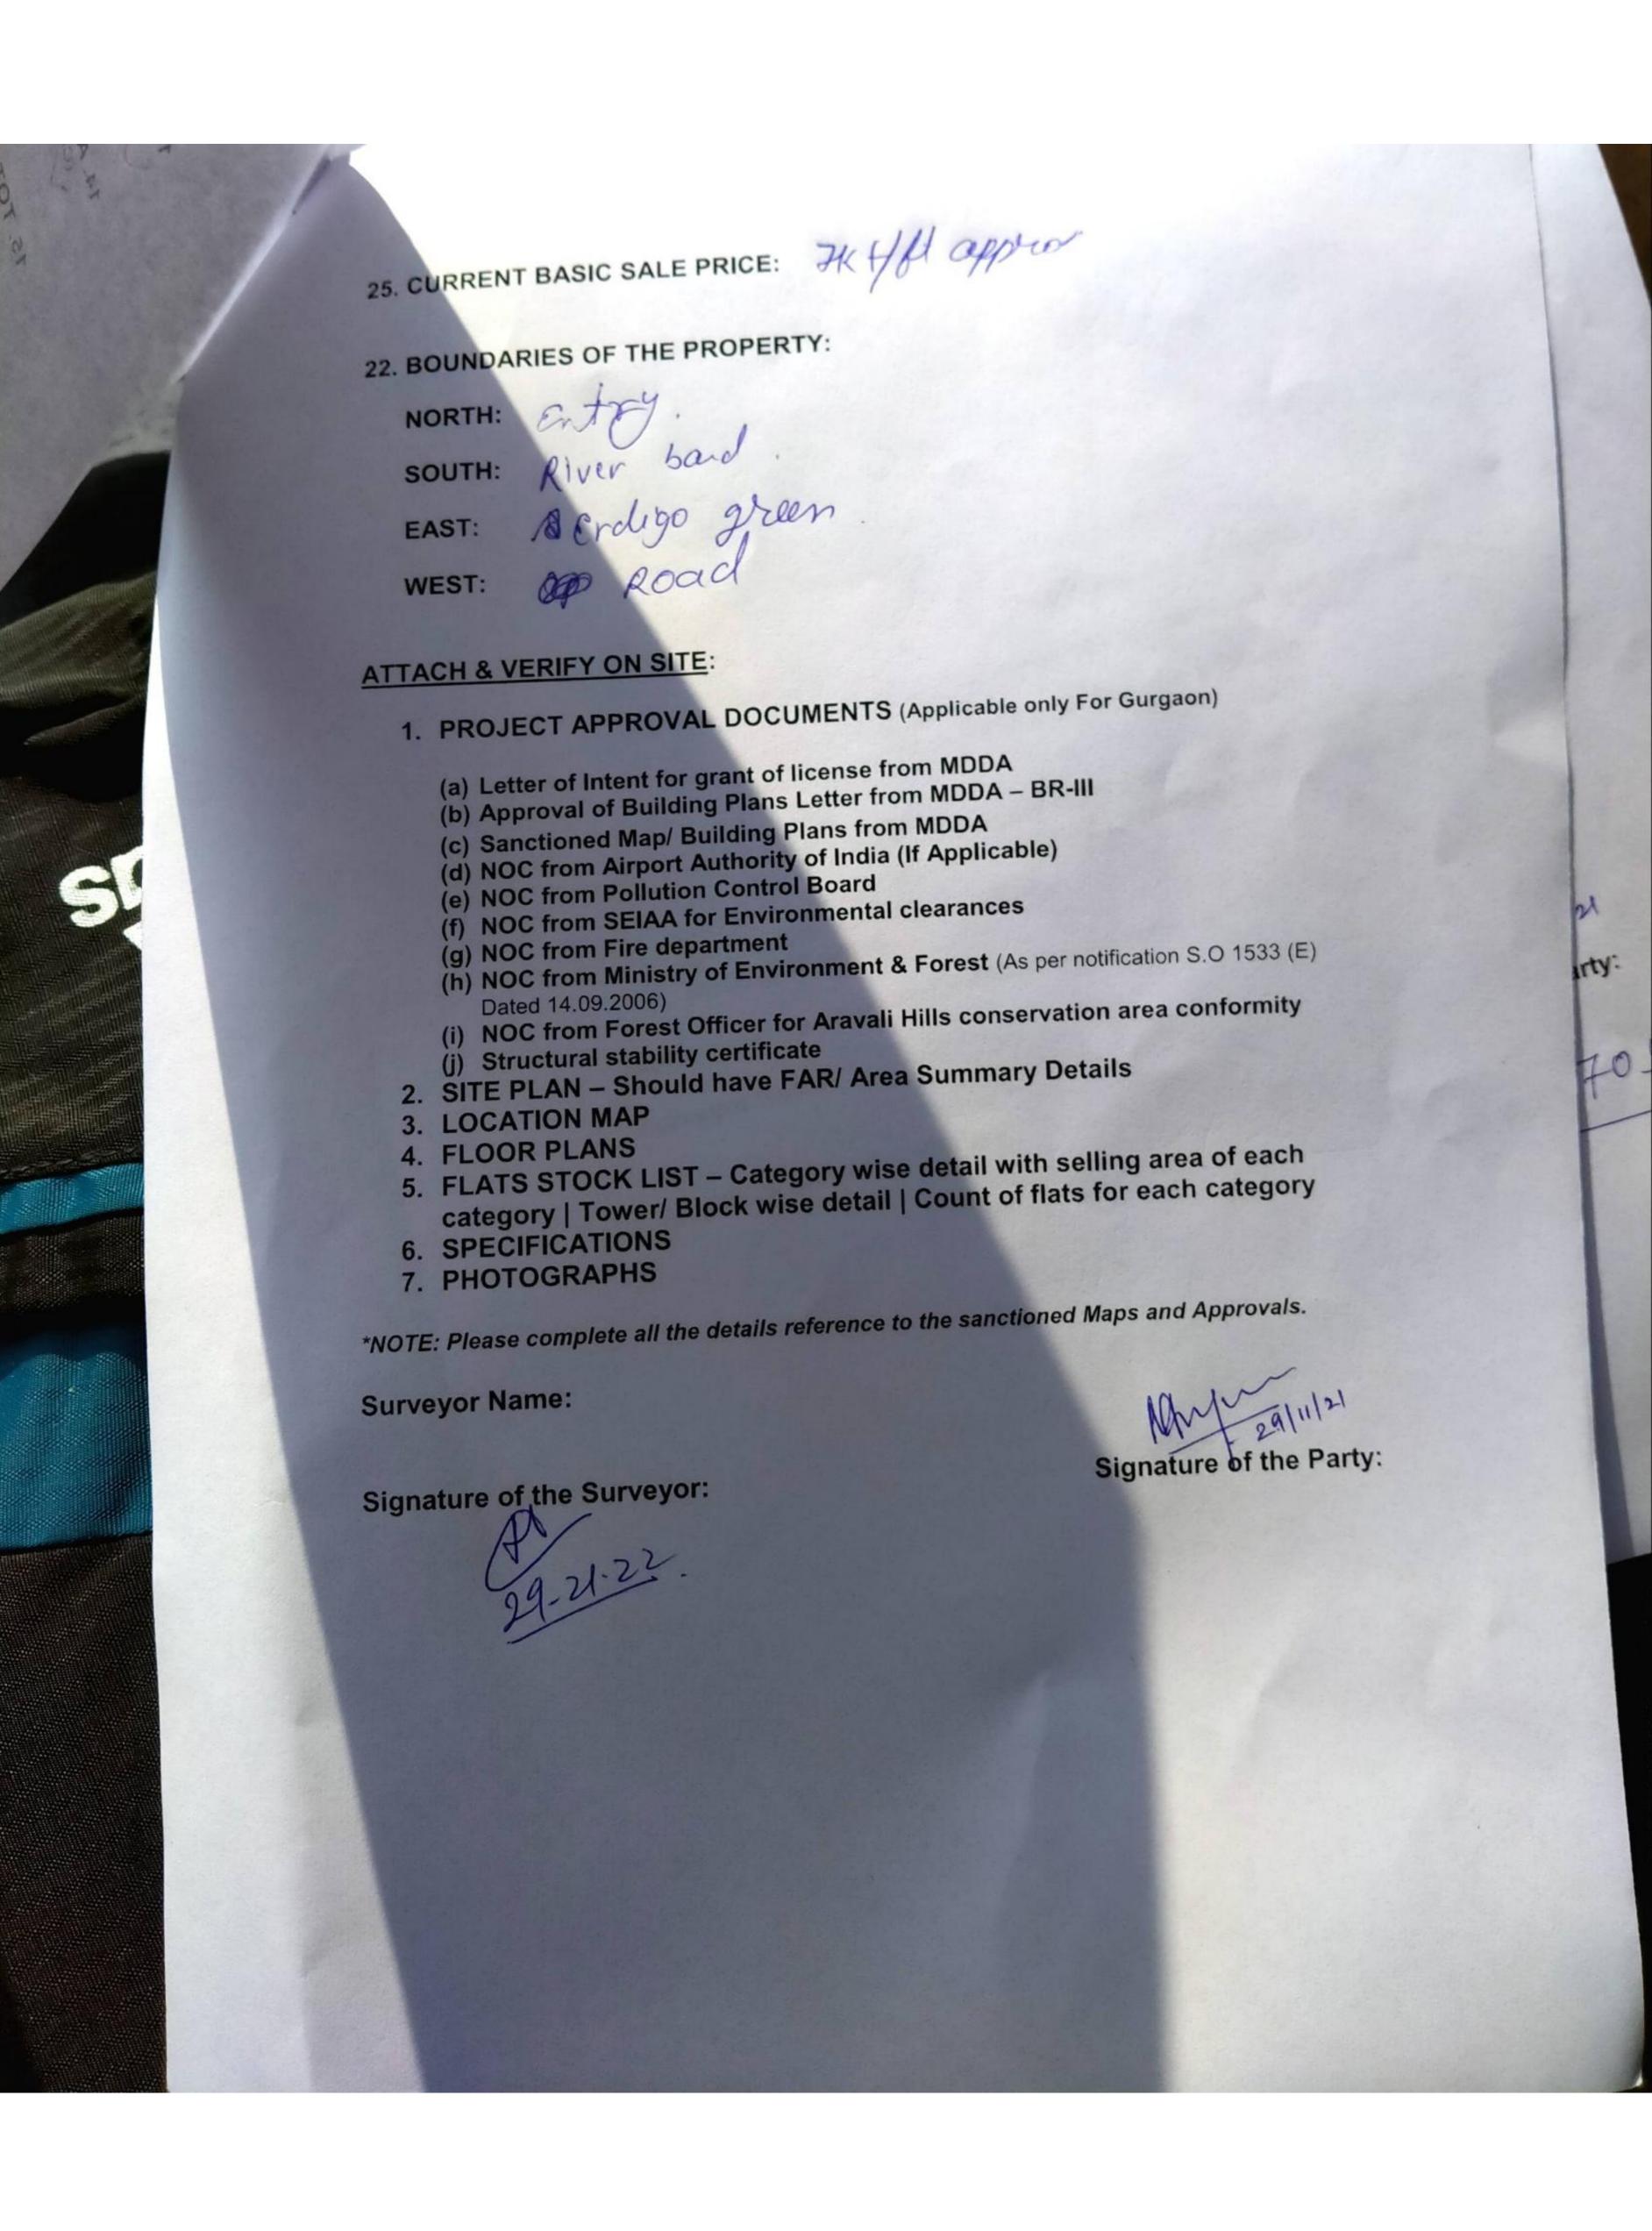

Tower Ø, - 26th floor in progress. 911 A2 - Same. SHIP A3 - 25th in progress sur dy - 24th 9/8428 @B8 - Terrace complted 9/5428. B9- Terrace en progren SISt 28 B10 = Terrace complted. St9 + 2 C 19= 19th in progress 3/427 C20 = 18th in progrts. Spar C21 = 16th in progres.
