

REPORT FORMAT: V-L3 (Medium) | Version: 6.0_2018

File No.: VIS (2021-22)-PL674-585-754 Dated:01.12.2021

PROJECT TIE -UP REPORT

OF

GROUP HOUSING SOCIETY

EUREKA PARK

SITUATED AT

PLOT NO. SC-02/A1, SPORTS CITY, SECTOR-150, NOIDA, UTTAR PRADESH

DEVELOPED & OWNED BY

MIS. LAND KART BUILDERS PVT. LTD.

- Corporate Valuers
- Business/ Enterprise/ Equity Valuations
- bosinessy chierprisey equity valounous

Lender's Independent Engineers (LIE)

REPORT PREPARED FOR

STATE BANK OF INDIA, HLST BRANCH, NOIDA, UTTAR PRADESH

- Techno Economic Viability Consultants (TEV)
- Agency for Specialized Arcount Manitoring (ASM) y query/ issue or escalation you may please contact Incident Manager
- Project Techno-Financial Advisors
- Frojeci lecilio-filialiciai Advisors
- Chartered Engineers
 Chartered Engineers<
- Industry/Trade Rehabilitation Consultants
- NPA Management

CORPORATE OFFICE:

D-39, 2nd floor, Sector 2, Noida-201301 Ph - +91-0120-4110117, 4324647, +91 - 9958632707 E-mail - valuers@rkassociates.org | Website: www.rkassociates.org

 Panel Valuer & Techno Economic Consultants for PSU Banks

EUREKA PARK, SECTOR-105, NOIDA



PART A

SUMMARY OF THE PROJECT TIE-UP REPORT

1. GENERAL DETAILS a. Report prepared for b. Name & Address of Organization c. Name of Promoter d. Name of Property Owner e. Address & Phone Number of the owner owner f. Type of the Property g. Type of Loan h. Type of Valuation i. Report Type j. Date of Inspection of the Property k. Date of Valuation Project Tie-Up Report j. Surveyed in presence of n. Scope of the Report o. Out-of-Scope of Report o. Out-of-Scope of Report p. Documents provided for perusal Bank State Bank of India, HLST Branch, Noida, U.P State Bank of India, HLST Branch, Noida, U.P State Bank of India, HLST Branch, Noida, U.P Mrs. Land Kart Builders Pvt. Ltd. Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127 Regis	S.NO.	CONTENTS	DES	SCRIPTION			
b. Name & Address of Organization c. Name of Promoter d. Name of Property Owner e. Address & Phone Number of the owner M/s. Land Kart Builders Pvt. Ltd. ### Ms. Land Kart Builders Pvt. Ltd. ### Ms. Land Kart Builders Pvt. Ltd. ### Ms. Land Kart Builders Pvt. Ltd. ### Registered Office: 7º Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 ### Ms. Land Kart Builders Pvt. Ltd. ### Registered Office: 7º Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 ### Ms. Land Kart Builders Pvt. Ltd. ### Registered Office: 7º Floor, Tower-B, Plot No.08, Sector-127 Noida - 201301 ### Ms. Land Kart Builders Pvt. Ltd. ### Ms. Land Ka	1.	GENERAL DETAILS					
c. Name of Promoter d. Name of Property Owner e. Address & Phone Number of the owner Noida - 201301 f. Type of the Property Group Housing society g. Type of Loan h. Type of Valuation i. Report Type j. Date of Inspection of the Property l. Surveyed in presence of Project Tie-up Report l. Surveyed in presence of Project Tie-up Report l. Surveyed in presence of Project Tie-up Report l. Surveyed in Project Tie-up Report l. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report iii. Identification of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vi. Drawing Map & design of the property is out of scope of the work. Documents provided for perusal Documents Requested Documents Provided Total 05 documents provided. Property Title document Sub - Lease Dated 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained) from UP-RPATAN News.	a.	Report prepared for	Bank				
c. Name of Promoter d. Name of Property Owner e. Address & Phone Number of the owner Noida - 201301 f. Type of the Property Group Housing society g. Type of Loan h. Type of Valuation i. Report Type j. Date of Inspection of the Property l. Surveyed in presence of Project Tie-up Report l. Surveyed in presence of Project Tie-up Report l. Surveyed in presence of Project Tie-up Report l. Surveyed in Project Tie-up Report l. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report iii. Identification of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vi. Drawing Map & design of the property is out of scope of the work. Documents provided for perusal Documents Requested Documents Provided Total 05 documents provided. Property Title document Sub - Lease Dated 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained) from UP-RPATAN News.	b.	Name & Address of Organization	State Bank of India, HLST I	Branch, Noida, U.P			
e. Address & Phone Number of the owner f. Type of the Property g. Type of Loan h. Type of Valuation i. Report Type j. Date of Inspection of the Property k. Date of Valuation Project Tie-up Report J. Surveyed in presence of Project Tie-up Report Promoter's representative Mrs. Minakshi Contact No.8802570553 M. Purpose of the Valuation Project Tie- Up Report Project Tie- Up Report I. Surveyed in presence of Project Tie- Up Report Project Tie- Up Report O. Out-of-Scope of Report I. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. II. Legal aspects of the property are out-of-scope of this report iii. Identification is not done at our end. V. Measurement is only limited upto sample random measurement. V. Measurement is only limited upto sample random measurement. V. Measurement of the property as a whole is not done at our end. V. Measurement of the property as a whole is not done at our end. V. Measurement of the property as a whole is not done at our end. V. Measurement of the property as a whole is not done at our end. V. Measurement of the property as a whole is not done at our end. V. Measurement of the property is out of scope of the work. Documents Requested Documents Provided Total 05 documents Provided Approved Map Property Title document Sub - Lease Dated 15/06/2016 Approved Map Approved Map Approved Map Approved Map Address Provided Property Title document	C.		M/s. Land Kart Builders Pvt. Ltd.				
f. Type of the Property g. Type of Loan h. Type of Valuation i. Report Type Project Tie-up Report j. Date of Inspection of the Property j. Date of Inspection of the Property j. Date of Valuation Report l. Surveyed in presence of Promoter's representative Project Tie- up Report Promoter's representative Mrs. Minakshi Contact No.8802570553 m. Purpose of the Valuation Project Tie- up Report Project Tie- up Report l. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report lidentification of the property are out-of-scope of this report lidentification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vii. Drawing Map & design of the property is out of scope of the work. p. Documents provided for perusal Property Title document Provided Approved Map Sanctioned Letter of building plans from NOIDA (obtained from UP-REPA). Approved Map Sanctioned Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of building plans from NOIDA (obtained from UP-REPA). Letter of the Property is out of scope and the property is	d.	Name of Property Owner	M/s. Land Kart Builders Pvt	. Ltd.			
g. Type of Loan h. Type of Valuation i. Report Type j. Date of Inspection of the Property j. Date of Inspection of the Property k. Date of Valuation Report l. Surveyed in presence of Project Tie-Up Report Project Tie-Up Report I. Surveyed in presence of Promoter's representative Project Tie- up Report Out-of-Scope of the Valuation Project Tie- up Report I. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report iii. Identification of the property are out-of-scope of this report iii. Identification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. V. Measurement is only limited upto sample random measurement. Vi. Measurement of the property as a whole is not done at our end. Vii. Drawing Map & design of the property is out of scope of the work. Documents Requested Documents Provided Provided Property Title document Provided Approved Map Sanctioned Interest Provided Approved Map Approved Map Approved Map NolDA (obtained from UP-REPANA Nace)	e.			r, Tower-B, Plot No	o.08, Sector-127,		
h. Type of Valuation i. Report Type j. Date of Inspection of the Property j. Date of Valuation Report l. Surveyed in presence of l. Verification Project Tie- up Report l. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report iii. Identification of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. l. Measurement of the property as a whole is not done at our end. vii. Drawing Map & design of the property is out of scope of the work. p. Documents provided for perusal Documents Requested Total 05 documents Provided Total 05 documents Provided Total 05 documents Provided. Property Title document Sub - Lease Deed 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-REPAIN Asset)	f.	Type of the Property	Group Housing society				
i. Report Type j. Date of Inspection of the Property j. Date of Inspection of the Property k. Date of Valuation Report 1. December 2021 I. Surveyed in presence of Promoter's representative Project Tie- up Report Dut-of-Scope of the Valuation Project Tie- Up Report O. Out-of-Scope of Report I. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report liii. Identification of the property are out-of-scope of this report liii. Identification of the property are out-of-scope of this report sit is identification is not done at our end. V. Measurement. V. Measurement is only limited upto sample random measurement. V. Measurement of the property as a whole is not done at our end. Vii. Drawing Map & design of the property is out of scope of the work. Documents Requested Documents Provided Property Title document Sub - Lease Deed 15/06/2016 Approved Map Approved Map Approved Map Approved Map Dated Etter of building plans from NOIDA (obtained from UP-REAK) assets Description of authenticity of documents represented in the property are out-of-scope of this report is not done at our end. V. Measurement is only limited upto sample random measurement. Vii. Deasurement of the property as a whole is not done at our end. Viii. Drawing Map & design of the property is out of scope of the work. Documents Requested Documents Provided Property Title document Sub - Lease Deed 15/06/2016 Approved Map Dated Etter of building plans from NOIDA (obtained from UP-REAK) assets Description from UP-REAK) assets	g.	Type of Loan	NA				
j. Date of Inspection of the Property k. Date of Valuation Report l. Surveyed in presence of Promoter's representative Contact No.8802570553 m. Purpose of the Valuation Project Tie- up Report o. Out-of-Scope of Report i. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. ii. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vii. Drawing Map & design of the property is out of scope of the work. p. Documents provided for perusal Documents Requested Documents Provided Total 05 documents provided. Property Title document Sub - Lease Deed 15/06/2016 Approved Map Approved Map Approved Map Approved Map Approved Map Dated 15/06/2016 Approved Map Approved Map Dated 24/10/2016 24/10/2016	h.	Type of Valuation	Project Tie-up Report				
k. Date of Valuation Report I. Surveyed in presence of Promoter's representative Project Tie- up Report Dout-of-Scope of Report O. Out-of-Scope of Report I. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report iii. Identification of the property are out-of-scope of this report. iii. Verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. V. Measurement is only limited upto sample random measurement. Vi. Measurement of the property as a whole is not done at our end. Vii. Drawing Map & design of the property is out of scope of the work. Documents Requested Documents Provided Total 05 documents provided. Property Title document Sub - Lease Deed 15/06/2016 Approved Map NOIDA (obtained from UP-REPA) Association and the plant of the property as a whole is not done at our end. Viii. Drawing Map & design of the property is out of scope of the work. Documents Requested Documents Provided Reference No. Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-REPA) Association with revenue officers for the property is out of scope of the property is out of scope of the work.	i.	Report Type	Project Tie-Up Report				
I. Surveyed in presence of Promoter's representative Contact No.8802570553 m. Purpose of the Valuation Project Tie- up Report n. Scope of the Report Project Tie- Up Report o. Out-of-Scope of Report Project Tie- Up Report i. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report iii. Identification of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vii. Drawing Map & design of the property is out of scope of the work. p. Documents provided for perusal Documents Requested Documents Provided Reference No. Total 05 documents provided. Property Title document Sub - Lease Deed 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-REPA) And account of the property are out-of-scope of the property is out of scope of the work.	j.	Date of Inspection of the Property	29 November 2021				
m. Purpose of the Valuation Project Tie- up Report n. Scope of the Report Project Tie- Up Report o. Out-of-Scope of Report Project Tie- Up Report i. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report iii. Identification of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vii. Drawing Map & design of the property is out of scope of the work. p. Documents provided for perusal Documents Requested Documents Provided Reference No. Total 05 documents Total 05 requested. Documents provided. Property Title document Sub - Lease Deed 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-REPAIN Mass).	k.	Date of Valuation Report	1 December 2021				
n. Scope of the Report o. Out-of-Scope of Report i. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report iii. Identification of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vii. Drawing Map & design of the property is out of scope of the work. p. Documents provided for perusal Documents Requested Total 05 documents Provided Total 05 documents requested. Documents Provided. Property Title document Sub - Lease Deed 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-REPA) is associated.	I.	Surveyed in presence of	Promoter's representative	Company of the Compan	570553		
i. Verification of authenticity of documents from originals or cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report lidentification of the property are out-of-scope of this report iii. Identification of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vii. Drawing Map & design of the property is out of scope of the work. p. Documents provided for perusal Documents Requested Documents Provided Reference No. Total 05 documents requested. Documents Sub - Lease Deed 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-REPA)	m.	Purpose of the Valuation	Project Tie- up Report				
cross checking from any Govt. deptt. is not done at our end. ii. Legal aspects of the property are out-of-scope of this report iii. Identification of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vii. Drawing Map & design of the property is out of scope of the work. Documents Requested Documents Provided Reference No. Total 05 documents requested. Total 05 Total 05 documents provided. Property Title document Sub - Lease Deed 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-RERA) Massa.	n.	Scope of the Report	Project Tie- Up Report				
Total 05 documents requested. Property Title document Approved Map Total 05 Total 05 documents provided. Property Title document Sub - Lease Deed Deed 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-RERA) NASSON			cross checking from any Govt. deptt. is not done at our end ii. Legal aspects of the property are out-of-scope of this reportion iii. Identification of the property is only limited to cross verification from its boundaries at site if mentioned in the provided documents. iv. Getting cizra map or coordination with revenue officers for site identification is not done at our end. v. Measurement is only limited upto sample random measurement. vi. Measurement of the property as a whole is not done at our end. vii. Drawing Map & design of the property is out of scope of the				
requested. Property Title document Sub - Lease Deed Deed 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-RERA) KAsson.	p.	Documents provided for perusal		Provided	Reference No.		
Property Title document Sub - Lease Deed Deed 15/06/2016 Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-RERA)KAsson			18 SOUTHERN DOUBLE SAME AND ADDRESS OF THE SAME AND AD	NY REPORTS NAMED IN	07		
Approved Map Approved Map Sanctioned letter of building plans from NOIDA (obtained from UP-RERA)KAsson				provided.			
letter of building 24/10/2016 plans from NOIDA (obtained from UP-RERA)KAsson			Property Title document				
			Approved Map	letter of building plans from NOIDA (obtained	24/10/2016		
			Copy of TIR				


FILE NO.: VIS(2021-22)-PL-674-585-754

Page 1 of 35

EUREKA PARK, SECTOR-105, NOIDA



		Project Approval Letter		Height Clearance NOC from Airport Authority of India	Dated 18/05/2015
		Project NOC's issued from the concern authority		Enviromental clearance NOC from SEIAA	Dated 07/10/2016
			None	Copy of RERA Certificate	UPRERAPRJ5 448
			None	NOC from Pollution control Board, U.P	Dated 02/10/2019
			None	NOC from Fire Service Department, Lucknow	Dated 21/04/2015
			None	None	
			None	None	
q.	Identification of the property		Cross checked from bein the deed	oundaries of the pro	perty mentioned
		\boxtimes	Done from the name p	olate displayed on t	he property
		\boxtimes	Identified by the Prom	oter's representativ	/e
			Enquired from local re	sidents/ public	
			Identification of the pr	operty could not be	done properly
			Survey was not done		
2.	BRIEF DESCRIPTION OF THE PE	ROPERT	Y UNDER VALUATION		

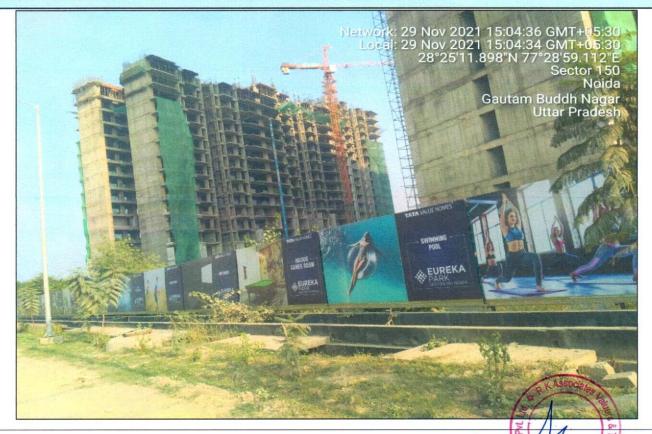

VALUATION REPORT EUREKA PARK, SECTOR-105, NOIDA



This project tie-up report is prepared for group housing project "**Eureka Park**" being developed at the aforesaid address having total land admeasuring 83970 sq.mtr. / 20.75 Acres as per the sub-lease deed provided to us by the bank.

This is a Lease hold land purchased by the virtue of a sub - lease deed executed in favour of M/s. Lotus Greens Construction Pvt. Ltd. by Noida Authority for the developing a group housing society on total land area measuring 12,00,000 sq. mtr. Further the lessee (M/s. Lotus Greens Construction Pvt. Ltd.) has sub- divided this whole project land into thirteen different plots, namely nos. SC-02/A, SC-02/A1 to SC-02/A10, SC-02/H&I and SC-02/J&K with each having different land area's and has transferred these various land parcels to twelve different Special Purpose Companies (SPC's) by execution of sub lease deeds in their favour and these land parcel are leased for 90- years starting from 14 Dec 2014.

This project Tie- Up report is prepared for the project being developed at plot No. SC-02/A1 having total land area measuring 83970.00 m2 (20.75 acres).

This land parcel has been transferred by the Lessee in favour M/s. Land Kart Builder Pvt. Ltd. (which is a 100% owned subsidiary company of M/s. Lotus Greens Construction Pvt. Ltd) by the virtue of sublease deed dated on 15 Jun 2016.

Further, the sub- lessee M/s. Land Kart Builders Pvt. Ltd. (Referred to as Promoter) has given all the development & marketing rights to M/s. Tata Value Homes Limited (Referred to as developer) by the virtue of Development Management Agreement (DMA) signed between them.

The developer of the project has proposed to develop a modern group housing project with all the basic amenities in the name of 'Eureka Park.' As per the copy of master plan, this project is comprised of 20 towers. The details of each tower are tabulated below:-

Sr. No	Tower Details	Total no of Towers	Total no of Floors	Total no of Dwelling units
1	Type A	7	S+28	980
2	Type B1	2	G/S+28	224
3	Type B2	4	G/S+28	448
4	Type C1	1	G/S+22	88
5	Type C2	6	G/S+22	528
	Т	otal		2268



EUREKA PARK, SECTOR-105, NOIDA





The developer of the project has proposed to develop the whole project in two phases i.e. phase-I & phase-II and each phase consist of 10 towers. At present, developer has launched the phase-I of the project and details of the project is tabulated below:-

S. No.	Flat Type	Number of Units	Carpet Area (sq.ft)	Super Area/ Saleable Area (sq.ft.)			
Carry Carry Color House		TYPE-A (TO)	VER-1)	(33)			
1	2BHK+2T	140	647.61	1100			
	TYPE-A (TOWER-2)						
1	2BHK+2T	140	647.61	1100			
	TYPE-A (TOWER-3)						
1	2BHK+2T	140	647.61	1100			
	TYPE-A (TOWER-4)						
1	2BHK+2T	140	647.61	1100			
		TYPE-B2 (TO	WER-8)				
1	3BHK+2T	112	783.41	1285			
		TYPE-B2 (TO	WER-9)				
1	3BHK+2T	112	783.41	1285			
		TYPE-B1 (TOV	VER-10)				
1	3BHK+2T	112	783.41	1285			
		TYPE-C1 (TOV	WER-19)				
1	ЗВНК+ЗТ	88	981.46	1575			
		TYPE-C2 (TOV	VER-20)				
1	3BHK+3T	88	981.46	1575			
		TYPE-C2 (TOV	WER-21)				
1	ЗВНК+ЗТ	88	981.46	1575			
	otal	1160					
Total Carp			884993				
Total Supe	er Area		1463560				

Developer has obtained most of the preliminary necessary statutory approvals from different government agencies to develop a Sports City comprising of 20 High Rise Towers and Open commercial

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 4 of 35





units. This is as a modern housing society being developed with all basic & urban facilities and amenities.

As per the site survey following observation has been made are as follows:

	Prog	ress report of M/s. E	ureka Park - Phase 1
Type of Tower Tower Name		Total No Of Floors	Comment
	A1	S+28	Super structure done upto 25 floor and 26th floor is in under construction phase
	A2	S+28	Super structure done upto 25 floor and 26th floor is in under construction phase
A A3	А3	S+28	Super structure done upto 24 floor and 25th floor is in under construction phase
	A4	S+28	Super structure done upto 24 floor and 25th floor is in under construction phase
	B8	G/S+28	Super structure is completed of all 28 floors
В	B9	G/S+28	Super structure is completed of all 28 floors
	B10	G/S+28	Super structure is completed of all 28 floors
	C19	G/S+22	Super structure is completed upto 18 floor and 19 floor is in under construction phase
С	C20	G/S+22	Super structure is completed upto 17 floor and 18 floor is in under construction phase
	C21	G/S+22	Super structure is completed upto 16 floor and 17 floor is in under construction phase

The location of the subject project is in a good developing Sector-150, Noida in which other group housing projects are proposed and some are under development. Subject project is located 5 Km from main Noida-Greater Noida Expressway which is 160 mtr wide.

3.	ENCLOSURES	
a.	Part B	Valuation Report as per SBI Format Annexure-II
b.	Part C	Area description of the Property
C.	Part D	Valuation Assessment of the Property
d.	Enclosure 1	Valuer's Remark - Page No. 39-40
e.	Enclosure 2	Screenshot of the price trend references of the similar related properties available on public domain - Page No. 41-44
f.	Enclosure 3	Google Map – Page No.45
g.	Enclosure 4	Photographs – Pages 03
h.	Enclosure 5	Copy of Circle Rate - Page 01
i.	Enclosure 6	Survey Summary Sheet - Pages xx
j.	Enclosure 7	Copy of relevant papers from the property documents referred in the Valuation – Pages 06

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 5 of 35

EUREKA PARK, SECTOR-105, NOIDA



PART B SBI FORMAT OF VALUATION REPORT

Name & Address of Branch	State Bank of India, HLST Branch, Noida
Name of Promoter	M/s. Land Kart Builders Pvt. Ltd.

S.NO.	CONTENTS	DESCRIPTION			
1.	INTRODUCTION				
a.	Name of Property Owner	M/s. Land Kart Builders Pvt. Ltd.			
	Address & Phone Number of the	Registered Office: 7th Floor, Tower-B, Plot No.08, Sector-127,			
	Owner	Noida - 201301			
b.	Purpose of the Valuation	Project Tie-up Report			
C.	Date of Inspection of the Property	29 November 2021			
d.	Date of Valuation Report	1 December 2021			
e.	Name of the Developer of the	M/s. Land Kart Builders Pvt. Ltd.			
	Property				
	Type of Developer	Private developer promoted			

	PHYSICAL CHARACTERISTICS	OF THE PROPERTY		
a.	Location attribute of the property			
i.	Nearby Landmark	Near- ATS Pristine Golf Villas		
ii.	Postal Address of the Property	Plot No. SC-02/A1, Sports City, Pradesh	Sector-150, Noida, Utta	
iii.	Area of the Plot/ Land	83970 sq.mtr. (20.75 Acres)		
		Also please refer to Part-B Area de	escription of the property.A	
		area measurements are on approx	rimate basis. Verification of	
		the area measurement of the prop		
		sample random checking and	not based on full scale	
		measurement.		
iv.	Type of Land	Solid/ On road level		
٧.	Independent access/ approach to	Clear independent access is available		
	the property			
vi.	Google Map Location of the Property	Enclosed with the Report		
	with a neighborhood layout map	Coordinates or URL: 28°25'11.6"N 7	77°29'01.1"E	
vii.	Details of the roads abutting the prope	erty		
	Main Road Name & Width	Noida- Greater Noida Expressway	160 mtr wide road	
	2. Front Road Name & width	Private Road	18 mtr wide road	
	Type of Approach Road	Bituminous Road		
	Distance from the Main Road	3.5 km from Noida-Greater Express	way	
viii.	Description of adjoining property	Residential Area		
ix.	Plot No./ Survey No.	Plot No. REP-1		
Χ.	Zone/ Sector	Residential	Sector-150	
xi.	Sub registrar	Noida		
xii.	District	Gautam Buddha Nagar, Uttar Pradesh		
xiii.	Any other aspect	Valuation is done for the property id owner representative. Responsibilit property to the Valuer/ its authorized	ty of identifying the correct	

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 6 of 35





				end we with refor per reque proper case same then proper docurred to the control of the control	owner for which we have just cross we ference to the documents as per our sted from them. It is carried out is the property mention which security no blease inform the Value on which security no blease inform the value of the property mention of the property because inform the property because inform the property because inform the property because inform the property because in the property because it is a property becaus	erified the uments whi standard of Method by also mentioned in the nortgage had aluer office erty is only site if more of this at the period of this at the uncontrol of the period of this at the uncontrol of the period of the uncontrol of the u	identification checklist of which identified in the Valuation as been or immediate limited to be the vith revenssignmen	could provide to us of the documents entification of the e report clearly. In a report is not the has to be created sely. It cross verification in the provided ue officers for site
					Cross checked from mentioned in the		ries of the	property
					Done from the na	me plate di	splayed o	n the property
	1.	Identification of the	property					
				☐ Enquired from local residents/ public				
					Identification of th	e property	could not	be done properly
					Survey was not d	one		
	2.			Yes				
		demarcatedby perr						
		temporary boundar	•					
	3.				is an independent	single bour	ided prop	erty
		colluded with any o property	tner	NA				
	4.				Metro City		Urb	an developing
	5.				Good			nin Residential
			-				Dev	veloped Zone
	6.	Property location		Ordin	nary location within	Co	ner	None
		classification		120000000000000000000000000000000000000	the locality			-
		Property Facing		_ 201100-0-0-0-0-0	Facing			
b.		ed Built-up area des		Please refer to the attached sheet below.				
	(Plintn	/ Carpet/ Saleable A	rea)	area the ai samp	olease refer to Part measurements are rea measurement d le random check urement.	on approx of the prop	imate ba erty is do	sis. Verification of ne only based on
c.		daries schedule of	the Proper					
i.	Are Bo	oundaries matched			oundaries are not m			
ii.		Directions	As	•	ase Deed	A	Charles and the second	nd at Site
		North			A		Ent	Dand
		South			A		River I	sand
		East			A		Fideco	green August
		West		IN	A		Ros	101

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 7 of 35





3.	TOWN PLANNING/ ZONING PARAMETE	RS				
a.	Master Plan provisions related to property in	Residential				
	terms of Land use					
	i. Any conversion of land use done	NA				
	ii. Current activity done in the property	Construction of Residentia building	l Apartment in multistoried			
	iii. Is property usage as per applicable zoning	Yes				
	iv. Any notification on change of zoning regulation	No				
	v. Street Notification	Residential				
b.	Provision of Building by-laws as applicable	PERMITTED	CONSUMED			
	i. FAR/ FSI	Please refer to area chart description	Please refer to area chart description			
	ii. Ground coverage	do	do			
	iii. Number of floors	do	do			
	iv. Height restrictions	dodo-				
	v. Front/ Back/ Side Setback	do	do			
C.	Status of Completion/ Occupational	Not applicable since	Not applicable since			
	certificate	subject project is under construction	subject project is under construction			
d.	Comment on unauthorized construction if any	Not applicable since s construction	subject project is unde			
e.	Comment on Transferability of	As per regulation of	Greater Noida Industria			
	developmentalrights	Development Authority (NC	DIDA)			
f.	i. Planning Area/ Zone	NOIDA Master Plan				
	ii. Master Plan currently in force	NOIDA Master Plan - 2031				
	iii. Municipal limits	NOIDA				
g.	Developmental controls/ Authority	NOIDA				
h.	Zoning regulations	Residential				
i.	Comment on the surrounding land uses &	Other Group Housing Socit	ies is under construction			
	adjoining properties in terms of uses					
j.	Comment of Demolition proceedings if any	Not applicable, since project	ct is under construction			
k.	Comment on Compounding/ Regularization proceedings	Not Applicable since constron	uction of the project is going			
I.	Any other aspect					
	i. Any information on encroachment	No				
	ii. Is the area part of unauthorized area/ colony	No (As per general informa	tion available)			

4.	DOCUMENT DETAILS AND LEGAL ASPECTS OF THE PROPERTY						
a.	Ownership documents provided	Sub Lease Deed	None	None			
b.	Names of the Legal Owner/s	M/s. Land Kart Builde	M/s. Land Kart Builders Pvt. Ltd.				
C.	Constitution of the Property	Lease hold, have to t	ake NOC in order	to transfer			
d.	Agreement of easement if any	Not required	(2) A	Colif of the Colif			





Page 9 of 35

e.	Notice of acquisition if any and area under acquisition	No, as per general information available in the public domain
f.	Notification of road widening if any and area under acquisition	No, as per general information available in the public domain
g.	Heritage restrictions, if any	No
h.	Comment on Transferability of the property ownership	Lease hold, have to take NOC in order to transfer
i.	Comment on existing mortgages/ charges/ encumbrances on the property, if any	No Information available NA to us. Bank to obtain details from the Developer
j.	Comment on whether the owners of the property have issued any guarantee(personal or corporate) as the case may be	No Information available to us. Bank to obtain details from the Developer.
k.	Building plan sanction:	
	 Authority approving the plan 	NOIDA
	ii. Name of the office of the Authority	NOIDA
	iii. Any violation from the approved Building Plan	Not applicable since subject project is unde construction
I.	Whether Property is Agricultural Land if yes, any conversion is contemplated	No, not an agricultural property
m.	Whether the property SARFAESI complaint	Yes
n.	i. Information regarding municipal taxes	Tax name
	(property tax, water tax, electricity bill)	Receipt number
		Receipt in the name of
		Tax amount
	ii. Observation on Dispute or Dues if any in payment of bills/ taxes	Not known to us
	Is property tax been paid for this property	Not available. Please confirm from the owner.
	iii. Property or Tax Id No.	Not provided
Ο.	Whether entire piece of land on which the unit is set up / property is situated has been mortgaged or to be mortgaged	No information provided to us
p.	Qualification in TIR/Mitigation suggested if any	Copy of TIR not given to us, hence cannot comment
q.	Any other aspect	
	 Since how long owners owing the Property 	05 Years as per lease deed
	ii. Year of Acquisition/ Purchase	Year 2016 as per lease deed
	iii. Property presently occupied/ possessed by	Developer
	iv. Title verification	To be done by the competent Advocate
	v. Details of leases if any	Yes, Sub-lease was executed in favor of the sub lessee on 15/06/2016





5.	ECONOMIC ASPECTS OF THE PROPER	ΓY
a.	Reasonable letting value/ Expected market monthly rental	NA
b.	Is property presently on rent	No
	i. Number of tenants	NA
	ii. Since how long lease is in place	NA
	iii. Status of tenancy right	NA
	iv. Amount of monthly rent received	NA
C.	Taxes and other outgoing	Owner/Developer company to provide this information
d.	Property Insurance details	Owner/Developer company to provide this information
e.	Monthly maintenance charges payable	Owner/Developer company to provide this information
f.	Security charges, etc.	Owner/Developer company to provide this information
g.	Any other aspect	NA
6.	SOCIO - CULTURAL ASPECTS OF THE F	PROPERTY
a.	Descriptive account of the location of the property in terms of Social structure of the area in terms of population, social stratification, regional origin, age groups, economic levels, location of slums/squatter settlements nearby, etc.	
b.	Whether property belongs to social infrastructure like hospital, school, old age homes etc.	No

7.	FUNCTIONAL AND UT	ILITARIAN SE	ERVICES, FACILITIES & AMENITIES
a.	Description of the function	ality & utility of t	the property in terms of :
	i. Space allocation		Yes (Proposed)
	ii. Storage spaces		Yes (Proposed)
	iii. Utility of spaces prov building	ided within the	Yes (Proposed)
	iv. Car parking facilities		Yes (Proposed)
	v. Balconies		Yes (Proposed)
b.	Any other aspect		
	i. Drainage arrangeme	nts	Yes (Proposed)
	ii. Water Treatment Pla	nt	Yes (Proposed)
	iii. Power Supply	Permanent	Yes, for construction & office purpose at present
	arrangements	Auxiliary	DG will be installed
	iv. HVAC system	-1	No
	v. Security provisions		Yes/ Private security guards
	vi. Lift/ Elevators		Yes (Proposed)
	vii. Compound wall/ Mai	n Gate	Yes
	viii. Whether gated socie	ty	Yes
	ix. Internal developmen		Labon IV
	Garden/ Park/ W	ater bodies	Internal roads Pavements Boundary Wal
	Land scraping		

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 10 of 35





Yes (Proposed) Yes (Proposed)	Yes (Proposed)	Yes (Proposed)	Yes/ 6' high 9" brick wall
-------------------------------	----------------	----------------	-------------------------------

8.	INFRASTRU	CTURE AVAII	LABILITY					
a.	Description of	Aqua Infrastruc	ture availability	in terms of	:			
	i. Water Supply			Yes (P	rop	osed)		
	ii. Sewerag	ge/ sanitation sy	stem	Under	grou	und (Proposed)		
	iii. Storm w	ater drainage		Yes (P	rop	osed)		
b.	Description of	other Physical I	nfrastructure fa	acilities in te	erms	of:		
	i. Solid waste management		Yes, to	Yes, to be done by Authority (Proposed)				
	ii. Electricity		Yes, fo	Yes, for construction & office purpose at present				
	iii. Road and Public Transport connectivity			y Yes	Yes			
	iv. Availability of other public utilities nearb			by Transp		Market, Hospi	tal etc. are ava	ilable in close
C.	Proximity & av	ailability of civic	amenities & s	ocial infrast	ruct	ure		
	School	Hospital	Market	Bus Sto	р	Railway Station	Metro	Airport
	6 km	7 km	3.5 km	6 km		36 km	6 km	55 km
	Availability of r spaces etc.)	ecreation facilit	ies (parks, open	1000 0000 0000		loping area ar developed nea		facilities are

9.	MARKETABILITY ASPECTS OF THE PRO	OPERTY:		
a.	Marketability of the property in terms of			
	i. Location attribute of the subject property	Good		
	ii. Scarcity	Similar kind of properties are easily available on demand.		
	 iii. Market condition related to demand and supply of the kind of the subject property in the area 	Good demand of such properties in the market.		
	iv. Comparable Sale Prices in the locality	Please refer to Part C: Valuation Assessment of the Property.		
b.	Any other aspect which has relevance on the value or marketability of the property	No		
	Any New Development in surrounding area	Yes		
	ii. Any negativity/ defect/ disadvantages in the property/ location	No Construction of many other group housing societies is in progress.		

10.	ENGINEERING AND TECHNOLOGY ASPECTS OF THE PROPERTY:	
a.	Type of construction & design	RCC framed structure (under construction)
b.	Method of construction	Construction done using professional contractor workmanship based on architect plan (under cosntruction)
C.	Specifications	legy legy

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 11 of 35





	i. Class of construction	Under construction	
	ii. Appearance/ Condition of structures	Internal -Under construction	
		External -Under construction	ı
	iii. Roof	Floors/ Towers	Type of Roof
		20 Towers, Proposed to	RCC (Proposed)
		be B+S+22 to B+S+28	8
		Story as per the master	
		site plan	
	iv. Floor height	Approx. 10 feet (Proposed)	
	v. Type of flooring	Ceramic Tiles, Vitrified tiles	(Proposed)
	vi. Doors/ Windows	Wooden frame & panel door	rs, Wooden frame & panel
		doors (Proposed)	
	vii. Interior Finishing	Neatly plastered and putty of	
	viii. Exterior Finishing	Simple plastered walls (Proj	•
	 ix. Interior decoration/ Special architectural or decorative feature 	Good looking interiors. decoration. (Proposed)	Medium use of interior
	x. Class of electrical fittings	Internal/ High quality fittings	used (Proposed)
	xi. Class of sanitary & water supply fittings	Internal/ High quality fittings	used (Proposed)
d.	Maintenance issues	Not Applicable since constru	uction work is in progress
e.	Age of building/ Year of construction	Under Construction	Under Construction
f.	Total life of the structure/ Remaining life expected	Approx. 60-65 years (After Completion)	Approx. 60-65 years (After Completion)
g.	Extent of deterioration in the structure	Not Applicable as constructi	ion work is in progress
h.	Structural safety	Not Applicable since construin progress	
i.	Protection against natural disasters viz. earthquakes etc.	Proposed to be designed for Zone IV	or seismic consideration for
j.	Visible damage in the building if any	Not Applicable since construin progress	uction work of the project is
k.	System of air conditioning	Under construction property	
I.	Provision of firefighting	Yes (Proposed)	
m.	Status of Building Plans/ Maps	Building plans are appro-	ved by the developmen
	i. Is Building as per approved Map	Cannot comment since cor progress	nstruction of the project in
	ii. Details of alterations/ deviations/ illegal	☐Permissible Alterations	Not Applicable
	construction/ encroachment noticed in the structure from the original approved plan	□Not permitted alteration	Not Applicable
	iii. Is this being regularized	NA	
	ENVIRONMENTAL FACTORS:	1,	

11.	ENVIRONMENTAL FACTORS:	
a.	Use of environment friendly building materials like fly ash brick, other Green building techniques if any	THE STATE OF THE S
b.	Provision of rainwater harvesting	Yes (Proposed)
C.	Use of solar heating and lighting systems, etc.	No information available to us





d.	Presence of environmental pollution in the	Yes, normal vehicle & Construction pollution are
	vicinity of the property in terms of industries,	present in atmosphere
	heavy traffic, etc. if any	

12.	ARCHITECTURAL AND AESTHETIC QUALITY OF THE PROPERTY:		
a.	Descriptive account on whether the building is modern, old fashioned, etc., plain looking or with decorative elements, heritage value if applicable, presence of landscape elements, etc.		

13.	PROJECT DETAILS:	
a.	Name of the Developer	M/s. Land Kart Builders Pvt. Ltd.
		(100% Owned Subsidiary Company of M/s. Lotus
		Greens Constructions Pvt. Ltd.)
b.	Name of the Architect	AR. Smita Jain
		CA No. 2014/62840
C.	Developer market reputation	Established Builder with years long experience in
		market and have successfully delivered multiple
		Projects.
d.	Proposed completion date of the Project	As per RERA- 31-03-2023 (For Phase-I)
e.	Progress of the Project	Refer to the sheet attached on page no.25 & 26
f.	Other Salient Features of the Project	
	(Proposed)	Apartments, Affordable housing, Club,
		Swimming Pool, ⊠ Play Area, ⊠ Walking Trails, □
		Gymnasium, ⊠ Convenient Shopping, ⊠ Parks, □
		Multiple Parks, ⊠ Kids Play Area`

14.	VALUATION:			
a.	Methodology of Valuation - Procedures	Please refer to Sub-Point 'n' of Point 1 of Part D:		
	adopted for arriving at the Valuation	Valuation Assessment Factors of the report.		
b.	Prevailing Market Rate/ Price trend of the	Please refer to the Sub-Point 'o' of Point 1of Part D:		
	Property in the locality/ city from property	Valuation Assessment Factors of the report and the		
	search sites	screenshot annexure in the report.		
C.	Guideline Rate obtained from Registrar's	Please refer to Part D: Valuation Assessment		
	office/ State Govt. gazette/ Income Tax	Factors of the report and the screenshot annexure in		
	Notification	the report.		
d.	Summary of Valuation	For detailed Valuation calculation please refer to Point		
		1, 2, 3 & 4 of the Part D: Valuation Assessment		
		Factors of the report.		
	i. Guideline Value	Rs.487,02,60,000/-		
	1. Land	Rs.487,02,60,000/-		
	2. Building	NA		
	ii. Prospective Fair Market Value	Rs.8,26,68,00,000/-		
	iii. Realizable Value	Rs.702,67,80,000/-		
	iv. Distress Value*	Rs.620,01,00,000/-		

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 13 of 35





	purpose	of structure for Insurance	NA
e.	See Somewhat and Commence of the Commence of t	n for more than 20% difference Circle Rate	Circle rates are determined by the District administration as per their own theoretical internal policy and Market rates are adopted based on current practical market dynamics which is explained clearly in Valuation assessment factors.
		last two transactions in the ea to be provided, if available	No authentic last two transactions details could be known. However prospective transaction details as per information available on public domain and gathered during site survey is mentioned in <i>Point 'o'</i> of <i>Part D:</i> Valuation Assessment Factors of the report and the screenshots of the references are annexed in the reportfor reference.
15.	Declaration (Also see Enclosure: 1 Valuer's Remarks)	ii. The analysis and conclusion and the information came Assumptions Remarks & Lesection of the Report. iii. If firm have read the Hand Valuation by Banks and HF provisions of the same and and this report is in conformation Handbook. iv. No employee or member of v. Our authorized surveyor by on 29 November 2021 in the vi. I am a registered Valuer under the same and the same an	strue and correct to the best of my knowledge and belief. Ons are limited by the reported assumptions, limiting conditions to knowledge during the course of the work. Please see the Limiting conditions described in Part D: Valuation assessment dbook on Policy, Standards and Procedures for Real Estate Fls in India, 2011 issued by IBA and NHB, fully understood the diffollowed the provisions of the same to the best of my ability formity to the Standards of Reporting enshrined in the above of R.K. Associates has any direct/ indirect interest in the property, and any presence of the developer's representative. The presence of the developer's representative and the subject property are presence of the developer's representative. The presence of the developer's representative and the subject property are presence of the developer's representative. The presence of the developer's representative and the subject property are presence of the developer's representative. The presence of the developer's representative and the subject property are presence of the developer's representative. The presence of the developer's representative and the subject property are presented to the Bank. The presence of the developer's representative and the subject property are presented to the Bank.

16.	VALUATION COMPANY DETA	ILS:	
a.	Name & Address of Valuer company	Wealth Tax Registration No.	Signature of the authorized person
b.	M/s R.K. Associates Valuers & Techno Engineering Consultants Pvt. Ltd. G-183, Preet Vihar, Delhi- 110092	2303/ 1988	Theyat
C.	Total Number of Pages in the Report with enclosures	49	
d.	Engineering Team worked on the report	SURVEYED BY: AE Harshit M	layank I .
		PREPARED BY: Er. Ritesh kun	nar Singh
		REVIEWED BY: HOD Valuation	os Values Values

BANK OF INDIA, HLST, NOIDA.

ix. This valuation work is carried out by our Engineering team on the request from STATE

FILE NO.: VIS(2021-22)-PL-674-585-754

Page **14** of **35**





17.	ENCLOSED DOCUMENTS:		
a.	Layout plan sketch of the area in which the property is located with latitude and longitude	Google Map enclosed with coordinates	
b.	Building Plan	Enclosed with the report	
C.	Floor Plan	Enclosed with the report	
d.	Photograph of the property (including geo- stamping with date) and owner (in case of housing loans, if borrower is available) including a "Selfie" of the Valuer at the site	Enclosed with the report	
e.	Certified copy of the approved / sanctioned plan wherever applicable from the concerned office	Enclosed with the report	
f.	Google Map location of the property	Enclosed with the Report	
g.	Price trend of the property in the locality/city from property search sites viz Magickbricks.com, 99Acres.com, Makan.com etc	Enclosed with the Report	
h.	Any other relevant documents/extracts (All enclosures & annexures to remain integral part & parcel of the main report)	 i. Part C: Area Description of the Property ii. Part D: Valuation Assessment of the Property iii. Assumption, Remarks& Limiting conditions iv. Valuer's Remark - Page No.39-40 v. Google Map - Page No.45 vi. Photographs - Pages 03 vii. Copy of Circle Rate - Pages 01 viii. Survey Summary Sheet - Pages xx ix. Copy of relevant papers from the property documents referred in the Valuation - Pages 06 	



VALUATION REPORT EUREKA PARK, SECTOR-105, NOIDA



Page **16** of **35**

PART C AREA DESCRIPTION OF THE PROPERTY

1.	Land Parcel Area			83970 m ² (20.75 Acres) (for whole Project)		
2.	Land Parcel Area		48422 m ² (for Phase 1)			
^	Ground Coverage	Proposed Permissible		10679.615 m ² (for whole Project)		
3.	Area					
		UNDER	AR	Proposed	Present Status	
			Residential	203605.522 m ²		
			Commercial	435.080 m ²		
			Sports Centre	1523.446 m ²		
			Proposed	205564.048 m ²		
		TOTAL		No such information		
		TOTAL	Permissible	mentioned in the		
				provided documents		
		15 % Facility	Proposed	33699.621 m ²	Under Construction	
		FAR		No such information		
		FAR	Permissible	mentioned in the		
1.	Covered Area			provided documents		
		Total	Proposed	239263.669 m ²		
			Froposeu	(2575410.20 ft. ²)		
				No such information		
			Permissible	mentioned in the		
				provided documents		
		UNDER NON FAR				
		Stilt		4385.686 m ²		
			Basement Area	65317.126 m ²		
			Proposed	69702.812 m ²	Under Construction	
		TOTAL		(750274.098 ft. ²)		
			Permissible	NA		
5.	Open/ Green Area		Proposed	39077.624 m ²		
	open ereen nea	Min	imum Required	36645.193 m ²		
_	_		Proposed	10206 Persons (for whole Project)		
6.	Density		Permissible	No such information mentioned in the provided		
				documents		
7.	Plinth/ Built-up Area (As per IS 3861-1966)			308966.481 m ² (FAR + N	ION FAR)	
8.	Carpet Area			884993 sq.ft (for Phase-	1)	
9.	Net Floor Area			NA	*	
	COLONDO DI SI SIMBORIO DI GROPINESI			1463560 sq.ft (for Phase	e-I)	
	Super Area					
10. 11.				NA	,	





		To	otal Blocks/ Floors/ Fl	ats		
1.	Approved as po		Actually provide (as per inventory li	Current Status		
	Phase-I & II		Phase-I			
	Tower Type - A (7	Nos): S+28	Tower Type – A (Tower No. 1 to 4):			
	Floors - 980 DUs		G/S+28 Floors - 560 D	Us		
	Tower Type - B1 (2 Nos): G/S+28	Tower Type - B1 (Tow	ver No. 10):		
	Floors - 224 DUs		G/S+28 Floors - 112 D	Us		
	Tower Type - B2 (4 Nos): G/S+28	Tower Type - B2 (Tow	rer No. 8 & 9):	Refer to the Table 1	
	Floors - 448 DUs		G/S+28 Floors - 224 D	Us	attached below	
	Tower Type – C1 (1 Nos): G/S+22	Tower Type – C1 (Tow	attached below		
	Floors - 88 DUs		G/S+22 Floors - 88 DU			
	Tower Type – C2 (6 Nos): G/S+22	Tower Type – C2 (Tow	ver No. 20 & 21):		
	Floors - 528 DUs		G/S+22 Floors – 176 DUs			
	Total DUs : 2268 D	U	Total DUs: 1160 DU (I	n Phase-I)		
	Total no. of Flats/	Main Units	1	160 DUs (in Phase	e-I)	
	Units	Service Units		NA		
	Type of Flats		Refer to the sheet attac	hed below		
			Required	Required 2584 ECS		
2.			Basement Car	2014 ECS		
	Number of Car Parl	king available	Parking			
	Number of Car Pan	king available	Stilt Car Parking	80 ECS		
			Open Car Parking	501 ECS		
			Total	2596 ECS		

Table 1:

Progress report of M/s. Eureka Park - Phase 1				
Type of Tower	Tower Name Total No Of Floors		Comment	
	A1	S+28	Super structure done upto 25 floor and 26th floor is in under construction phase	
А	A2	S+28	Super structure done upto 25 floor and 26th floor is in under construction phase	
	АЗ	S+28	Super structure done upto 24 floor and 25th floor is in under construction phase	
	A4	S+28	Super structure done upto 24 floor and 25th floor is in under construction phase	
	B8	G/S+28	Super structure is completed of all 28 floors	
В	В9	G/S+28	Super structure is completed of all 28 floors	
	B10	G/S+28	Super structure is completed of all 28 floors	
	C19	G/S+22	Super structure is completed upto 18 floor and 19 floor is in under construction phase	
С	C20	G/S+22	Super structure is completed upto 17 floor and 18 floor is in under construction phase	
	C21	G/S+22	Super structure is completed up to 16 floor and 17 floor is in under construction phase	

EUREKA PARK, SECTOR-105, NOIDA



PARTD

PROJECT APPROVAL DETAILS

S.No.	REQUIRED APPROVALS	REFERENCE NO./ DATE	STATUS (Approved/ Applied For/ Pending)
1.	Approved Building Plan	Letter No.IV-1500/934 (Dated:24/10/2016 valid for 5 years)	Approved
2.	Building Plan Approval Letter		
3.	NOC from Airport Authority of India	No. AAI/R.Hq/NR/ATM/NOC/2015/164/2642-45 (Dated:18/05/2015 valid for 5 years)	Approved
4.	Environmental clearance Ref No. 276/Parya/SEAC/2901/2016 NOC from SEIAA (Dated:07/10/2016 valid for 5 years)		Approved
5.	NOC from Pollution Control Board Ref No. 60668/UPPCB/Noida(UPPCBRO)/CTE/NOIDA/2019 (Dated:02/10/2019 valid for 5 years)		Approved
6.	Provisional NOC from Fire Letter No.Bha-16/J.D/Fa.Sa/Lucknow-15/165 Authority (Dated: 21/04/2015 valid for 5 years)		Approved
7.	Certificate of assurance for Water Supply		
8.	Certificate of assurance for Electricity Supply		
9.	NOC from Forest Department		
10.	NOC for ground water extraction		
11.	NOC from Sewerage and		
12.	RERA Registration Certificate	RA Registration RERA No. UPRERAPRJ5448	
13.	Structural Stability Certificate		

OBSERVATIONS: - Project meets preliminary necessary compliance statutory approvals. NOC from Airport Authority of India has expired and the bank is advised to check the extension of the same from the developer.

FILE NO.: VIS(2021-22)-PL-674-585-754 Page 18 of 35

EUREKA PARK, SECTOR-105, NOIDA



PARTE

VALUATION ASSESSMENT OF THE PROPERTY

1.		ASSESSMENT FACTORS					
a.	Valuation Type	Group Housing Society Value Group Housing Society Value					
b.	Scope of the Valuation	To assess Project Establishment Rep			placement Value		
C.	Property Use factor	Curre			Highest &Best Use		
		Construction of Group Housing		Group Housi	ng Society		
		Soc	The state of the s			-	
d.	Legality Aspect Factor (Refer sub clause I & j of Point 7)	Positive as per documents produced			d to us		
e.	Land Physical factors	Shape	Size		Level	Frontage to depth ratio	
		Irregular	La	irge	On Road Level	Normal frontage	
f.	Property location category factor	City Categorization		ality orization	Property location classification	Floor Level	
		Metro City	Go	bod	On wide	Not	
		2000			approach road	Applicable	
			Proper	ty within	NA		
			deve	loped	NA		
		residential zon		tial zone			
		Property Facing	West Fa	acing			
g.	Any New Development	Other developmen	nent Development of other group housing				
	in surrounding area	77		projects	is going on.		
h.	Any specific advantage/ drawback in the property	No					
i.	Overall property usability Factor	Normal					
j.	Comment on Property Salability Outlook	Easily sellable					
k.	Comment on Demand & Supply in the Market	Good demand of	such prop	perties in	the market		
l.	Sale transaction method assumed	Free market transaction at arm's length wherein the parties, after full market survey each acted knowledgeably, prudently and without any					
m.	Best Sale procedure to realize maximum Value	compulsion. Free market transaction at arm's length wherein the parties, after full market survey each acted knowledgeably, prudently and without any compulsion.					
n.	Methodology/ Basis of	Govt. Guideline	Value: C	ircle Rate	s of NOIDA-2019)	
	Valuation	Market Value: L	and Valu	ie is calc	ulated on the ba	sis of 'Market	
		Comparable Sale	es appro	ach' and	Building constru	ction value is	
		calculated on the	basis of '	Depreciat	ed Replacement (Cost approach'	

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 19 of 35





0.	Refer	ences on pr	been n seller c and va seeing know t made.	owing comparable market sales, significant local enquiries has nade from our side representing ourselves as both buyer and of the similar property and thereafter based on this information rious factors of the property, a rate has been judiciously taken the market scenario. Kindly please refer below section to the name & contact numbers from whom enquiries have been at Rate/Price trend of the property and Details of the sources	
W. 60				thered (from property search sites & local information)	
	i.	Name:		NA	
	7,000	Contact No.:			
		Nature of reference:			
		Size of the Property:			
		Location:			
		Rates/ Price i	- Contract the Land Contract to Contract t		
		Any other details/ Discussion held:			
	ii.	Name:		NA	
		Contact No.:			
		Nature of reference:			
		Size of the Pr	operty:		
		Location:			
		Rates/ Price			
		held:	ails/ Discussion		
	Adopt	ed Rates		he specific purpose to develop group housing society. And Group Housing	
	Justifi	cation	The state of the s	ostly directly auctioned by the authority. No other sale purchase information	
				be known from the market survey because of very few transactions taking place in	
				resent for such type of land. This project land is situated on 18 mtr. wide	
				considering all these factors and premium for the development of the land,	
	mtr.		mtr. to Rs.35,00	tes for these type of specific land should be between Rs.30,000/- per sq. 00/- per sq.mtr. We have taken Rs.32,000/- per sq. mtr. as the land rate nion seems to be reasonable.	
			willen in our opir	IIOH SEEHIS LO DE FERSONADIE.	

2.	VALUATION OF LAND						
	Particulars	Govt. Circle/ Guideline Value	Prospective Fair Market Value				
a.	Prevailing Market Rate range	Rs.58,000/- per m ²	Rs.30,000/- to Rs.35,000/- per m ²				
b.	Rate adopted considering all characteristics of the property	Rs.58,000/- per m ²	Rs.32,000/- per m²				
C.	Total Development Land Area considered (documents vs site survey whichever is less)	83970 m² (20.75 Acres)	83970 m² (20.75 Acres)				
d.	Total Permissible FAR	83970 m ² x Rs.58,000/-per m ²	83970 m ² x Rs.32,000/- per m ²				
e.	Total Value of land (A)	Rs.487,02,60,000/-	Rs.268,70,40,000/-				

3.		VALUATION OF BUILDING CONSTRUCTION	
	Particulars	Expected Building Construction Value	1





			FAR	NON FAR			
		Rate range	Rs.1,200/- to 1,700/- per ft.2	Rs.1,000/- to 1,500/- per ft.2			
	Structure	Rate adopted	Rs.1,550/- per ft.2	Rs.1,250/- per ft. ²			
		Covered Area	239263.669 m ² / 2575410.20 ft. ²	69702.812 m ² / 750274.098 ft. ²			
	Construction Value	Valuation Calculation	Rs.1,550/- per ft. ² X 2575410.20 ft. ²	Rs.1,250/-per ft. ² X 750274.098 ft. ²			
		Total Value	Rs.399,18,85,810/-	Rs.93,78,42,623/-			
а.	Depreciation percentage		NA				
	(assuming salvage value % per year)		(Above replacement rate is calculated after deducting the prescribed depreciation)				
b.	Age Factor		Under construction				
C.	Structure Type/	Condition	RCC framed structure (Proposed)				
d.	Construction De Replacement Va		Rs.492,97,28,433/-				

4.	VALUATION OF AL	DDITIONAL BUILDING & SITE	AESTHETIC WORKS
	Particulars	Specifications	Depreciated Replacement Value
a.	Add extra for Architectural aesthetic developments, improvements (add lump sum cost)		
b.	Add extra for fittings & fixtures (doors, windows, wood work, cupboards, modular kitchen, electrical/ sanitary fittings)		Rs.25,00,00,000/-
C.	Add extra for services (Water, Electricity, Sewerage, Main gate, Boundary, Lift, Auxiliary power, AC, HVAC, Firefighting etc.)		Rs.25,00,00,000/-
d.	Add extra for internal & external development (Internal roads, Landscaping, Pavements, Street lights, Green area development, External area landscaping, Land development, Approach road, etc.)		Rs.15,00,00,000/-
e.	Depreciated Replacement Value (C)	NA	Rs.65,00,00,000/-

5.	MARKET/	SALABLE VALUE OF THE FLATS
a.	Total No. of Flats (Launched at present)	1160 DUs (In Phase-I)
b.	Total No. Villas (Launched at present)	NA
C.	Total No. of Studio apartments (Launched at present)	NA
d.	Total Proposed Salable Area	1463560 sq.ft (for Phase-I)
e.	Launch Price = (approx.) (including PLC + Car Parking + EDC + IDC + Club & other charges)	Rs.4,800 to Rs.5,500 per sq.ft on super area

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 21 of 35





	Government Circle rate	Rs.40,000/- per sq.mtr. (Rs.3716/-per sq.ft.) on super area
	Present Market Rate (including PLC + Car Parking + EDC + IDC + Club & other charges)	Rs.6,000 to Rs.6,500 per sq.ft on super area
f.	Remark	The subject project is significantly new in the market and as per the information gathered on public domain there is no proper secondary market developed yet for this project and only the booking rate quote by the developer is available in the market. The booking value of the proposed Flats varies from floor to floor, size and location of the flat & villa i.e. park facing, corner etc. This will be a modern society and the builder proposes to construct modern flats as per the information available on public domains. As per information gathered from the public domain & market participants of that area, and it is found that booking rate for these flats is between Rs.6,000/- to Rs.6,500/- per sq.ft. on super area.


S. No	Flat Type	Number of Units	Number of Units Carpet area (In sq ft) (In sq ft)		Average Price per unit (INR)	Total (INR)	
		TYI	PE A (TOWER 1	L)			
1	2BHK+2T	140	647.61	1100	68,20,000	95,48,00,000	
		TYF	PE A (TOWER 2	2)			
2	2BHK+2T	140	647.61	1100	68,20,000	95,48,00,000	
		TYF	PEA (TOWER 3	3)			
3	2BHK+2T	140	647.61	1100	68,20,000	95,48,00,000	
		TYF	PE A (TOWER	1)			
4	2BHK+2T	140	647.61	1100	68,20,000	95,48,00,000	
		TYP	E B2 (TOWER	8)			
5	3BHK+2T	112	783.41	1285	79,67,000	89,23,04,000	
		TYP	E B2 (TOWER	9)			
6	3BHK+2T	112	783.41	1285	79,67,000	89,23,04,000	
		TYPI	B1 (TOWER 1	.0)			
7	3BHK+2T	112	783.41	1285	79,67,000	89,23,04,000	
		TYPI	EC1 (TOWER 1	.9)			
8	3BHK+3T	88	981.46	1575	97,65,000	85,93,20,000	
		TYPE	E C2 (TOWER 2	(0)			
9	3BHK+3T	88	981.46	1575	97,65,000	85,93,20,000	
		TYPE	C2 (TOWER 2	1)			
10	3BHK+3T	88	981.46	1575	97,65,000	85,93,20,000	
Total		1160	7885.05	12980		9,07,40,72,000	
Total carp	et area (In sq ft)	884993			-		
Total sup	er area (In sq ft)	1463560					
Remarks:							
l. The ma	rket of flats varie	es from Rs.6,000/- to	Rs.6,500/- pe	r sq ft on sup	per area. So we	have	
		ce which is Rs. 6, 200,					

Note: Normally, apart from the Basic Sale Price (BSP) mentioned in the Agreement to Sale, a one-time cost of additional amenities & other costs related to the property which are permanent in nature and add up to the realizable value of security/property (viz. Township Corpus Fund, One Time Maintenance fund/deposit/corpus, Development Charges, Premium for insurance/of Mortgaged Property, Electrical Fittings, One Time Generator Charges, Club House Membership



EUREKA PARK, SECTOR-105, NOIDA

Charges, Electricity/Water/Sewerage Board one time charges/deposits, cost of rooftop Solar Photo Voltiac System) are charged. Now GST will be added as part of Project Cost for assessing the loan amount in lieu of VAT, Service Tax, etc. However, Stamp Duty, Registration Charges and other documentation Charges, which are not realizable in nature will not be included in the value of the property/agreement to sale for arriving at the loan eligibility.







6.		CONSOLIDATED VALUE				
	Particulars	Govt. Circle/ Guideline Value	Prospective Fair Market Value			
a.	Land (A)	Rs.487,02,60,000/-	Rs.268,70,40,000/-			
b.	Structure Construction Value(B)	NA	Rs.492,97,28,433/-			
C.	Additional Building & Site Aesthetic Works Value (C)	NA	Rs.65,00,00,000/-			
d.	Total Add (A+B+C)	Rs.487,02,60,000/- (Land Value Only)	Rs.826,67,68,433/-			
e.	Additional Premium if any					
	Details/ Justification					
f.	Deductions charged if any					
	Details/ Justification					
g.	Total Prospective Fair Market Value#	NA	Rs.826,67,68,433/-			
h.	Rounded Off		Rs.826,68,00,000/- (After Completion of the whole project)			
i.	Realizable Value		Rs.702,67,80,000/-			
j.	Distress Value*		Rs.620,01,00,000/-			
k.	Valuation of structure for Insurance purpose	NA	NA			

(Rupees Eight Hundred Twenty Six Crores Sixty Eight Lakhs Only)

7.	Concluding comments if any	a. Valuation of the asset is done as found on as-is-where basis.b. Any kind of unpaid statutory, utilities, lease, interest or any other				
		pecuniary dues on the asset has not been factored in the Valuation. c. Secondary/ Tertiary costs related to asset transaction like Stamp				
		Duty, Registration charges, Brokerage, Bank interest etc. pertaining to the sale/ purchase of this property are not considered while assessing the Market Value.				
		. As per the scope of the assignment, Value assessment is subject to				
		Assumptions, Remarks & Limiting Conditions mentioned in				
		Point '7' below, R.K Associates Important Notes and Valuer's				
		Remarks(Enclosure: 1)& other enclosed documents with the				
		Report which will remain part & parcel of the report. Without these enclosures/ documents report shall stand null & void.				







3.	ASSUMPTIONS REMARKS LIMITING CONDITIONS
a.	Information of the average market rates is taken based on the verbal market survey in the subject area from th local people, property agents, recent deals, demand-supply, internet postings which has been relied upon. No writte record is generally available for such market information and only the verbal information has to be relied upon.
b.	Forced, compulsion, constraint, obligatory sales transactions data doesn't forms part of the Fair Market Valuatio exercise.
C.	Sale transaction method of the asset is assumed as free market transaction while assessing Prospective Fair Market Value of the asset.
d.	This Valuation report is prepared based on the facts of the property on the date of the survey. However in future property Market may go down, property conditions may change or may go worse, Property reputation may differ Property vicinity conditions may go down or become worse, Property market may change due to impact of Gov policies or effect of World economy, Usability prospects of the property may change, etc. Hence before financing Banker/ FI should take into consideration all such future risk and should loan conservatively to keep the advance money safe in case of the downward trend of the property value.
e.	Valuation of the same asset/ property can fetch different values in different situations. For eg. Valuation of a running operational shop/ hotel/ factory will fetch better value and in case of closed shop/ hotel/ factory it will have considerable lower value. Similarly an asset sold directly by an owner in the market will fetch better value and if the same asset/ property is sold by any financer due to encumbrance on it will fetch lower value. Hence before financing Banker/ FI should take into consideration all such future risks and should loan conservatively to keep the advance money safe in case of any such situation.
f.	This report is prepared based on the copies of the documents/ information which interested organization or custome could provide to us out of the standard checklist of documents sought from them and further based on or assumptions and limiting conditions. All such information provided to us has been relied upon and we have assume that it is true and correct. Verification or cross checking of the documents provided to us from the originals has no been done at our end. If at any time in future it's found or came to our knowledge that misrepresentation of facts incomplete or distorted information has been provided to us then this report will automatically become null & void.
g.	Getting cizra map or coordination with revenue officers for site identification is not done at our end.
h.	All area measurements are on approximate basis. Verification of the area measurement of the property is done on based on sample random checking and not based on full scale measurement. Area of the large land parcels of more than 2500 sq.mtr or of uneven shape, is taken as per property documents which has been relied upon.
İ.	Legal aspects for eg. ownership rights, lien, charge, mortgage, etc. are not considered in this report. It is assume and taken into account that the concerned Bank/ Financial Institution has first got the legal verification cleared to the competent Advocate before requesting for the Valuation report. In case Valuation is obtained before taking leg scrutiny or opinion then it is expected from the Bank to inform back the Valuer timely about such change of right on the property as soon as it comes into the notice of the Bank/ Financer which may affect their charge on the mortgage asset so that accordingly Valuation modification can be done only for that portion for which the Bank has complete charge/ rights.
j.	Investigation of title of the property and its legal right is beyond the scope of this report. If this property is offered a collateral security, then concerned financial institution is requested to verify & satisfy themselves on the ownersh & legality of the property shown in this valuation report with respect to the latest legal opinion.
k.	Valuation is done for the property identified to us by the owner/ owner representative. Responsibility of identifying the correct property to the Valuer/ its authorized surveyor is solely of the client/ owner for which Valuation has to be carried out. At our end we can just cross verify the identification of the property with reference to the document produced for perusal. Method by which identification of the property is carried out is also mentioned in the report clearly. It is requested from the Bank to cross check from their own records/ information if this is the same property of which Valuation has to be carried out to ensure that owner has not misled the Valuer company or misrepresented the property due to any vested interest.
L	In India more than 70% of the geographical area is lying under rural/ remote/ non municipal/ unplanned area when the subject property is surrounded by vacant lands having no physical demarcation or having any display of proper survey or municipal number / name plate on the property clearly. Even in old locations of towns, small cities districts where property number is either not assigned ornot displayed on the properties clearly and also due to the presence of multiple/ parallel departments due to which ownership/ rights/ illegal possession/ encroachment issue are rampant across India anddue to these limitations at many occasions it becomes tough to identify the proper with 100% surety from the available documents, information & site whereabouts and thus chances of error misrepresentation by the borrower and margin of chances of error always persists in such cases. To avoid any such chances of error it is advised to the Bank to engage municipal/ revenue department officials to get the confirmation of the property to ensure that the property shown to Valuer/ Banker is the same as for which documents are provided.
m.	If this Valuation Report is prepared for the Flat/ dwelling unit situated in a Group Housing Society or Integrate
	Township then it is assumed that the Banker or the concerned organization has satisfied themselves with the

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 25 of 35





approval of the Group Housing Society/ particular floor & building before allotting the Valuation case to the Valuer company.
Due to fragmented & frequent change in building/ urban planning laws/ guidelines from time to time, different laws/ guidelines between regions/ states and no strict enforceability of Building Bye-Laws in India specially in non-metro and scale b & c cities & Industrial areas, property owners many times extend or make changes in the covered area/ layout from the approved/ applicable limits. There are also situations where properties are decades old when there was no formal Building Bye-Laws applicable when the construction must have been done. Due to such discrete/ unplanned development in many regions sometimes it becomes tough to determine the exact lawful situation on ground for the Valuer. In case nothing specific is noted on the covered built-up area considered in the Valuation Report, the covered area present on the site as per site survey will be considered in the Valuation.
In case of Valuation of Plant & Machinery or equipment, condition of machines is evaluated by visual observation only. No technical/ mechanical testing of any kind has been carried out at our end to ascertain the condition and efficiency of the machines. Valuation of Plant & Machinery is done on the basis of physical existence of the assets rather than their technical expediency.
Secondary/ Tertiary costs related to asset transaction like Stamp Duty, Registration charges, Brokerage, Bank interest, etc. pertaining to the sale/ purchase of this property are not considered while assessing the Market Value.
Any kind of unpaid statutory, utilities, lease, interest or any other pecuniary dues on the asset has not been factored in the Valuation.
Valuation is a subjective field and opinion may differ from consultant to consultant. To check the right opinion, it is important to evaluate the methodology adopted and various data point/ information/ factors/ assumption considered by the consultant which became the basis for the Valuation report before reaching to any conclusion.
At the outset, it is to be noted that Value analysis of any asset cannot be regarded as an exact science and the conclusions arrived at in many cases will, of necessity, be subjective and dependent on the exercise of individual judgment. Given the same set of facts and using the same assumptions, expert opinions may differ due to the number of separate judgment decisions, which have to be made. Therefore, there can be no standard formulae to establish an indisputable exchange ratio. In the event of a transaction, the actual transaction value achieved may be higher or lower than our indicative analysis of value depending upon the circumstances of the transaction. The knowledge, negotiability and motivations of the buyers and sellers and the applicability of a discount or premium for control will also affect actual price achieved. Accordingly, our indicative analysis of value will not necessarily be the price at which any agreement proceeds. The final transaction price is something on which the parties themselves have to agree. However our Valuation analysis can definitely help the stakeholders to make them informed and wise decision about the Value of the asset and can help in facilitating the arm's length transaction.

R.K ASSOCIATES IMPORTANT NOTES:

- 1. <u>DEFECT LIABILITY PERIOD</u> In case of any query/ issue or escalation you may please contact Incident Manager by writing at valuers@rkassociates.org. We ensure 100% accuracy in the Calculations done, Rates adopted and various other data points & information mentioned in the report but still can't rule out typing, human errors or any other mistakes. In case you find any mistake, variation, discrepancy or inaccuracy in any data point of the report, please help us by bringing all such points into our notice in writing at <u>valuers@rkassociates.org</u>within 30 days of the report delivery, to get these rectified timely, failing which R.K Associates won't be held responsible for any inaccuracy in any manner. Also if we will not hear back anything from you within 30 days, we will assume that report is correct in all respect and no further claim of any sort will be entertained thereafter. We would welcome and appreciate your feedback & suggestions in order to improve our services.
- COPYRIGHT FORMAT This report is prepared on the copyright format of R.K Associates to serve our clients in the best
 possible way. Legally no one can copy or distribute this format without prior approval from R.K Associates. It is meant only for
 the organization as mentioned on the cover page of this report. Distribution or use of this format other than R.K Associates will
 be seen as unlawful act and necessary legal action can be taken against the defaulters.

IF REPORT IS USED FOR BANK/ FIS

NOTE: As per IBA Guidelines in case the valuation report submitted by the valuer is not in order, the banks / FIs shall bring the same to the notice of the valuer within 15 days of submission for rectification and resubmission. In case no such communication is received, it shall be presumed that the valuation report has been accepted.

At our end we have not verified the authenticity of any documents provided to us. Bank is advised to verify the genuineness of the property documents before taking any credit decision.

EUREKA PARK, SECTOR-105, NOIDA



ENCLOSURE: 1- VALUER'S REMARKS

1.	Fair Market Value#suggested by the competent Valuer is that prospective estimated amount of the subject asset/property in his expert & prudent opinion without any prejudice after he has carefully & exhaustively evaluated all the
	facts & information related the subject asset at which the subject asset/ property should be exchanged between a
	willing buyer and willing seller at an arm's length transaction after proper marketing, wherein the parties, each acted
2.	knowledgeably, prudently and without any compulsion on the date of the Valuation. Realizable Value^ is the minimum prospective value of the property which it may be able to realize at the time of
2.	actual property transaction factoring in potential prospects of deep negotiations carried out between the buyer & seller for ultimately finalizing the transaction. Realizable value may be 10-20% less of the Fair Market Value
•	depending on the various salability prospects of the subject property.
3.	Forced/ Distress Sale Value* is the value when the property has to be sold due to any compulsion or constraint like financial encumbrances, dispute, as a part of a recovery process, any defect in the property, having unclear title or any such sort of condition or situation. In this type of sale minimum disposable value is assessed which varies from 20-35% less from the Fair Market Value based on the nature, size &salability prospects of the property. In this type of sale negotiation power of the buyer is always more than the seller and eagerness of selling the property is more than buying it. Therefore the Forced/ Distress Sale Value always fetches less value.
4.	Best rates are rationally adopted based on the facts of the case came to our knowledge during the course of the assignment considering many factors like nature of the property, size, location, approach, market situation and
	trends.
5.	Construction rates are adopted based on present replacement cost of construction and calculating applicable depreciation & deterioration factor as per its existing condition, specifications based on the visual observation of the structure. No structural, physical tests have been carried out in respect of it.
6.	This Valuation report is prepared based on the facts of the property on the date of the survey. However in future property Market may go down, property conditions may change or may go worse, Property reputation may differ, Property vicinity conditions may go down or become worse, Property market may change due to impact of Govt. policies or effect of World economy, Usability prospects of the property may change, etc. Hence before financing, Banker/ FI should take into consideration all such future risk and should loan conservatively to keep the advanced money safe in case of the downward trend of the property value.
7.	Valuation of the same asset/ property can fetch different values in different situations. For eg. Valuation of a running/ operational shop/ hotel/ factory will fetch better value and in case of closed shop/ hotel/ factory it will have considerable lower value. Similarly an asset sold directly by an owner in the market will fetch better value and if the same asset/ property is sold by any financer due to encumbrance on it will fetch lower value. Hence before financing, Banker/ FI should take into consideration all such future risk and should loan conservatively to keep the advanced money safe in case of any such situation.
8.	No employee or member of R.K Associates has any direct/ indirect interest in the property.
9.	Sale transaction method of the asset is assumed as free market transaction while assessing Fair Prospective Market Value of the asset.
10.	Area measurements considered in the Valuation Report pertaining to Land & Building is adopted from relevant approved documents or actual site measurement whichever is less. All area measurements are on approximate basis only.
11.	This report is having limited scope as per its fields to provide only the general basic idea of the value of the property prevailing in the market based on the documents/ data/ information provided by the client. The suggested value should be considered only if transaction is happened as free market transaction.
12.	The condition assessment and the estimation of residual economic life of the structure is based on the visual observations and appearance found during the site survey. We have not carried out any structural design or stability study; nor carried out any physical tests to assess structural integrity & strength.
13.	This report is prepared based on the copies of the documents/ information which interested organization or customer could provide to us out of the standard checklist of documents sought from them and further based on our assumptions and limiting conditions. All such information provided to us has been relied upon and we have assumed that it is true and correct. Verification or cross checking of the documents provided to us from the originalshas not been done at our end. If at any time in future it's found or came to our knowledge that misrepresentation of facts or incomplete or distorted information has been provided to us then this report will automatically become null & void.
14.	Investigation of title of the property and its legal right is beyond the scope of this report. If this property is offered as collateral security, then concerned financial institution is requested to verify & satisfy themselves on the ownership & legality of the property shown in this valuation report with respect to the latest legal opinion.

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 27 01350






15.	Value varies with the Purpose/ Date/ Condition of the market. This report should not to be referred if any of these points are different from the one mentioned aforesaid in the Report. The Value indicated in the Valuation Report holds good only upto the period of 3 months from the date of Valuation.
16.	Analysis and conclusions adopted in the report are limited to the reported assumptions, conditions and information came to our knowledge during the course of the work.
17.	This report is prepared on the RKA V-L6 (Medium) Valuation format as per the client requirement, charges paid and the time allotted. This report is having limited scope as per its fields to provide only the general estimated basic idea of the value of the property prevailing in the market based on the information provided by the client. The Valuation assessed in this Valuation Report should hold good only if transaction is happened as per free market transaction. No detailed analysis or verification of the information is carried upon pertaining to the value of the subject property. No claim for any extra information will be entertained whatsoever be the reason. For any extra work over and above the fields mentioned in the report will have an extra cost which has to be borne by the customer.
18.	This is just an opinion report and doesn't hold any binding on anyone. It is requested from the concerned Client/ Bank/ Financial Institution which is using this report for mortgaging the property that they should consider all the different associated relevant & related factors also before taking any business decision based on the content of this report.
19.	All Pages of the report including annexures are signed and stamped from our office. In case any paper in the report is without stamp & signature then this should not be considered a valid paper issued from this office.
20.	Defect Liability Period is <u>30 DAYS</u> . We request the concerned authorized reader of this report to check the contents, data and calculations in the report within this period and intimate us in writing if any corrections are required or in case of any other concern with the contents or opinion mentioned in the report. Corrections only related to typographical, calculation, spelling mistakes will be entertained within the defect liability period. No request for any illegitimate value revision, date change or any other change will be entertained other than the one mentioned above.
21.	R.K Associates encourages its customers to give feedback or inform concerns over its services through proper channel at valuers@rkassociates.org in writing within 30 days of report delivery. After this period no concern/complaint/ proceedings in connection with the Valuation Services can be entertained due to possible change in situation and condition of the property.
22.	Our Data retention policy is of <u>ONE YEAR</u> . After this period we remove all the concerned records related to the assignment from our repository. No clarification or query can be answered after this period due to unavailability of the data.
23.	This Valuation report is governed by our (1) Internal Policies, Processes & Standard Operating Procedures, (2) R.K Associates Quality Policy, (3) Valuation & Survey Best Practices Guidelines formulated by management of R.K Associates, (4) Information input given to us by the customer and (4) Information/ Data/ Facts given to us by our field/ office technical team. Management of R.K Associates never gives acceptance to any unethical or unprofessional practice which may affect fair, correct & impartial assessment and which is against any prevailing law. In case of any indication of any negligence, default, incorrect, misleading, misrepresentation or distortion of facts in the report then it is the responsibility of the user of this report to immediately or atleast within the defect liability period bring all such act into notice of R.K Associates management so that corrective measures can be taken instantly.
24.	R.K Associates never releases any report doing alterations or modifications from pen. In case any information/ figure of this report is found altered with pen then this report will automatically become null & void.
25.	If this report is prepared for the matter under litigation in any Indian court, no official or employee of R.K Associates will be under any obligation to give in person appearance in the court as a testimony. For any explanation or clarification, only written reply can be submitted on payment of charges by the plaintiff or respondent which will be 10% of the original fees charged where minimum charges will be Rs.2500/






ENCLOSURE: 2- REFERENCE FROM PUBLIC DOMAIN













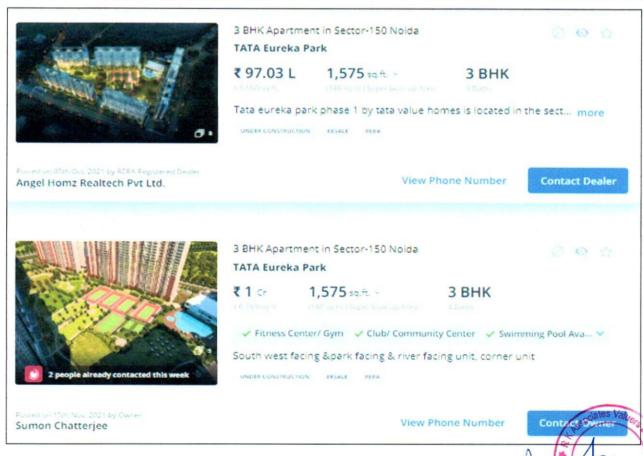

EUREKA PARK, SECTOR-105, NOIDA



ENCLOSURE: 3- GOOGLE MAP LOCATION

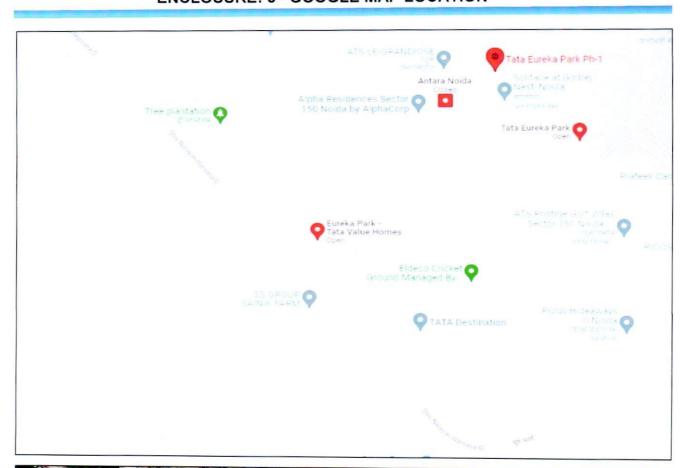



EUREKA PARK, SECTOR-105, NOIDA



ENCLOSURE: 4- CIRCLE RATES

क्षेफटवेगर में अवटित फिया गया पी-कोड	सैक्टर का कमांक	का निषंपक, कार्यालयों के	निषंद्रक, कार्यालयों के प्रयोजन, 12 मीटर क्षेत्रधिकार प्रथम, एक घौडी शहक पर द्वितीय व ट्रीय के (वेस्किक वेस्यू)	र 10000 वर्ग मीटर प्रयोजन 10060	যুদ ভাতবিশ	अधिकाम द्वारा परिचानक प	आधिकरण क्षता प्रस्थानक प्रयोजन हेतु आयदेश गूधनक की दर्र संस्थान्या बेणी से प्रयोजन से अभार वर			
					र्चा गीटर रो अधिक के	भूखण्ड हेतु निर्धास्ति दर	नमका चेक्टारें से क्रनार्चन आसएनकाकी/ सकरवेदन/ समिता फिल्म आढियों वीदियों स्ट्रीवेदी/आईएडीएपार्क/ आईएडीएईएस्स्ट/स्वाटेक पार्च हेतु मृजयह	कार्यलग् उपयोग का पूजार	सरकारी/देतीकोन केंद्रर/पोस्ट आफिस/दिद्युत एव स्टेशन, नोएटा द्वारा आबदित कृति धूने पर कार्य दाजब	अर्द्धरारकारी/किसपे न्तारी/चुपरबाजार/ दुन्ध/शब्दी एवं फल नितरन केन्द्र
0145	137	प्रथम	52500	159000	-	84500	-	78500	-	-
0146	138	द्वितीय	40000	121000	12500	-	22000	60000	10000	20000
0147	139	तृतीय	40000	121000	-			60000	-	-
0148	140	प्रथम	40000	121000	12500	75000	22000	78500	10000	20000
0149	140A	प्रथम	40000	121000	12500	75000	22000	78500	10000	20000
0150	141	द्वितीय	40000	121000	-	58000	-	60000	-	-
0151	142	तुतीय	52500	159000	-	75000	28000	78500	-	-
0152	143	प्रथम	52500	159000	-	84500	28000	78500	-	-
0153	143B	प्रथम	52500	159000	-	75000		78500	-	-
0154	144	द्वितीय	52500	159000	7.=	84500	28000	78500	-	-
0155	145	तृतीय	40000	121000	-	58000	-	60000	-	
0156	146	प्रथम	40000	121000	-	58000		60000	-	-
0157	147	द्वितीय	40000	121000	-	58000	-	60000	-	-
0158	148	वृतीय	40000	159000	-	58000	-	60000	-	-
0159	149	प्रथम	40000	121000		58000	-	60000	-	-
0160	150	द्वितीय	40000	121000	-	58000	-	60000	-	-
0161	151	वृतीय	52500	159000		75000	-	78500	-	
0162	152	प्रथम	52500	159000	-	75000	28000	78500	-	
0163	153	द्वितीय	52500	121000	-	75000	28000	78500	-	-
0164	154	तुतीय	52500	121000	-	75000	28000	78500	-	-

सहायक महानिरीक्षक निबंधन (प्रथम) गीतमबुद्धनगर।

अपर जिलाधिकारी(विँत्त एंव राजस्व) गौतमबुद्धनगर। जिलाधिकारी गौतमबुद्धनगर।

मल्टीस्टोरीज काम्पलेक्स का प्रचलित नाम	सैक्टर वन कमांक/ भोडल्ला का नाम जड़ाँ काम्प्लेक्स अवस्थित है।	मीहत्त्वे का प्रारूप-1 के अधीन आवंटित वी-कोड	सुपर एरिया के निर्माण की दर (प्रति वर्गमीटर रु० में0)	कार पार्किंग	
				कवर्ड पार्किंग	औपन पार्किंग
1	2	3	4	5	
तदैव	143	0152	40000	3 लाख	1.5 লাভ
तदैव	143B	0153	40000	3 लाख	1.5 लाख
तदैव	144	0154	40000	3 লাভ্ৰ	1.6 লাভ
तदैव	145	0155		•	
तदैव	146	0156		-	•
तदैव	147	0157			•
तदैव	148	0158	•	•	-
तदैव	149	0159	-		
तदैव	150	0160	40000	3 লাভ্ৰ	1.5 লাভ
तदैव	151	0161	40000	3 লাভ্ৰ	1,5 লাভ্র
तदैव	152	0162		-	-
तदैव	153	0163		•	-
तदैव	154	0164	-	-	
तदैव	155	0165	•		-

सहायक महानिरीक्षक निबंधन (प्रथम) गौतमबुद्धनगर। अपर जिलाधिकारी(वित्तं एंव राजस्व) गौतमबुद्धनगर। ्री N ू जिलाधिकारी गौतमबुद्धनगर।

FILE NO.: VIS(2021-22)-PL-674-585-754

Page 32 of 35

EUREKA PARK, SECTOR-105, NOIDA



ENCLOSURE: 5- PHOTOGRAPHS





EUREKA PARK, SECTOR-105, NOIDA



Page 34 01 35





EUREKA PARK, SECTOR-105, NOIDA





